

Transportation Report 3.2023

Communication

- Feb Social Media Reach: **15.6k** (11k in Jan)
- Feb Duval Loop signage QR scans: **2.7k** (2.5k in Jan)
- Ebike Workshop 3/2




Safety & Vision Zero

- Free rechargeable lights and bells are available to those in need and can be picked up from City Hall, the Police Station, and the Library.
- Crash data summarized below and available at <https://s4.geoplan.ufl.edu/> (see limitations)

Transit

- Transit ridership, roughly Dec 2022 through February 2023:

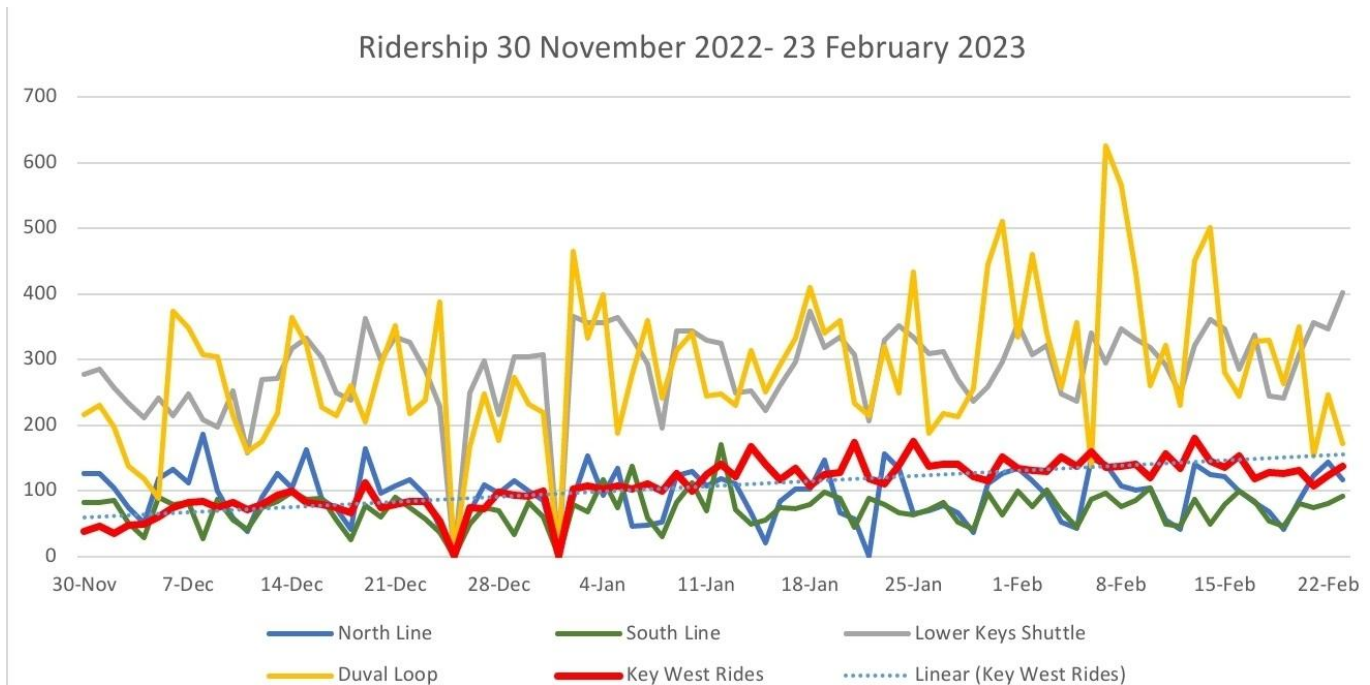

- Past 60 days ridership: Key West Rides-9285; North Line-8096; South Line-6184; Lower Keys Shuttle-24,602; Duval Loop-24,351

Bike Parking

Public map / request more: <http://bit.ly/kwracks>

- Bike rack order shipping expected week of 3/06/2023

Wayfinding

- Working with Community Services to install bicycle route wayfinding phase I

Infrastructure Type Project Updates

Updates for state projects found here: <https://www.fdotmiamidade.com/current-projects/monroe-county.html>

Updates for city projects can be found on City website GIS map <http://bit.ly/kwstreets>

- **1st Street and Bertha St** - Expected completion ~~February~~ March 2023
- **Southard St** construction completed, Status of bicycle facility in flux pending amendment to parking contract with Monroe County
- **Flagler Pedestrian Upgrades** awaiting part order - expecting completion after First & Bertha project
- **Whitehead St** target completion: Summer 2023
- **S Roosevelt Blvd** target completion date Spring 2025
- **Keys COAST CV** project - target completion Summer 2023, configuration to state intersection traffic controllers being installed
- **Staples Ave Pedestrian Bridge** is finishing the design stage
 - Updates online: <http://bit.ly/staplesbridge>
 - FDOT to install and maintain non-motorized counter at replacement bridge
- **Caroline St** bicycle infrastructure finalizing design and expected in-house routing
- **United St** construction bids received, selecting bidder
- **South St** bicycle infrastructure is in vendor design, preliminary plans expected March 2023
- **Wickers** is in design: seeking additional design services 3/07
- **North Roosevelt Blvd at Palm Ave** ([434684-4-52-01](#)) is expected to begin construction phase in 2023
- **North Roosevelt Blvd** (FM# [446011-1](#)): Finishing scoping phase, Safety audit to be presented in March

Collision Data Presented by Signal Four Analytics

s4.geoplan.ufl.edu




FLORIDA TRAFFIC SAFETY DASHBOARD



Data available from January 1, 2012 to March 1, 2023. Last update completed March 2, 2023 at 1:01 AM.

Disclaimer Data Dictionary

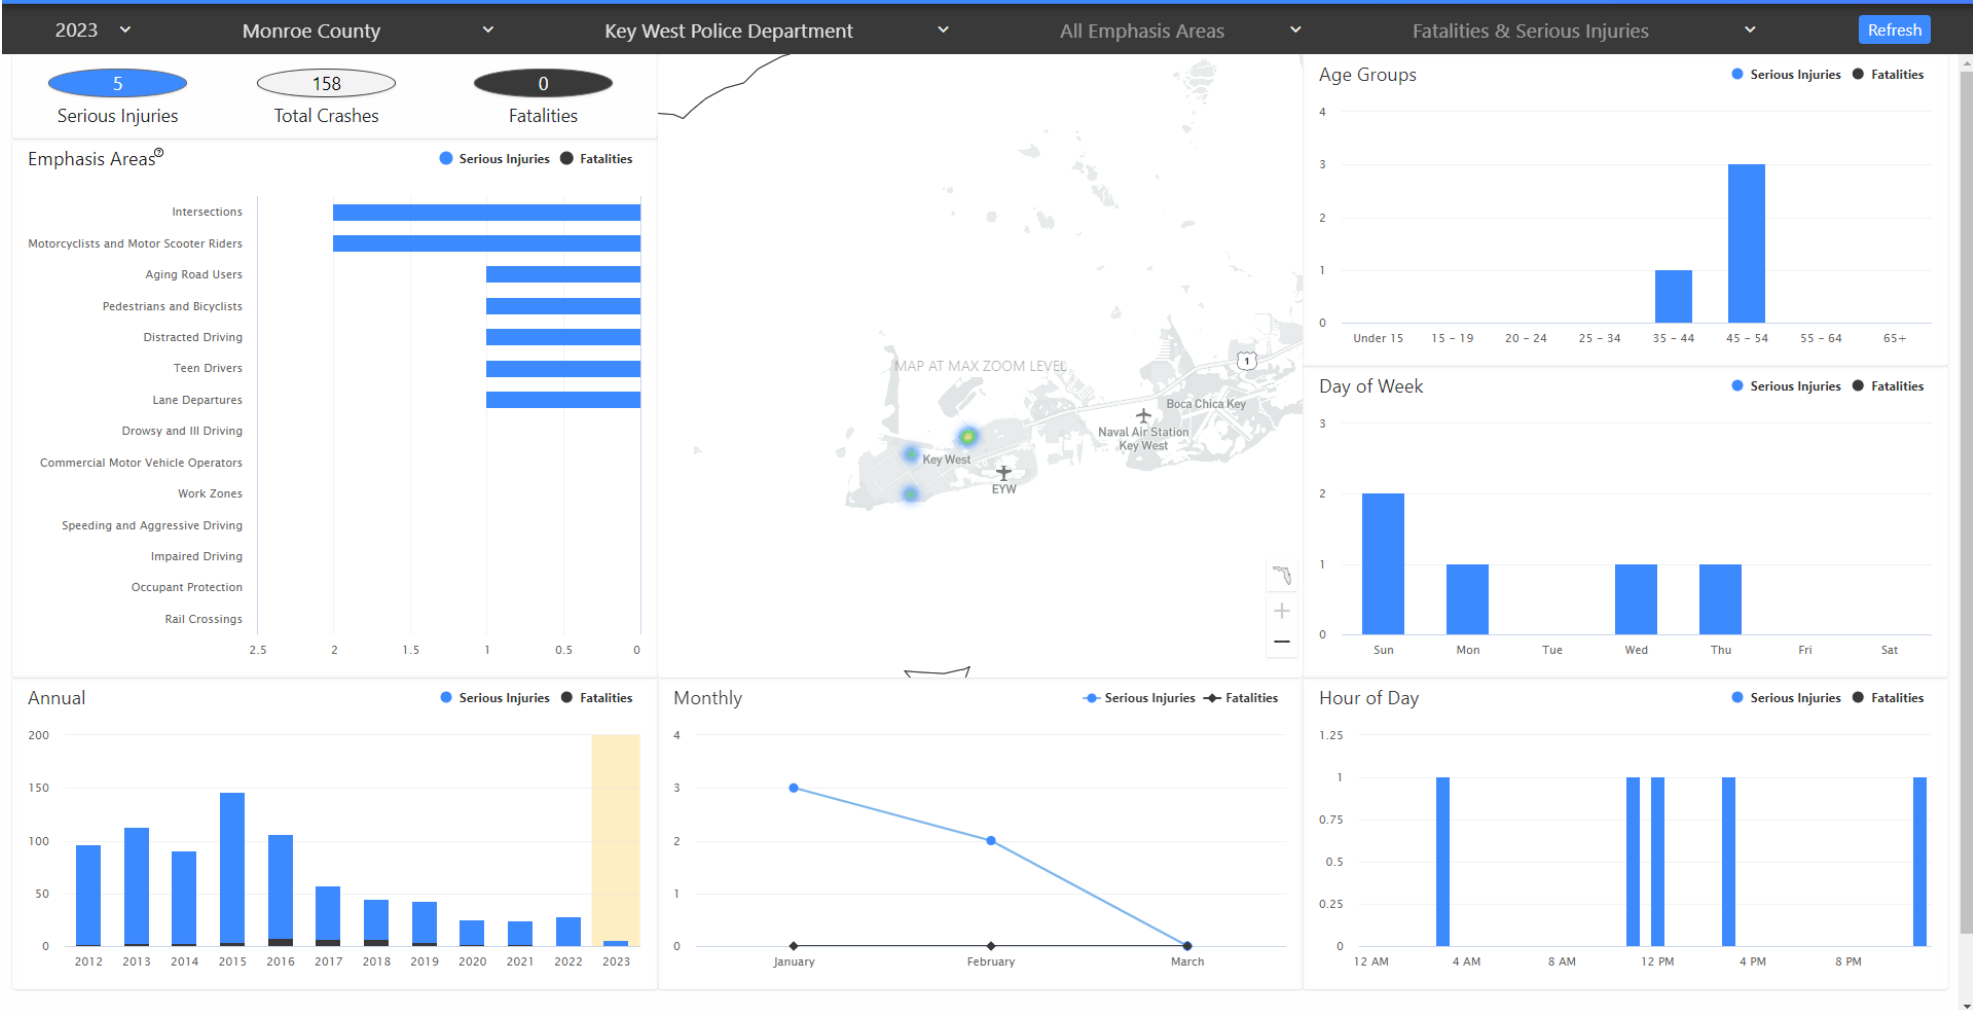

This dashboard and analytics system receives data from Florida's statutory custodian of records, the Florida Department of Highway Safety and Motor Vehicles (FLHSMV). Every effort is made to ensure that all data, information, and results posted on this website are accurate and complete. However, all data is considered preliminary until the year is reconciled and closed out by the FLHSMV, and thus certain adjustments may be made to verify the data where clerical errors are noted. For further inquiries on Florida traffic crash and citation reports along with additional statistics please visit: <https://www.flhsmv.gov/resources/crash-citation-reports/>
