

Transportation Report 5.2023

Communication


- April Social Media Reach: **11k** (7.4k in March)
- April Duval Loop signage QR scans: **2.5k** (2.7k in March)
- May is **#NationalBikeMonth** !



Safety & Vision Zero

- Outreach at Earth Day plogging event. Free rechargeable lights are still available to those in need and can be picked up from City Hall, the Police Station, and the Library.
- Crash data summarized below and available at <https://s4.geoplan.ufl.edu/> (see limitations)

Transit

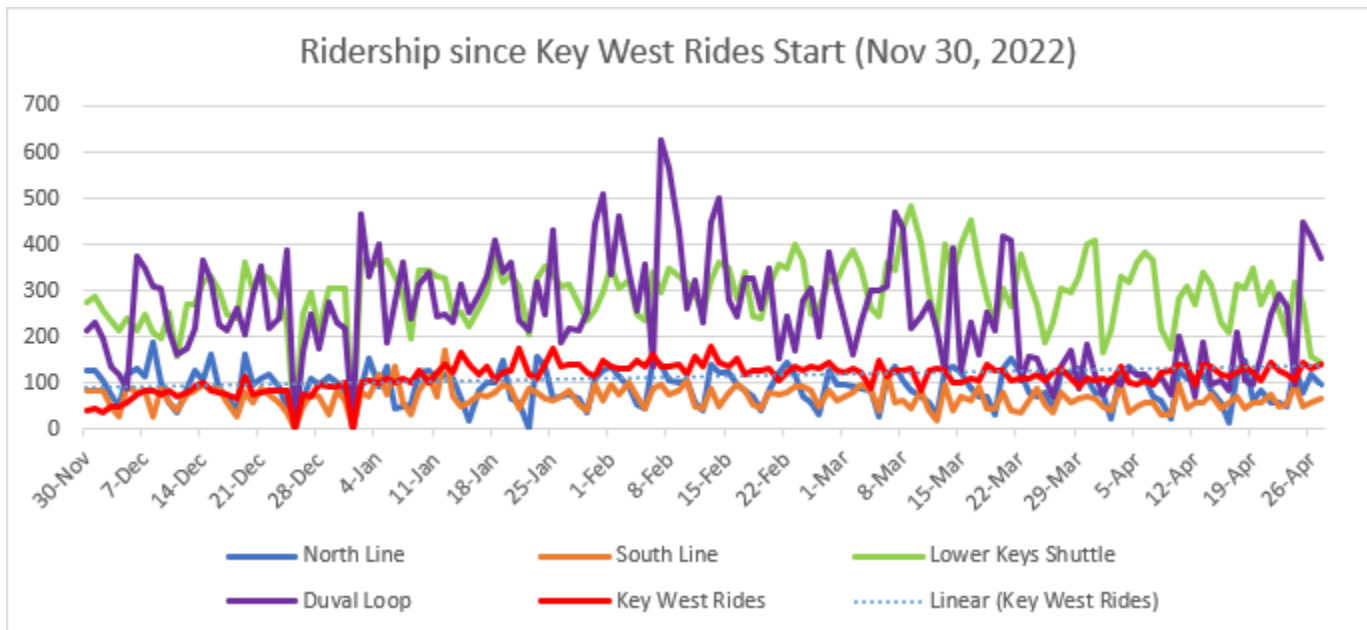

- North and South Lines scheduled to be converted to a Workforce Express route beginning May 15th.

Bike Parking

Public map / request more: <http://bit.ly/kwracks>

- Post-and-hitch bollard-style bicycle rack order has been received and is being installed by Community Services.
- Orders being placed for Emerson style
- Recent installs along Fleming St and Front St

Infrastructure Type Project Updates


Updates for state projects found here: <https://www.fdotmiamidade.com/current-projects/monroe-county.html>

Updates for city projects can be found on City website GIS map <http://bit.ly/kwstreets>

- **Pavement Striping Contract** Small bike lane improvements at Grinnell St and Caroline St as well at Eaton St at White St to fill in the Historic Seaport network
- **1st Street and Bertha St** - Final walkthrough completed
- **Southard St** construction completed, Status of bicycle facility in flux pending amendment to parking contract with Monroe County
- **Flagler Pedestrian Upgrades** largely completed, but awaiting part order
- **United St** construction underway, expected completion Nov 2023
- **Final Mile** Construction underway beginning on Stock Is, expected completion Nov 2023
- **Whitehead St** target completion: Summer 2023
- **S Roosevelt Blvd** target completion date Spring 2025
- **Keys COAST** target completion Summer 2023
- **Staples Ave Pedestrian Bridge** is finishing the design stage, targeting release June 2023
 - Updates online: <http://bit.ly/staplesbridge>
 - FDOT to install and maintain non-motorized counter at replacement bridge
- **Caroline St** bicycle infrastructure finalizing design and expected in-house routing
- **South St** bicycle infrastructure is in vendor design, preliminary plans were expected March 2023
- **Wickers** is in design: additional design services approved 3/07
- **North Roosevelt Blvd at Palm Ave (434684-4-52-01)** is expected to begin construction phase in 2023
- **North Roosevelt Blvd (FM# 446011-1)**: Finishing scoping phase, Safety audit was to be presented in March
- **Salt Ponds Trails** Related ILA with Monroe County passed March 2023 (T.6.#11868)

Collision Data Presented by Signal Four Analytics

s4.geoplan.ufl.edu

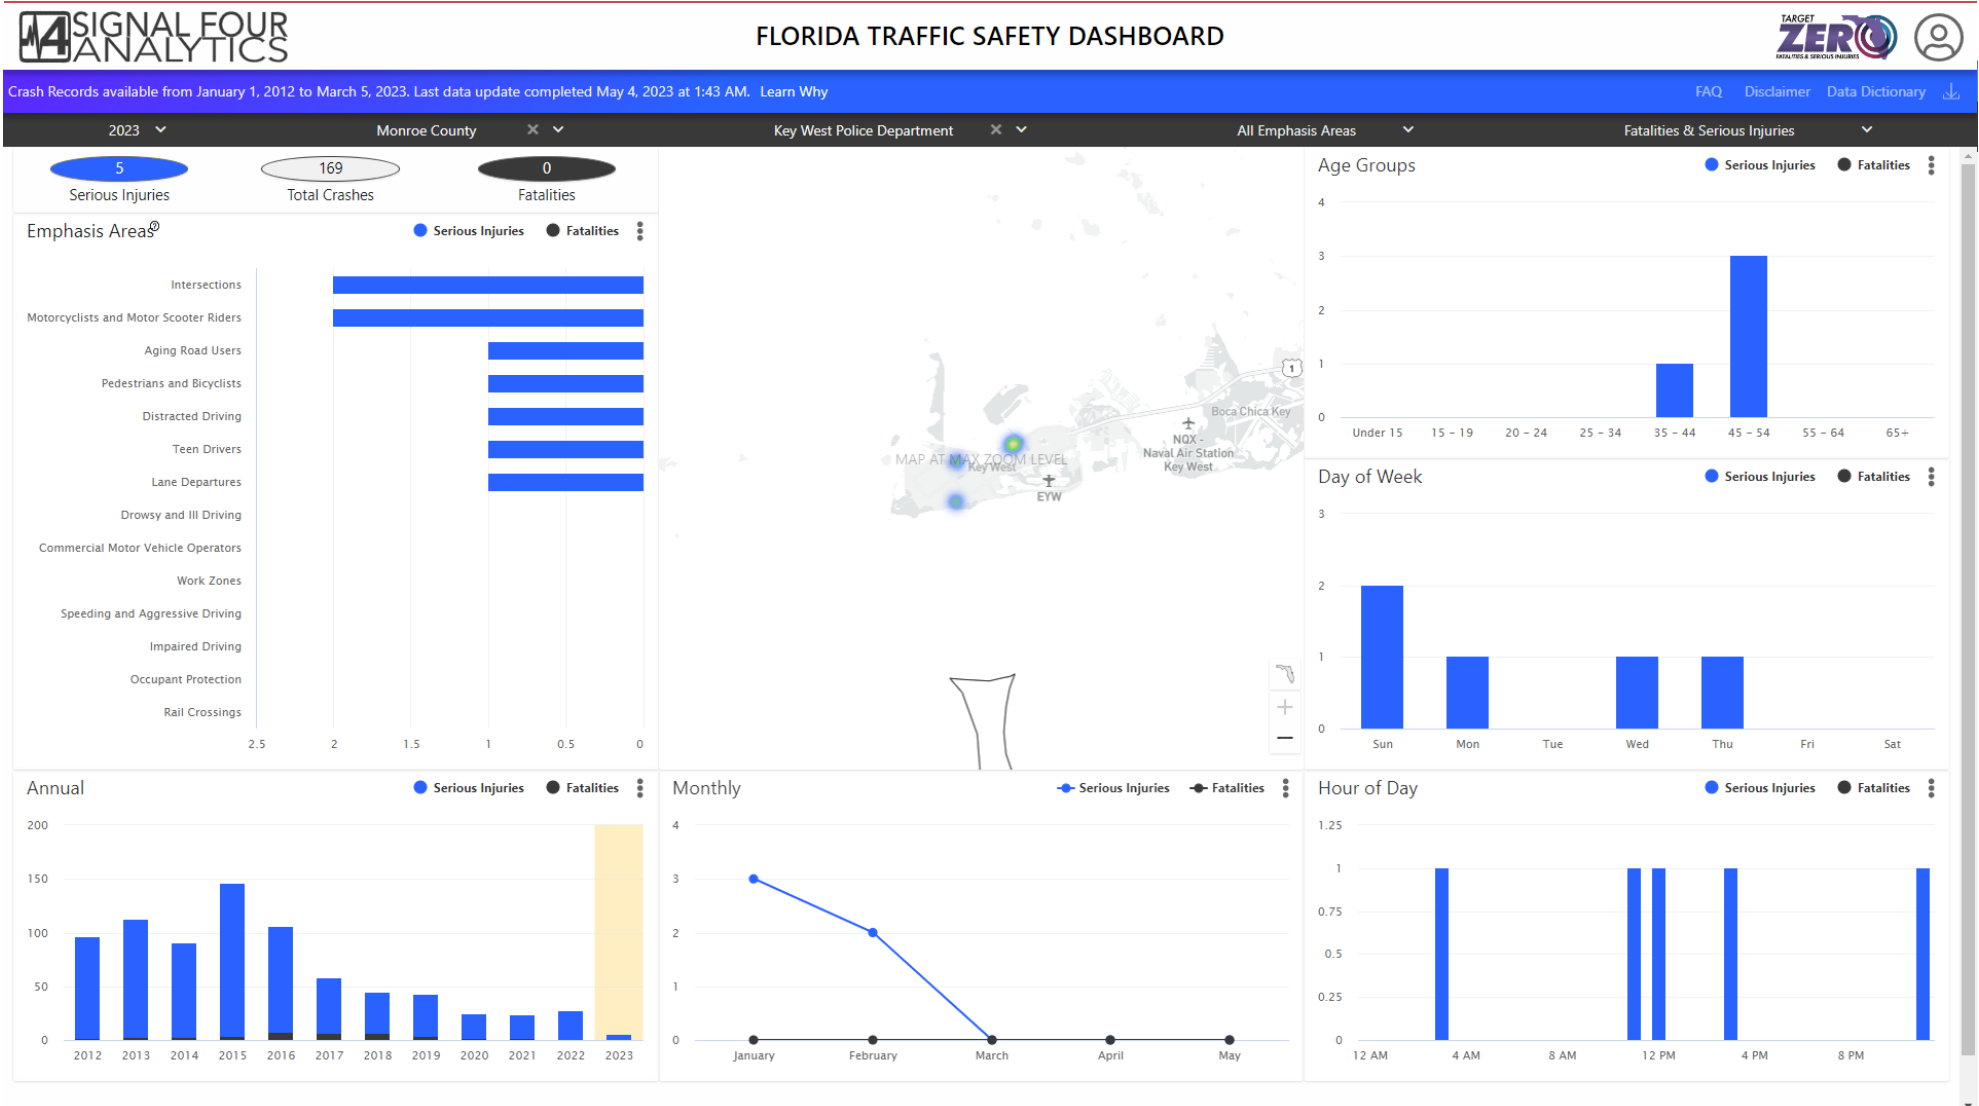

This dashboard and analytics system receives data from Florida's statutory custodian of records, the Florida Department of Highway Safety and Motor Vehicles (FLHSMV). Every effort is made to ensure that all data, information, and results posted on this website are accurate and complete. However, all data is considered preliminary until the year is reconciled and closed out by the FLHSMV, and thus certain adjustments may be made to verify the data where clerical errors are noted. For further inquiries on Florida traffic crash and citation reports along with additional statistics please visit: <https://www.flhsmv.gov/resources/crash-citation-reports/>
