

Transportation Report 2.2023

Communication

- Jan Social Media Reach:
11.0k (11.6k in Dec)
- Jan Duval Loop signage QR scans:
2.5k (2.1k in Dec) (30% of ridership)
- Bicycle Action Committee:
City-branded jerseys available for local vendors to sell. Currently available at WeCycle.




Safety & Vision Zero

- Free rechargeable lights and bells are available to those in need and can be picked up from City Hall, the Police Station, and the Library. Giveaway event at Staples Pedestrian Bridge 1/07.
- In-Street Pedestrian signs are being tested at some uncontrolled crossings along Eaton St.
- Crash data summarized below and available at <https://s4.geoplan.ufl.edu/> (see limitations)
- Selected for [\\$400k BIL award](#) to develop a City-wide Comprehensive Safety Action Plan

Transit

- 60 days of transit ridership, roughly Dec 2022 through January 2023:

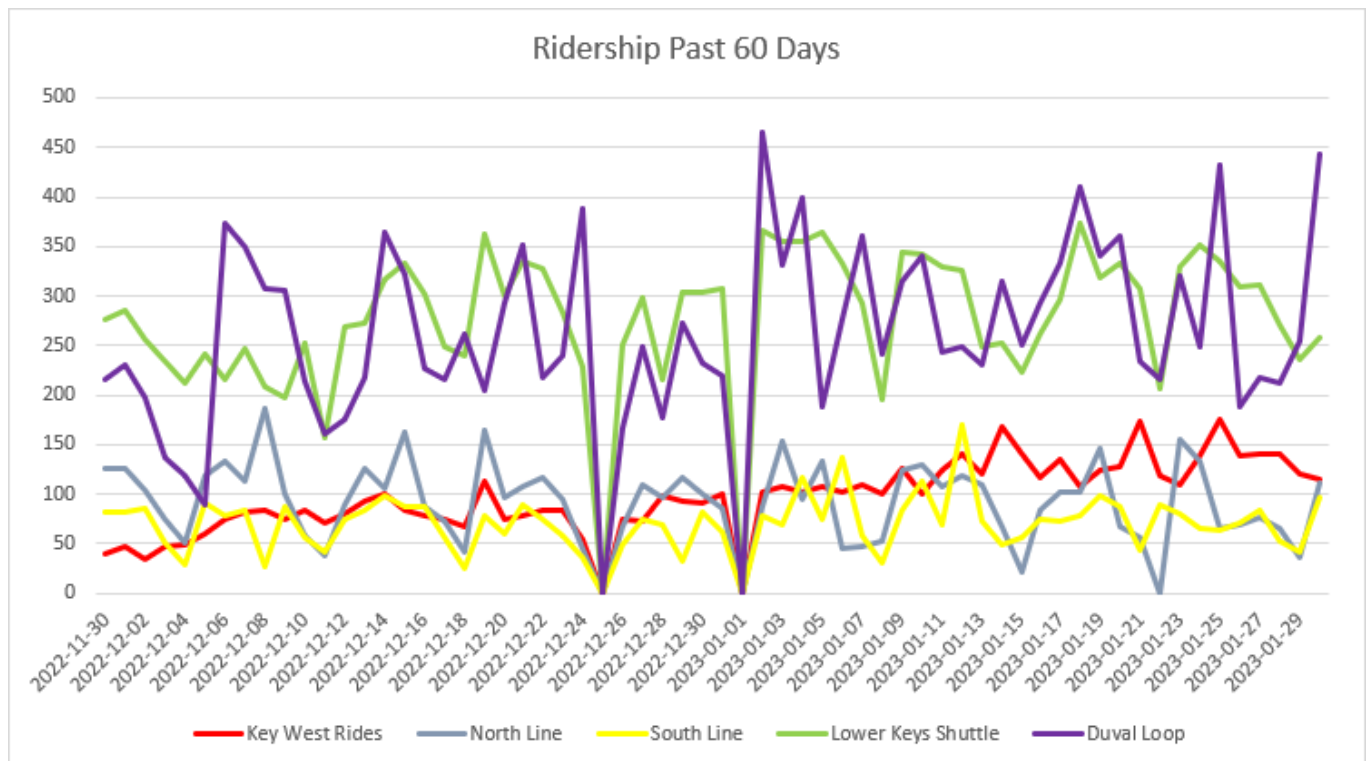

Bike Parking

Public map / request more: <http://bit.ly/kwracks>

- On-street racks placed at Packer St near Truman Ave & Fleming St at Nassau Ln.

Wayfinding

- Bicycle route wayfinding (first phase) in review

Infrastructure Type Project Updates

Updates for state projects found here: <https://www.fdotmiamidade.com/current-projects/monroe-county.html>

Updates for city projects can be found on City website GIS map <http://bit.ly/kwstreets>

- **1st Street and Bertha St** - Expected completion February 2023
- **Southard St** construction wrapping up - contract target completion February 2023
 - Status of bicycle facility in flux
- **Flagler Pedestrian Upgrades** are underway, concurrent with 1st St and Bertha St
- **Whitehead St** begins construction - contract target completion: Summer 2023
- **S Roosevelt Blvd** begins construction - contract target complete Spring 2025
- **Keys COAST** CV project - contract target completion Summer 2023
- **Staples Ave Pedestrian Bridge** is finishing the design stage
 - Updates online: <http://bit.ly/staplesbridge>
 - FDOT to install and maintain non-motorized counter at replacement bridge
- **Caroline St** bicycle infrastructure finalizing design and expected in-house routing
- **United St** bicycle infrastructure in review before release to bid construction
- **South St** bicycle infrastructure is in vendor design, preliminary plans expected March 2023
- **Wickers** is in design: seeking additional design services
- **North Roosevelt Blvd at Palm Ave (434684-4-52-01)** is expected to begin construction phase in 2023
- **North Roosevelt Blvd (FM# 446011-1)**: Finishing scoping phase

Collision Data Presented by Signal Four Analytics

s4.geoplan.ufl.edu




FLORIDA TRAFFIC SAFETY DASHBOARD



Data available from January 1, 2012 to January 31, 2023. Last update completed February 1, 2023 at 1:21 AM.

Disclaimer Data Dictionary

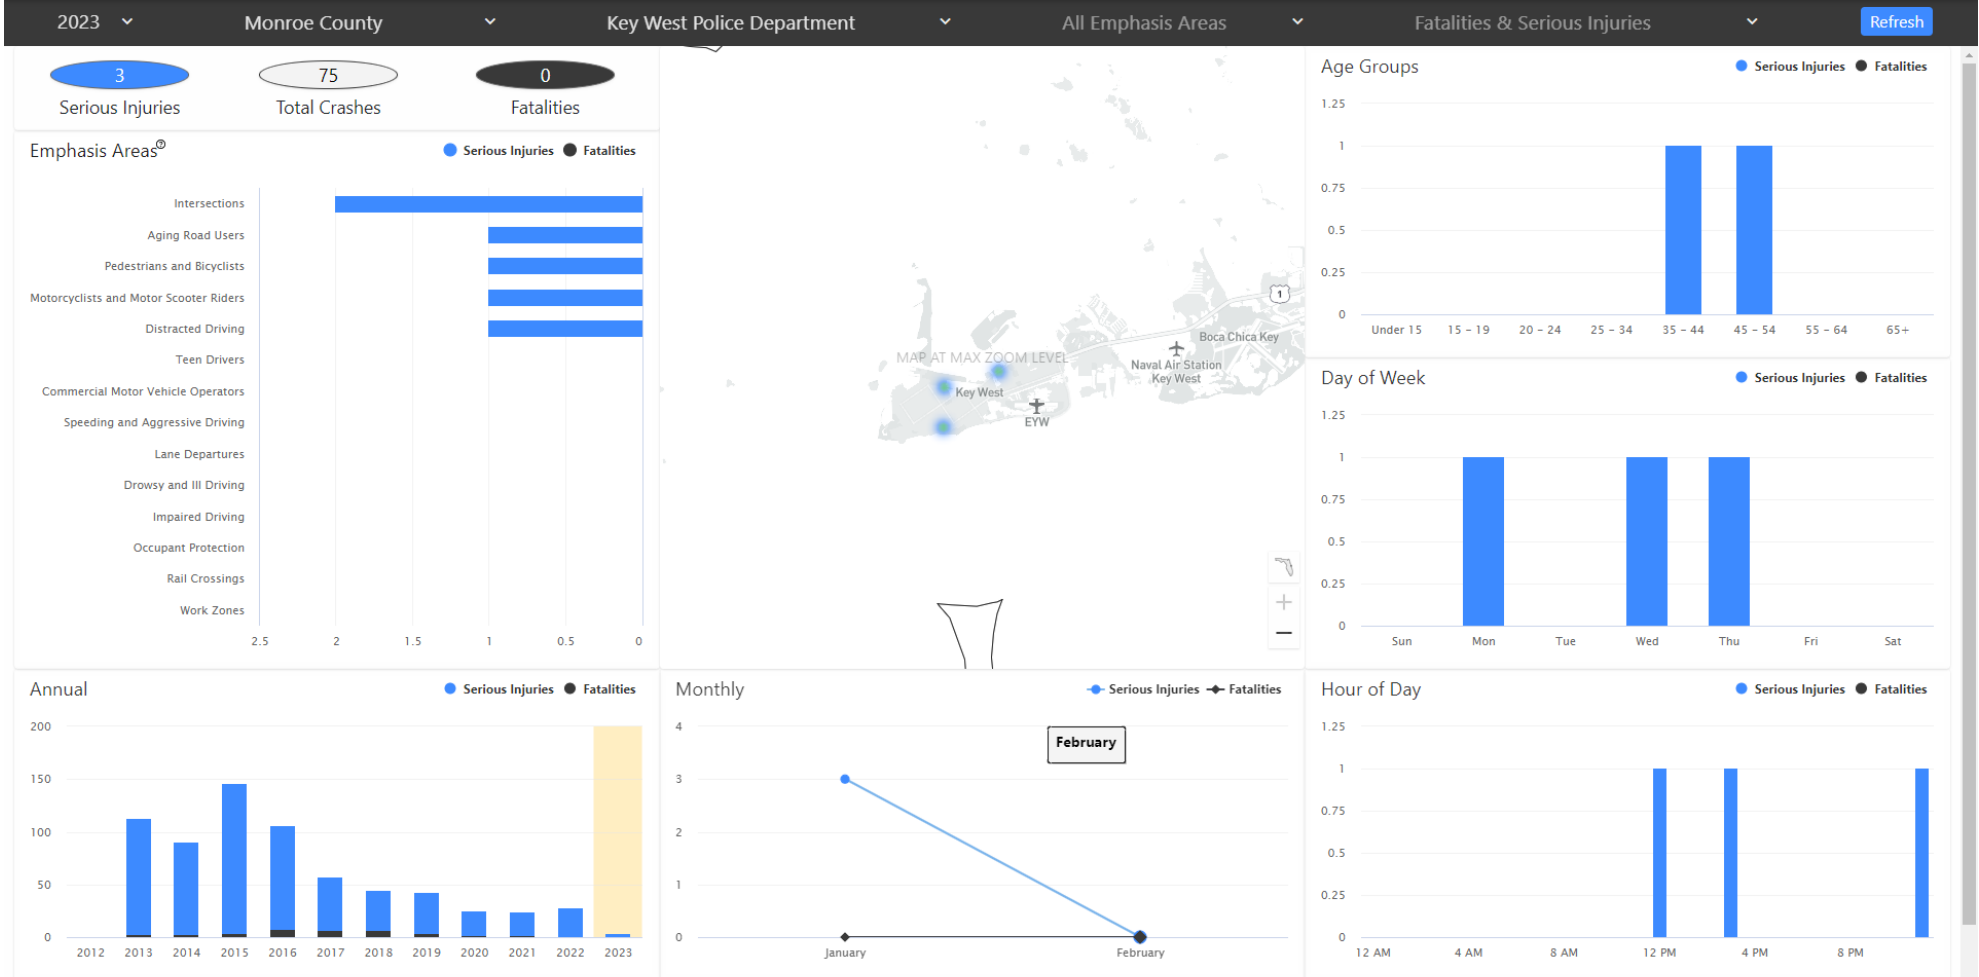

This dashboard and analytics system receives data from Florida's statutory custodian of records, the Florida Department of Highway Safety and Motor Vehicles (FLHSMV). Every effort is made to ensure that all data, information, and results posted on this website are accurate and complete. However, all data is considered preliminary until the year is reconciled and closed out by the FLHSMV, and thus certain adjustments may be made to verify the data where clerical errors are noted. For further inquiries on Florida traffic crash and citation reports along with additional statistics please visit: <https://www.flhsmv.gov/resources/crash-citation-reports/>
