

Please make POs and contracts out to:
 Porter Corp
 4240 136th Ave
 Holland, MI 49424-8442

Please mail checks to:
 same as P O mailing address

This proposal is presented by Rep Services, Inc.

Proposed To: City of Key West
 Public Works
 633 Palm Avenue
 Key West, FL 33040-4602

Ship To: TBD at a later date

Bill To: City of Key West
 Public Works
 633 Palm Avenue
 Key West, FL 33040-4602

Attn: Richard Sarver

Attn:

Attn: Richard Sarver

Project No: 21667
Proposal No: 21667.02
Proposal Date: 5/1/2025
Project Name: Key West Shelters
Proposal Name: Additional Shelters Key West
Proposal Expires: 5/21/2025

Project Contact: Richard Sarver
Project Location: 3420 Northside Dr
 Key West, FL 33040
 Project County: Monroe

For Questions Contact: Wendy Bowerman ☎ 407-853-3557 ✉ wendy@repsservices.com
Consultant: Kevin Harding ☎ 407-853-3575 ✉ kevin@repsservices.com

Opt/Rev: B/0 5/1/25 - WB

Vendor: Polygon **Proj Drawings:** Engr-permits 603386

Class	Part No	Qty	Description	Unit Price	Disc	Net Price	Ext Price
Shelters	23119R0	1 EA	Polygon Shelter Model: SQR 12 Primary Roof: PBR Secondary Roof: N/A Number of Columns 4 Eave Height (UPB): 8' Upper Roof Slope: 6/12 Electrical Cutout: 4 Electrical Access: Yes Ornamentation: N/A Powder Coat over Galvanized Exposure D Lightning Protection: N/A Anchor Bolts Included Yes 2023 Florida Building Code 8th Edition Engineering to comply with HVHZ: YES	32,036.00	-8.0%	29,473.12	29,473.12

Discount per the Sourcewell (NJPA) Purchasing Contract #012621-PPC: \$2,562.88 **Product Subtotal:** \$29,473.12
Electronic of Signed & Sealed Engineering: \$1,000.00
Freight: Prepaid Ship Method: Best Way FOB: Destination Weight: 1,693 lbs Freight Charge: \$3,200.00
Polygon Total: \$33,673.12

Vendor: Polygon **Proj Drawings:** Engr-permits 603387

Class	Part No	Qty	Description	Unit Price	Disc	Net Price	Ext Price
Shelters	23132R0	1 EA	Polygon Shelter Model: SQR 16 Primary Roof: PBR Secondary Roof: N/A Number of Columns 4 Eave Height (UPB): 8 Upper Roof Slope: 6/12 Electrical Cutout: 4 Electrical Access: yes Ornamentation: N/A Powder Coat over Galvanized Exposure D Lightning Protection: N/A Anchor Bolts Included Yes 2023 Florida Building Code 8th Edition Engineering to comply with HVHZ: Yes	40,299.00	-8.0%	37,075.08	37,075.08

Discount per the Sourcewell (NJPA) Purchasing Contract #012621-PPC: \$3,223.92 **Product Subtotal:** \$37,075.08
Electronic of Signed & Sealed Engineering: \$1,000.00
Freight: Prepaid Ship Method: Best Way FOB: Destination Weight: 2,306 lbs Freight Charge: \$4,750.00
Polygon Total: \$42,825.08

Vendor: Polygon **Proj Drawings:** Engr-permits 603390

Class	Part No	Qty	Description	Unit Price	Disc	Net Price	Ext Price
Shelters	23133R0	1 EA	Polygon Shelter Model: REK 16x18 Primary Roof: PBR Secondary Roof: N/A Number of Columns 4	43,712.00	-8.0%	40,215.04	40,215.04

Eave Height (UPB): 8

Upper Roof Slope: 4/12

Electrical Cutout: 4

Electrical Access: Yes

Ornamentation: N/A

Powder Coat over Galvanized

Exposure D

Lightning Protection: N/A

Anchor Bolts Included

2023 Florida Building Code 8th Edition

Engineering to comply with HVHZ:yes

Discount per the Sourcwell (NJPA) Purchasing Contract #012621-PPC: \$3,496.96	Polygon Total:	\$40,215.04
---	----------------	-------------

General Terms of Sale and Proposal Summary

Net 30	Product:	\$108,763.24
	Freight:	\$7,950.00
	Proposal Total:	\$116,713.24

Notes

Sourcwell Purchasing Contract #012621-PPC for Polygon: 8% discount off of product list price. All structures in Florida exceed the standard wind load conditions, and are therefore not included in the Sourcwell price list. The contract limits installation to 42% of the list price, before discount. Site preparation, concrete, engineered footings and freight are not subject to the Sourcwell contract.

Basis of Proposal:
Our proposal is based upon a request for shelters. Email request received 4/21/2024 for SQR 12, SQR 16 and REK 16x18 for equipment only.

- Proposal includes:
- Supply of equipment requested
 - Freight to site
 - Engineering for structure
- Proposal excludes
- Offloading, assembly, foundations and installation of shelters
 - permit filing and permit fees

Please note the vendor information itemized below.

If a performance and payment bond is required, add 3% to the proposal total.
If a owner controlled insurance program (OCIP) is required, add 2% to the proposal total.

Also, please be aware that we generate separate invoices for product at the time of delivery. If your project should include products from multiple manufacturers, each will be invoiced and taxed separately. If you require consolidated invoices, please alert your sales team.

Estimated project completion schedule
(This schedule starts when all required information for engineering has been gathered.)
8 Weeks: Shelter Engineering
4 Weeks: Submittal Approval
17 Weeks Longest manufacturing lead time. (Typical for scheduling.)
1 Week Shipping
30 Weeks TOTAL
Note that RSI is committed to do all it can to meet the needs of your project.

This proposal is for material, freight, and applicable tax only. Any building permits, engineering, unloading, assembly, installation, site preparation and surfacing are by others. Drivers will not unload the shipment. Purchaser must make arrangements for unloading of playground or exercise equipment, shade, and shelter product lines. In most circumstances this will require a forklift. For certain site furnishing orders, a lift gate and pallet jack may be available for an additional fee. Please alert your sales team of this need.

- Polygon by PorterCorp:**
- Porter units are designed to meet 2023 Florida Building Code 8th Edition.
 - Please provide Building Department permit application requirements including Risk Category.
 - The following certificates are available:
 - Miami-Dade County Certificate of Competency No. 23-0915.11
 - PCI (Powder Coating Institute) 4000 Certified
 - American Institute of steel construction quality management systems certified
 - Four sets of signed and sealed drawings and calc books for building permitting will be provided. If additional sets of drawings and calc books are required, additional fees will apply.

Electrical Cutout: Selections to be made at time of electrical cut out submittal approval
Color Selection:
To be made at time of color submittal approval
Can find standard roofing and frame color selections here: <https://polygon.com/shelter-option/frame-roof-colors/>
Non-Standard colors and finishes are available at an additional charge

Warranty
The 10-year limited warranty excludes buildings erected at sites where salt air, corrosive environment, high humidity, or sprinkler systems come in

contact with the shelter.

Failure to maintain the finished system with annual touch-ups and documented maintenance procedures will void the limited warranty.

See Polygon warranty document for full details and terms.

Terms Porter Billing

Porter requires a 50% deposit with the order before fabrication can begin. Balance net 15 with credit approval.

Time Limitations Holding Prices Firm:

Orders are shipped within our manufacturer's standard lead times. Requests for delayed shipping may result in additional costs due to increases in freight, material costs or other factors. To secure the prices on this proposal, the offer must be accepted prior to the expiration date noted.

If, during the performance of this contract, the price of a product increases 3% or more as documented by factory quotes, invoices or receipts to contractor (Rep Services, Inc.) from the date of the contract signing the price of shall be equitably adjusted by an amount reasonably necessary to cover such price increases. Where the delivery of a product is delayed, through no fault of contractor (RSI) as a result of the shortage or unavailability of a product, contractor (RSI) shall not be liable for any additional costs or damages associated with such delay(s).

The undersigned warrants that he/she is an authorized representative of the City of Key West noted and has the requisite authority to bind the City of Key West and/or principal.

Accepted By:

City of Key West


Company Name

Authorized By

Printed Name

Date

As Its: (Title)



PROJECT: _____

LOCATION: _____

BUILDING TYPE: SQR-12

ROOF TYPE: MULTI-RIB

BUILDING NUMBER: _____

ORDER NUMBER: _____

QUOTE NUMBER: _____

DRAWING LIST:

SHEET NUMBER	DRAWING DESCRIPTION
CS	COVER SHEET
1	ARCHITECTURAL ELEVATIONS
2	STRUCTURAL FRAMING PLAN
3	COLUMN LAYOUT

CERTIFICATES:
MIAMI-DADE COUNTY CERTIFICATE OF COMPETENCY NO. 21-0819.13
POI (POWDER COATING INSTITUTE) 4000 CERTIFIED

FABRICATOR APPROVALS:
CITY OF PHOENIX, AZ APPROVED FABRICATOR #C08-2010
CITY OF LOS ANGELES, CA APPROVED FABRICATOR #FB01586
CITY OF RIVERSIDE, CA APPROVED FABRICATOR #SF_000042
CITY OF HOUSTON, TX APPROVED FABRICATOR #470
CLARK COUNTY, NV APPROVED FABRICATOR #264
SANTA CLAY COUNTY, GA APPROVED FABRICATOR 02008-14
AISC APPROVED FABRICATOR C-00018751

MATERIALS:

DESCRIPTION
PIPE STEEL
SCHEDULE PIPE
RMT PIPE
LIGHT GAGE COLD FORMED
STRUCTURAL STEEL PLATE
ROOF PANELS (STEEL)

ASTM DESIGNATION
A500 (GRADE B)
A53 (GRADE B)
A519
A1003 (GRADE 50)
A36
A653

STOP!!

NOT FOR CONSTRUCTION

USE FOR PRELIMINARY
PLANNING AND ESTIMATING
ONLY



GENERAL NOTES:
UNLESS NOTED OTHERWISE, THIS STRUCTURE WAS DESIGNED TO
ONLY SUPPORT WHAT IS SHOWN ON THESE DRAWINGS. THE
MANUFACTURER MUST BE CONTACTED IF ANYTHING ELSE IS TO BE
ATTACHED TO THIS STRUCTURE (WALLS, COLUMN WRAPS, RAILINGS,
ETC.). THE DESIGN OF THIS STRUCTURE CAN BE REVIEWED AND
POSSIBLY REVISED.

UNLESS NOTED OTHERWISE, THIS STRUCTURE WAS DESIGNED
ASSUMING A 20' SEPARATION BETWEEN ANY ADJACENT STRUCTURE
WITH AN EAVE HEIGHT EQUAL TO OR GREATER THAN THE EAVE
HEIGHT OF THIS STRUCTURE. IF AN ADJACENT STRUCTURE EXISTS,
THE MANUFACTURER MUST BE CONTACTED SO THE DESIGN OF THIS
STRUCTURE CAN BE REVIEWED AND POSSIBLY REVISED.


STRUCTURAL STEEL SHALL BE DETAILED, FABRICATED, AND ERECTED
IN ACCORDANCE WITH THE LATEST EDITION OF THE AMERICAN
INSTITUTE OF STEEL CONSTRUCTION (AISC) SPECIFICATION MANUAL.

ALL WELDING IS PERFORMED BY AMERICAN WELDING SOCIETY
(AWS) CERTIFIED WELDERS AND CONFORMS TO THE LATEST EDITION
OF AWS D1.1 OR D1.3 AS REQUIRED.

PARTS SHOWN MAY BE UPGRADED DUE TO STANDARDIZED
FABRICATION. REFER TO THE SHIPPING BILL OF MATERIALS FOR
POSSIBLE SUBSTITUTIONS.




FOR PROPER FIELD INSTALLATION OF THE BUILDING IT IS
RECOMMENDED THAT THE INSTALLER HAVE THE FOLLOWING
EXPERIENCE INSTALLING THIS TYPE OF PRODUCT.

FOR PROPER FIELD INSTALLATION OF THE BUILDING IT IS
RECOMMENDED THAT ELECTRIC WIRING, IF REQUIRED, BE RUN
BEFORE THE STRUCTURAL MEMBERS BEFORE THE BUILDING IS
ERECTED.

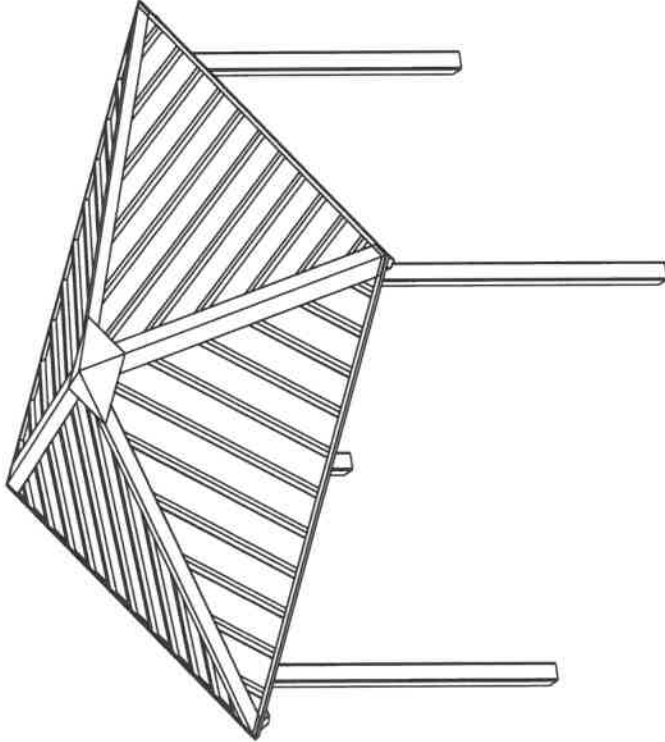

GENERAL ROOF NOTES:

1. METAL ROOFING:
 - 24 GAUGE
 - GALVALUME COATED
 - KYNAR 500 PAINTED
 - TRIM COLOR MATCHES ROOF
2. SEE POLYGON.COM FOR COLOR OPTIONS
- 3.

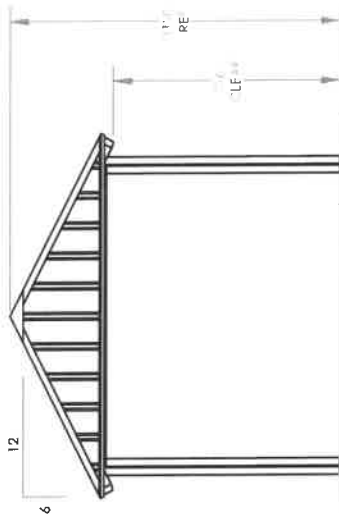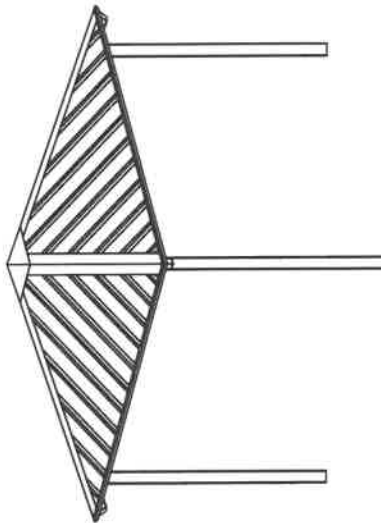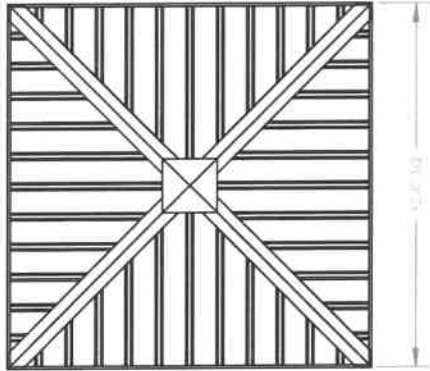

STOP!!
NOT FOR CONSTRUCTION
USE FOR PRELIMINARY
PLANNING AND ESTIMATING
ONLY




DRAWING:
ARCHITECTURAL ELEVATIONS
DATE: 11/18
REV: A

SHEET

1

poligon® (616)399-1963
www.poligon.com
by PORTERCORP

COPYRIGHT 2014
PORTERCORP EASTERN, L.L.C. HOLLAND, MI 48034

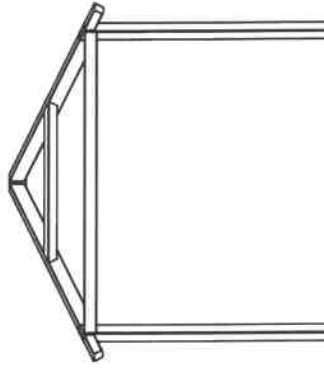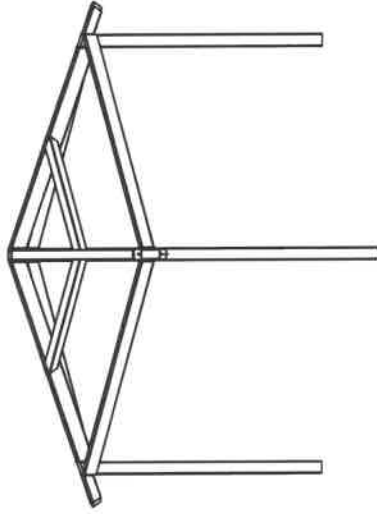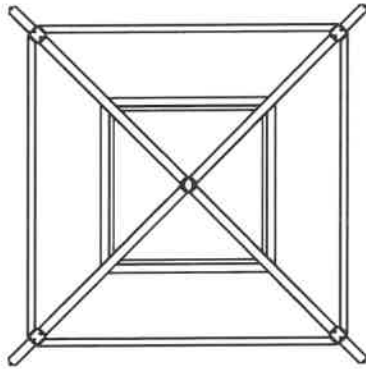


FINISH GRADE.
MOUNTING VARIES
BASED ON ENGINEERING
REQUIREMENTS.

STOP!!
NOT FOR CONSTRUCTION
USE FOR PRELIMINARY
PLANNING AND ESTIMATING
ONLY

DRAWING: STRUCTURAL FRAMING PLAN		SHEET 2	
SCALE: 1:48	REV LEVEL: A	www.poligon.com by PORTERCORP	
POLIGON® CORPORATION PATENTED OR PENDING PORTERCORP 428 N. 13TH AVE HOLLAND, MI 49423			


BASEPLATE NOTES:

1. POLYGON ENGINEERING WILL DETERMINE REQUIRED BASEPLATE DESIGN AFTER ENGINEERING PACKAGE IS ORDERED.
2. CUSTOMER MAY SUGGEST PREFERRED BASEPLATE DESIGN.

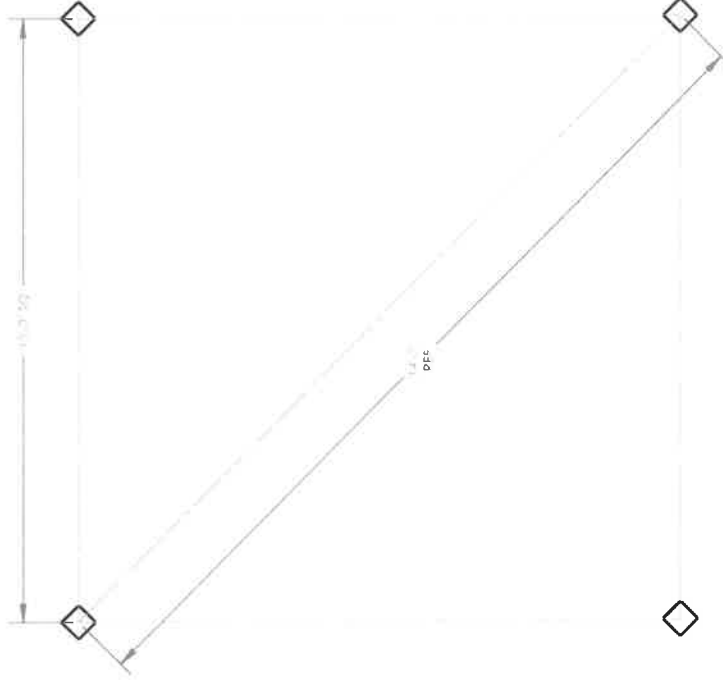

STOP!!
NOT FOR CONSTRUCTION
USE FOR PRELIMINARY
PLANNING AND ESTIMATING
ONLY

DRAWING: COLUMN LAYOUT		REV LEVEL:
SCALE:	1:24	A
poligon ® (616)399-1963 www.poligon.com CORPORATION ATTENTION: SALES PORTERCORP 5200 N. 138th AVE. HOLLAND, MI 48034		SHEET 3

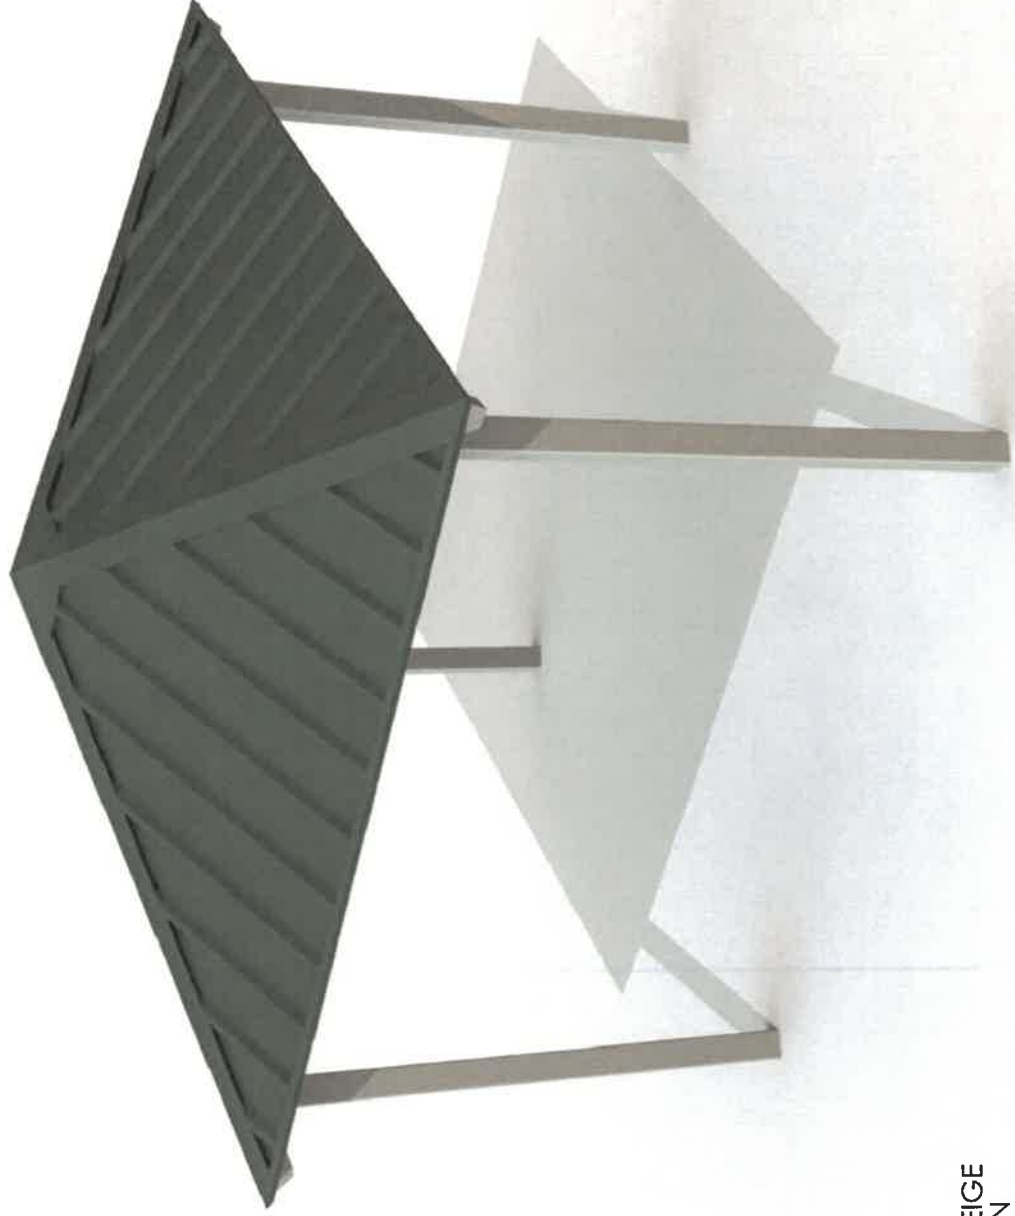

FRAME COLOR: SURREY BEIGE
ROOF COLOR: EVERGREEN
COLORS SHOWN FOR ILLUSTRATIVE PURPOSES ONLY. FOR OTHER
COLOR SELECTIONS, PLEASE SUBMIT AN ET DRAWING REQUEST.


SQR-12

poligon®

PROJECT: _____
LOCATION: _____
BUILDING TYPE: SQR-16
ROOF TYPE: MULTI-RIB
BUILDING NUMBER: _____
ORDER NUMBER: _____
QUOTE NUMBER: _____

DRAWING LIST:

SHEET NUMBER	DRAWING DESCRIPTION
CS	COVER SHEET
1	ARCHITECTURAL ELEVATIONS
2	STRUCTURAL FRAMING PLAN
3	COLUMN LAYOUT

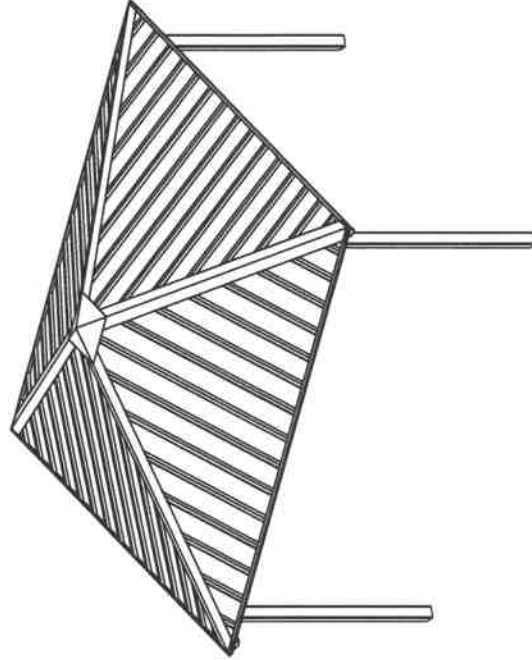

CERTIFICATES:
MAVAD COUNTY CERTIFICATE OF COMPETENCY NO. 21-0819.13
PCI (POWDER COATING INSTITUTE) 4000 CERTIFIED

FABRICATOR APPROVALS:
CITY OF PHOENIX, AZ APPROVED FABRICATOR #C08-2010
CITY OF PHOENIX, AZ APPROVED FABRICATOR #P801996
CITY OF RIVERSIDE, CA APPROVED FABRICATOR #00042
CITY OF HOUSTON, TX APPROVED FABRICATOR #470
CLARK COUNTY, NV APPROVED FABRICATOR #264
STATE OF UTAH APPROVED FABRICATOR 02008-14
AISC APPROVED FABRICATOR C-00018751

MATERIALS:

DESCRIPTION	ASTM DESIGNATION
SCHEDULE PIPE	A500 (GRADE B)
RMT PIPE	A519
LIGHT GAGE COLD FORMED	A1003 (GRADE 50)
STRUCTURAL STEEL PLATE	A36
ROOF PANELS (STEEL)	A653

STOP!!
NOT FOR CONSTRUCTION
USE FOR PRELIMINARY
PLANNING AND ESTIMATING
ONLY

GENERAL NOTES:
UNLESS NOTED OTHERWISE, THIS STRUCTURE WAS DESIGNED TO
BE CONSTRUCTED IN ACCORDANCE WITH THE LATEST EDITION
OF THE AISC STEEL CONSTRUCTION MANUAL. THE DESIGNER
MANUFACTURER MUST BE ADVISED OF ANY CHANGES TO BE
ATTACHED TO THIS STRUCTURE (WALLS, COLUMN WRAPS, RAILINGS,
ETC.) SO THE DESIGN OF THIS STRUCTURE CAN BE REVIEWED AND
POSSIBLY REVISED.

UNLESS NOTED OTHERWISE, THIS STRUCTURE WAS DESIGNED
ASSUMING A 20' SEPARATION BETWEEN THE EAVES OF ADJACENT
WITH AN EAVE HEIGHT EQUAL TO OR GREATER THAN THE EAVE
HEIGHT OF THIS STRUCTURE. IF THAT SEPARATION DOES NOT EXIST,
THE MANUFACTURER MUST BE CONTACTED SO THE DESIGN OF THIS
STRUCTURE CAN BE REVIEWED AND POSSIBLY REVISED.

STRUCTURAL STEEL SHALL BE DETAILED, FABRICATED, AND ERECTED
IN ACCORDANCE WITH THE LATEST EDITION OF THE AMERICAN
INSTITUTE OF STEEL CONSTRUCTION (AISC) SPECIFICATION MANUAL.

ALL WELDING IS PERFORMED BY AMERICAN WELDING SOCIETY
(AWS) CERTIFIED WELDERS AND CONFORMS TO THE LATEST EDITION
OF AWS D1.1 OR D1.3 AS REQUIRED.

PARTS SHOWN MAY BE UPGRADED DUE TO STANDARDIZED
FABRICATION. REFER TO THE SHIPPING BILL OF MATERIALS FOR
POSSIBLE SUBSTITUTIONS.




FOR PROPER FIELD INSTALLATION OF THE BUILDING, IT IS
RECOMMENDED THAT THE PRIMARY FRAME INSTALLER AND THE
ROOF INSTALLER HAVE A MINIMUM FIVE (5) YEARS DOCUMENTED
EXPERIENCE INSTALLING THIS TYPE OF PRODUCT.

FOR PROPER FIELD INSTALLATION OF THE BUILDING, IT IS
RECOMMENDED THAT ELECTRIC WIRING BE RUN
THROUGH THE STRUCTURAL MEMBERS BEFORE THE BUILDING IS
ERECTED.



GENERAL ROOF NOTES:

1. METAL ROOFING:
 - 24 GAUGE
 - GALVALUME COATED
 - KYNAR 500 PAINTED
 - TRIM COLOR MATCHES ROOF
2. SEE POLYGON.COM FOR COLOR OPTIONS
- 3.

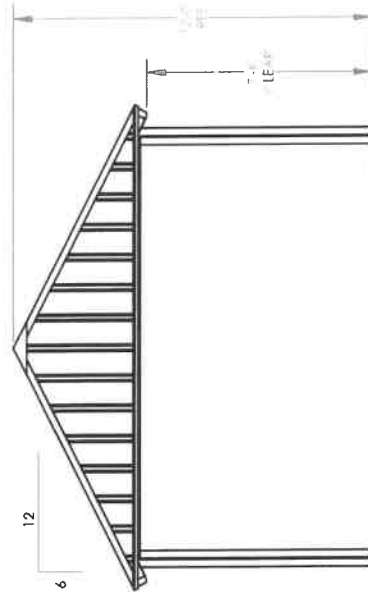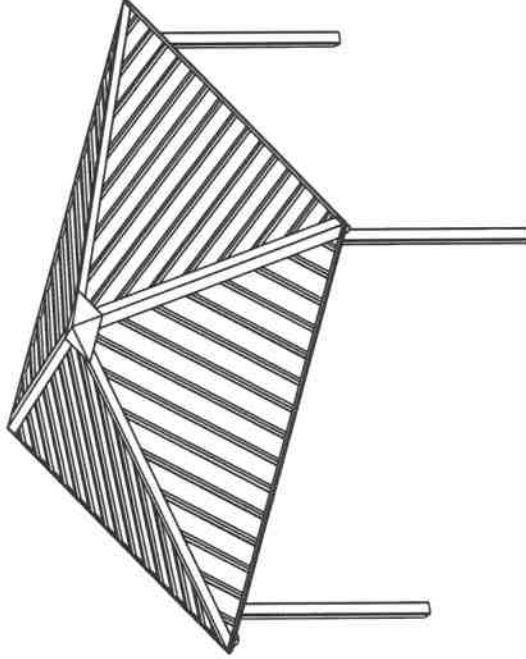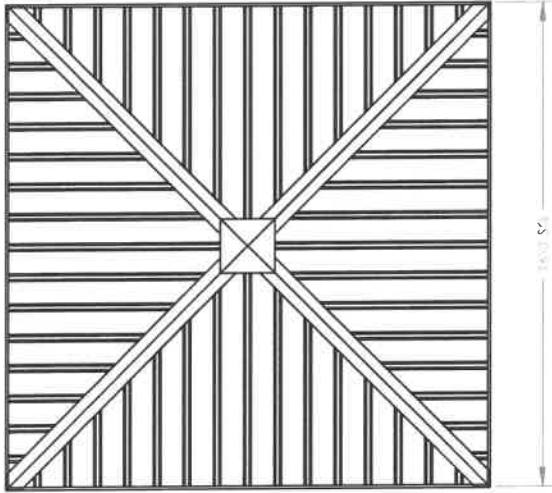




FINISH GRADE
MOUNTING VARIES
BASED ON ENGINEERING
REQUIREMENTS.

STOP!!
NOT FOR CONSTRUCTION
USE FOR PRELIMINARY
PLANNING AND ESTIMATING
ONLY

DRAWINGS
ARCHITECTURAL ELEVATIONS
SCALE
1:48
REV. BY: A

poligon® (616) 399-1963
www.poligon.com
by PORTERCORP
COPYRIGHT 2014
PORTERCORP 12345 N. 12345 AVE. HOLLAND, MI 48034

SHEET
1

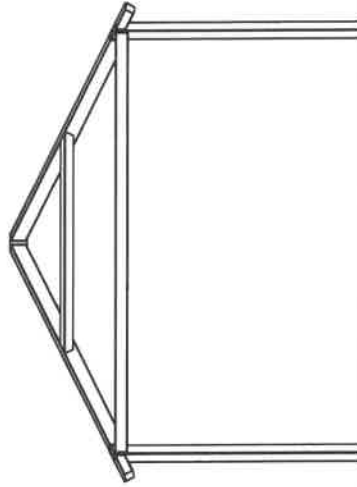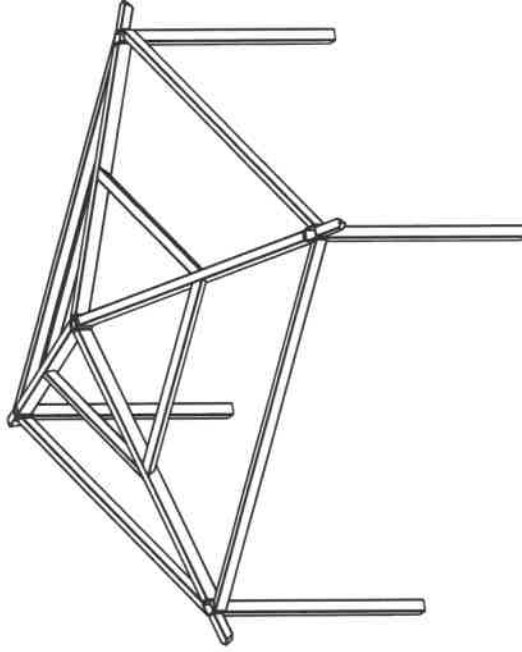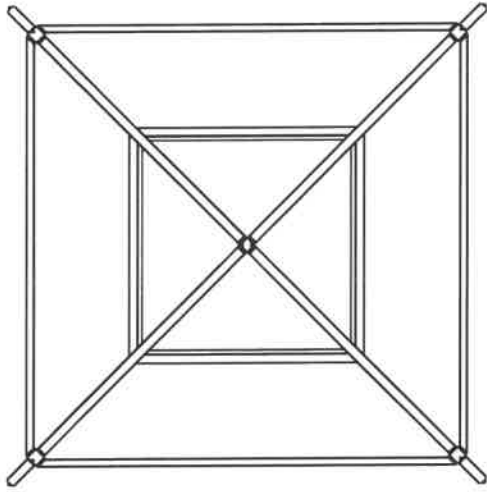


FINISH GRADE
MOUNTING VARIES
BASED ON ENGINEERING
REQUIREMENTS.

STOP!!
NOT FOR CONSTRUCTION
USE FOR PRELIMINARY
PLANNING AND ESTIMATING
ONLY

BASEPLATE NOTES:


1. POLYGON ENGINEERING WILL DETERMINE REQUIRED BASEPLATE DESIGN AFTER ENGINEERING PACKAGE IS ORDERED.
2. CUSTOMER MAY SUGGEST PREFERRED BASEPLATE DESIGN.

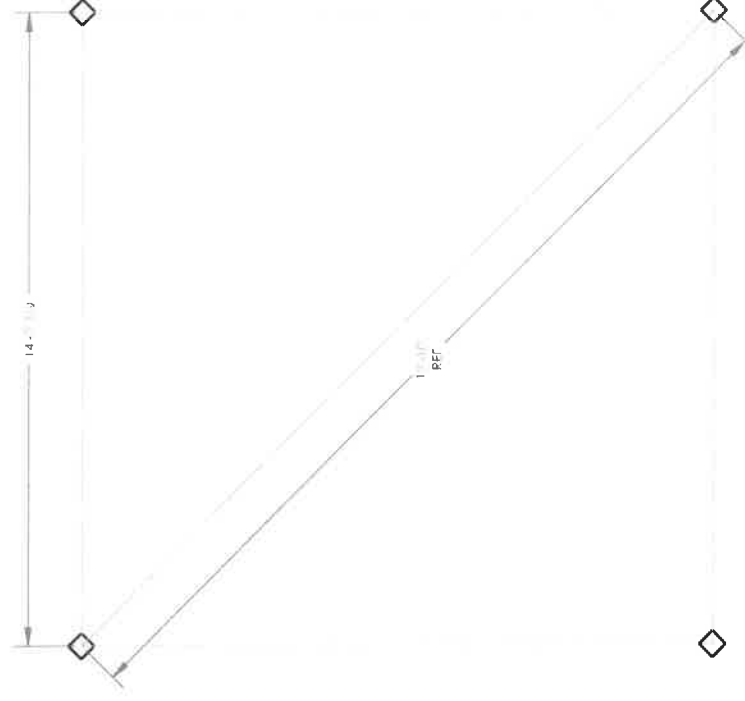

STOP!!
NOT FOR CONSTRUCTION
USE FOR PRELIMINARY
PLANNING AND ESTIMATING
ONLY

DRAWINGS	COLUMN LAYOUT		REV. LEVEL	A	SHEET	
SCALE	1'-32"					
polygon®		(616) 399-1963 www.polygon.com	by PORTERCORP			
COPYRIGHT 2014						
PARENT OF PATENTE PAVING						
PORTERCORP - 4240 N. 138th AVE. HOLLAND, MI 48126						

poligon®

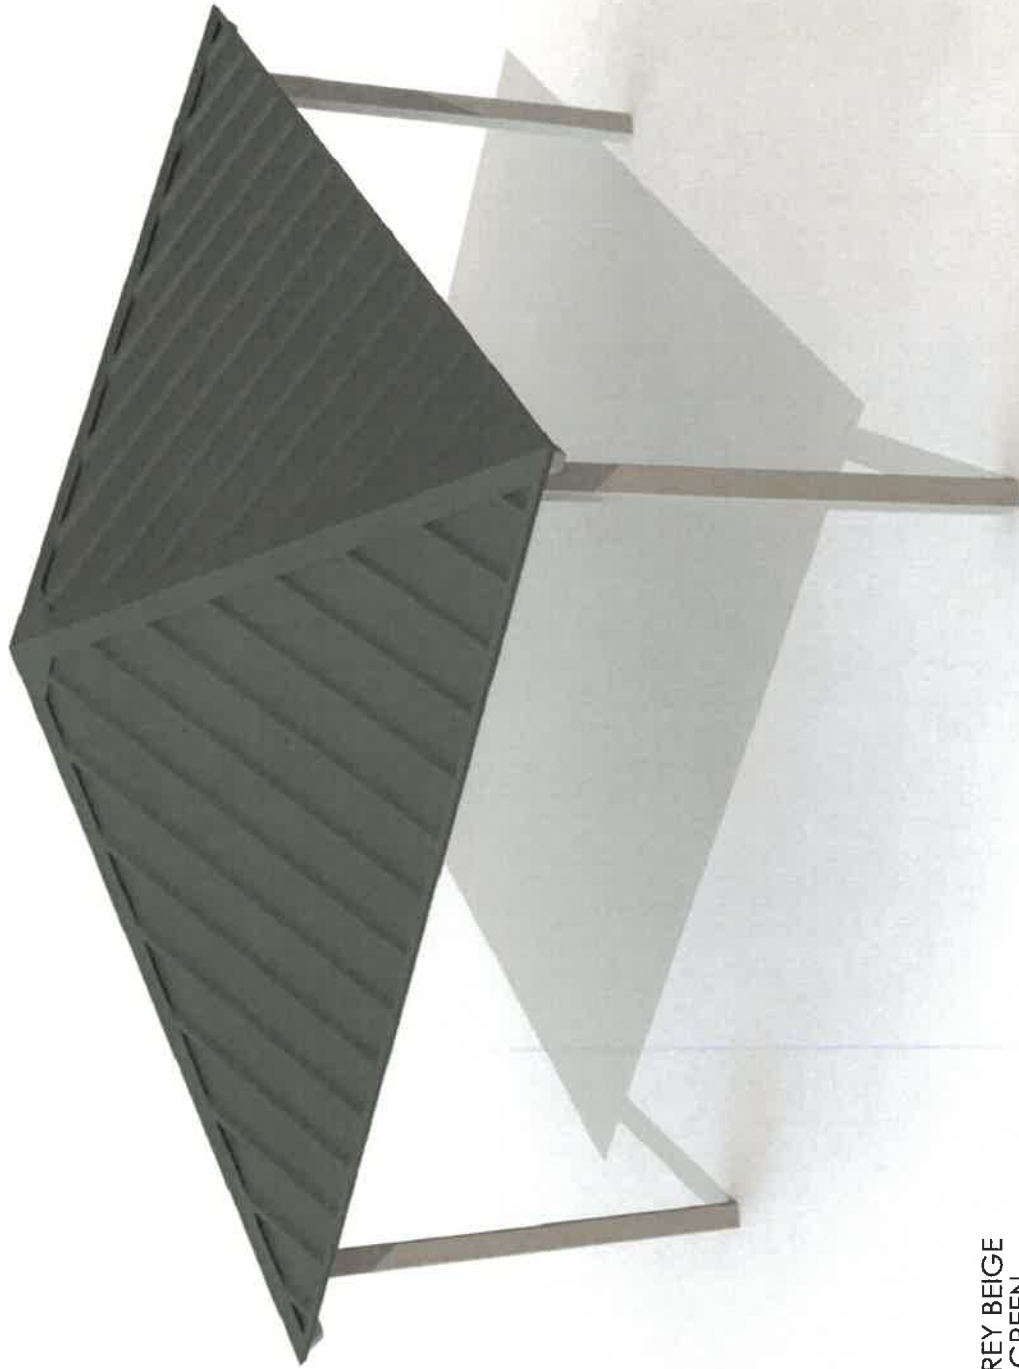

FRAME COLOR: SURREY BEIGE
ROOF COLOR: EVERGREEN
COLORS SHOWN FOR ILLUSTRATIVE PURPOSES ONLY. FOR OTHER
COLOR SELECTIONS, PLEASE SUBMIT AN E1 DRAWING REQUEST.

SQR-16
