ID	Task Mode	Task Name	Duration	Start	Finish
1		**PUMP STATION G REHAB**	**388 days**	**Mon 1/29/24**	**Wed 7/23/25**
2					
3		**NTP**	0 days	Mon 1/29/24	Mon 1/29/24
4		**Submittals**	**305 days**	**Mon 1/29/24**	**Fri 3/28/25**
5		Control Panel	55 days	Mon 1/29/24	Fri 4/12/24
6		Temp Bypass Plan	45 days	Mon 1/29/24	Fri 3/29/24
7		Pumps	45 days	Mon 1/29/24	Fri 3/29/24
8		Sluice Gate	106 days	Fri 11/1/24	Fri 3/28/25
9		Check Valves	40 days	Mon 1/29/24	Fri 3/22/24
10		Plug Valves	40 days	Mon 1/29/24	Fri 3/22/24
11		HDPE Fittings	40 days	Mon 1/29/24	Fri 3/22/24
12		Odor Control	40 days	Mon 1/29/24	Fri 3/22/24
13		Permits	30 days	Mon 1/29/24	Fri 3/8/24
14					
15		**Procurement**	**276 days**	**Mon 3/11/24**	**Mon 3/31/25**
16		**Control Panel**	**2 days**	**Tue 1/28/25**	**Wed 1/29/25**
17		Control Panel ETA	2 days	Tue 1/28/25	Wed 1/29/25
18		**Pumps**	**2 days**	**Wed 1/29/25**	**Thu 1/30/25**
19		ETA	2 days	Wed 1/29/25	Thu 1/30/25
20		**Sluice Gate**	**1 day**	**Mon 3/31/25**	**Mon 3/31/25**
21		ETA	1 day	Mon 3/31/25	Mon 3/31/25
22		Check Valves	40 days	Mon 3/25/24	Fri 5/17/24
23		Plug Valves	50 days	Mon 3/25/24	Fri 5/31/24
24		HDPE Fittings	20 days	Mon 3/25/24	Fri 4/19/24
25		Permits	20 days	Mon 3/11/24	Fri 4/5/24
26					
27		**General Site**	**29 days**	**Thu 1/2/25**	**Tue 2/11/25**
28		Mobilization	2 days	Thu 1/2/25	Fri 1/3/25
29		Erosion Control	2 days	Mon 1/6/25	Tue 1/7/25
30		Dewatering Well	10 days	Wed 1/8/25	Tue 1/21/25
31		Demolition	5 days	Wed 1/22/25	Tue 1/28/25
32		Pump out Connection	10 days	Wed 1/29/25	Tue 2/11/25
33		**Temporary Bypass**	**128 days**	**Mon 1/6/25**	**Wed 7/2/25**
34		Install pipe, conduits, and fencing	5 days	Thu 1/30/25	Wed 2/5/25
35		Install Pumps, floats, and telemetry	10 days	Thu 2/6/25	Wed 2/19/25
36		Bypass	90 days	Thu 2/20/25	Wed 6/25/25
37		Removal and restoration	5 days	Thu 6/26/25	Wed 7/2/25
38		Access Hatches	20 days	Wed 2/12/25	Tue 3/11/25
39		Yard Pipping	20 days	Thu 3/13/25	Wed 4/9/25
40		Aluminum Platform and Stairs	20 days	Mon 1/6/25	Fri 1/31/25
41					
42		**Electrical**	**121 days**	**Mon 1/6/25**	**Mon 6/23/25**
43		Temporary Power	5 days	Mon 1/6/25	Fri 1/10/25
44		Electrical Service/meter	15 days	Mon 1/13/25	Fri 1/31/25
45		ATS	5 days	Mon 2/3/25	Fri 2/7/25
46		Junction Boxes	5 days	Mon 2/10/25	Fri 2/14/25
47		Under ground cond uitsPumps/Controls/Sensors	15 days	Mon 2/17/25	Fri 3/7/25
48		Grounding	5 days	Mon 3/10/25	Fri 3/14/25
49		Lighting Protection	5 days	Mon 3/17/25	Fri 3/21/25
50		Terminations	10 days	Thu 6/5/25	Wed 6/18/25
51		Testing	3 days	Thu 6/19/25	Mon 6/23/25
52					
53		**Wet Well and Valve Vault**	**80 days**	**Thu 2/20/25**	**Wed 6/11/25**
54		Demolition	15 days	Thu 2/20/25	Wed 3/12/25
55		Concrete Repair	20 days	Thu 3/13/25	Wed 4/9/25
56		Pumps/Valves/Pipe	20 days	Thu 4/10/25	Wed 5/7/25
57		Coatings	20 days	Thu 5/8/25	Wed 6/4/25
58		Testing	5 days	Thu 6/5/25	Wed 6/11/25
59					
60		**Odor Control**	**32 days**	**Thu 3/13/25**	**Fri 4/25/25**
61		Concrete Pad	10 days	Thu 3/13/25	Wed 3/26/25
62		Odor Control Unit	10 days	Thu 3/27/25	Wed 4/9/25
63		Piping	10 days	Thu 4/10/25	Wed 4/23/25
64		Testing	2 days	Thu 4/24/25	Fri 4/25/25
65					
66		**Instrumentation and Controls**	**90 days**	**Mon 2/3/25**	**Fri 6/6/25**
67		Control Panel	15 days	Mon 2/3/25	Fri 2/21/25
68		Flowmeter	5 days	Thu 5/8/25	Wed 5/14/25
69		Floats/Salinity meter/P. Gauges	10 days	Thu 5/15/25	Wed 5/28/25
70		Antenna	5 days	Thu 5/29/25	Wed 6/4/25
71		Testing	2 days	Thu 6/5/25	Fri 6/6/25
72					
73		**Restoration**	**13 days**	**Thu 5/29/25**	**Mon 6/16/25**
74		Fencing	5 days	Thu 5/29/25	Wed 6/4/25
75		Concrete	5 days	Thu 6/5/25	Wed 6/11/25
76		Asphalt	3 days	Thu 6/12/25	Mon 6/16/25
77					
78		**Facility Testing/Start-up**	10 days	Thu 6/12/25	Wed 6/25/25
79					
80		**Substantial Completion**	0 days	Wed 6/25/25	Wed 6/25/25
81		**Punch out**	10 days	Thu 6/26/25	Wed 7/9/25
82		**Close out documents**	10 days	Thu 7/10/25	Wed 7/23/25
83		**Final Completion**	0 days	Wed 7/23/25	Wed 7/23/25

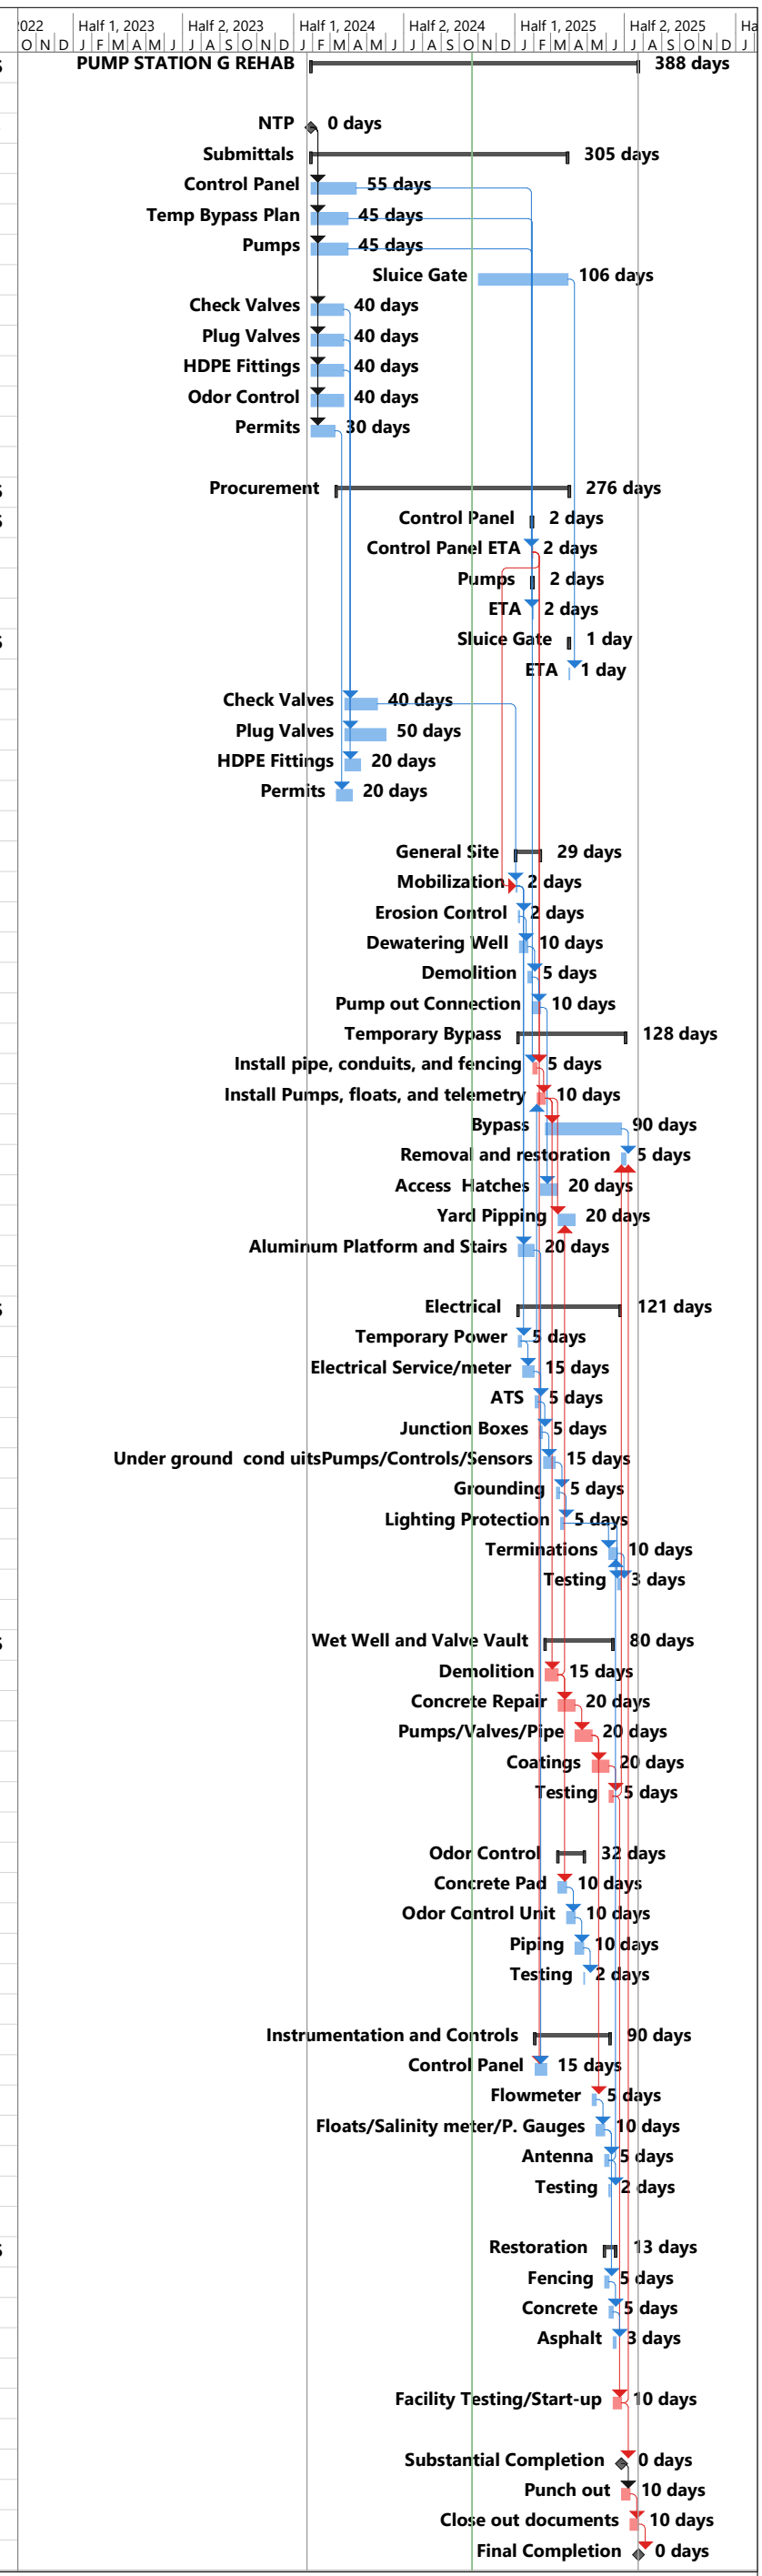

Project: Project1
Date: Tue 10/22/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress
