


CONTRACT DOCUMENTS FOR:



ITB #18-005

**DOCK REPAIR & PILING REPLACEMENT
D-DOCK
KEY WEST HISTORIC SEAPORT**

JULY 2018

CITY OF KEY WEST

MAYOR: CRAIG CATES

COMMISSIONERS:

JIMMY WEEKLEY

SAMUEL KAUFMAN

BILLY WARDLOW

RICHARD G. PAYNE

MARGARET ROMERO

CLAYTON LOPEZ

PREPARED BY:
City of Key Wes
Port & Marine Services

ITB DOCUMENTS

CITY OF KEY WEST

CAROLINE STREET AND BAHAMA VILLAGE
COMMUNITY REDEVELOPMENT AGENCY (CRA)

KEY WEST, FLORIDA

DOCUMENTS

for

**DOCK REPAIR & PILING REPLACEMENT
D-DOCK
KEY WEST HISTORIC SEAPORT**

CONSISTING OF:

PROCUREMENT REQUIREMENTS
CONTRACT FORMS
CONDITIONS OF THE CONTRACT
TECHNICAL SPECIFICATIONS
SUPPLEMENTAL INFORMATION

KEY WEST HISTORIC SEAPORT (KWHS)

JULY 2018

TABLE OF CONTENTS

	<u>Page</u>
PART 1 - <u>PROCUREMENT REQUIREMENTS</u>	
INVITATION TO BID	1
INSTRUCTIONS TO BIDDERS.....	3
BID FORMS	11
BID BOND	21
ANTI-KICKBACK AFFIDAVIT	23
PUBLIC ENTITIES CRIME FORM.....	24
CITY OF KEY WEST INDEMNIFICATION.....	26
EQUAL BENEFITS FOR DOMESTIC PARTNERS AFFIDAVIT	27
CONE OF SILENCE	28
NON-COLLUSION AFFIDAVIT	29
LOCAL VENDOR CERTIFICATION	30
BIDDER'S CHECKLIST	31
PART 2 - <u>CONTRACT FORMS</u>	
CONTRACT	33
FLORIDA PERFORMANCE BOND	35
FLORIDA PAYMENT BOND	37
LICENSE REQUIREMENT AND COST.....	39
PART 3 - <u>CONDITIONS OF THE CONTRACT</u>	
GENERAL CONDITIONS	43
SUPPLEMENTARY CONDITIONS	60
PART 4 - <u>SPECIFICATIONS</u>	
01001 GENERAL REQUIREMENTS	68
01010 SCOPE OF WORK.....	70
01025 MEASUREMENT AND PAYMENT	72
01300 SUBMITTALS	73
01700 CONTRACT CLOSEOUT.....	86
PART 5 – <u>SUPPLEMENTAL INFORMATION</u>	79
MATERIALS LIST	
DOCK PLAN VIEW W/ REPLACEMENT LEGEND AND PHOTOS	
ENVIRONMENTAL PERMITS	

PART 1

PROCUREMENT REQUIREMENTS

INVITATION TO BID

Sealed Bids for City of Key West Caroline Street and Bahama Village Community Redevelopment Agency (CRA) “**DOCK REPAIR & PILING REPLACEMENT, D-DOCK – KEY WEST HISTORIC SEAPORT,**” addressed to the City of Key West, will be received at the office of the City Clerk, 1300 White Street, Key West, Florida until **3:00 p.m.**, local time, on the **6th day of September 2018**, and then will be publicly opened and read. Any bids received after the time and date specified will not be considered.

Please submit one (1) original bid package and two (2) electronic copies on USB drives with a single PDF file of the entire bid package. Bid package shall be enclosed in a sealed envelope, clearly marked on the outside “**ITB #18-005 DOCK REPAIR & PILING REPLACEMENT, D-DOCK – KEY WEST HISTORIC SEAPORT**” addressed and delivered to the City Clerk at the address noted above.

The CRA is seeking BIDS from qualified individuals or firms for wood dock repair and piling replacement within the Key West Historic Seaport. Work will include piling replacement, dock repairs including horizontal and diagonal cross-members, bents and joists and replacement stainless steel hardware per the Scope of Work.

The full Invitation to Bid may be obtained from Demand Star by Onvia and The City of Key West website. Please contact Demand Star at www.demandstar.com or call 1-800-711-1712 or www.cityofkeywest-fl.gov

A **Mandatory pre-bid meeting** will be held in the conference room at the KWHS Port and Marine Services Offices, 201 William Street, Key West, Florida on **August 28, 2018 at 2:30 p.m.**

EACH BID MUST BE SUBMITTED ON THE PRESCRIBED FORM AND ACCOMPANIED BY BID SECURITY AS PRESCRIBED IN THE INSTRUCTIONS TO BIDDERS, PAYABLE TO THE CITY OF KEY WEST, FLORIDA, IN AN AMOUNT NOT LESS THAN FIVE (5) PERCENT OF THE AMOUNT BID.

THE BIDDER MUST BE A LICENSED CONTRACTOR BY THE STATE OF FLORIDA AND SUBMIT PROOF OF SUCH WITH THE BID.

The Bidder shall furnish documentation showing that they are in compliance with the licensing requirements of the State and the provisions of Chapter 66 Section 87 of the Code of Ordinances of the City of Key West; within 10 days the following the Notice of Award and must demonstrate that he holds at a minimum, the following licenses & certificates;

- A. City of Key West License, as defined in Code of Ordinances, Chapter 66, enabling the Contractor to perform the work stated herein.
- B. City of Key West Business Tax License Receipt

All bid bonds, contract bonds, insurance contracts, and certificates of insurance shall be either executed by or countersigned by a licensed resident agent of the Surety or Insurance Company having his place of business in the State of Florida, and in all ways complying with the insurance

laws of the State of Florida. Further, the said Surety or Insurance Company shall be duly licensed and qualified to do business in the State of Florida.

Before a Contract will be awarded for the work contemplated herein, the CRA will conduct such investigation as is necessary to determine the performance record and ability of the apparent low Bidder to perform the size and type of work specified under this Contract. Upon request, the Bidder shall submit such information as deemed necessary by the CRA to evaluate the Bidder's qualifications.

The CRA hereby notifies all Bidders that it will affirmatively ensure that in any contract entered into pursuant to this advertisement, Disadvantaged Business Enterprise will be afforded full opportunity to submit bids in response to this invitation and will not be discriminated against on the grounds of race, color, gender, religion, age, disability, marital status or national origin in consideration for an award.

For information concerning the proposed work please contact Karen Olson, Deputy Director, Port and Marine Services by email at kolson@cityofkeywest-fl.gov. Verbal communications, per the City's "Cone of Silence" ordinance are not allowed.

As stated above at the time of the BID submittal the Bidder must provide satisfactory documentation of State Licenses. The Bidder shall furnish documentation showing that he is in compliance with the licensing requirements of County, and City licenses as would be required within ten days of the award. The successful Bidder must also be able to satisfy the City Attorney as to such insurance coverage and legal requirements as may be demanded by the Proposal in question. The CRA may reject BID for any and/or all of the following reasons: (1) for budgetary reasons, (2) if the proposer misstates or conceals a material fact in its bid, (3) if the proposal does not strictly conform to the law or is non-responsive to the bid requirements, (4) if the proposal is conditional, or (5) if a change of circumstances occurs making the purpose of the proposal unnecessary to the CRA. (6) if such rejection is in the best interest of the CRA. The CRA may also waive any minor formalities or irregularities in any proposal.

The CRA retains the right to award bid to the bidder that best meet the needs of the City.

* * * * *

INSTRUCTIONS TO BIDDERS

1. CONTRACT DOCUMENTS

A. FORMAT

The Contract Documents are divided into parts, divisions, and sections for convenient organization and reference. Generally, there has been no attempt to divide the Specification sections into work performed by the various building trades, work by separate subcontractors, or work required for separate facilities in the Project.

B. DOCUMENT INTERPRETATION

Separate sections contained within these Contract Documents are intended to be mutually cooperative and provide all details reasonably required for the execution of proposed work.

Should there be any doubt as to the meaning or intent of said Contract Documents, the Bidder should request of the Deputy Port and Marine Services Director, in writing (at least **5** calendar days prior to Bid opening) an interpretation thereof. Any interpretation or change in said Contract Documents will be made only in writing in the form of Addenda to the Documents, which will be furnished to all registered holders of Contract Documents. Bidders shall submit with their Bids, or indicate receipt of all Addenda. The Owner will not be responsible for any other explanation or interpretations of said Documents.

2. SCOPE OF SERVICES

A general description of the work to be done is contained in the Scope of Services section.

3. REQUIRED QUALIFICATIONS

The prospective Proposers must meet the statutorily prescribed requirements before award of Contract by the CRA. Proposers must hold or obtain all licenses and/or certificates as required by the State and Local Statutes in order to bid and perform the work specified herein. Additionally, all proposers must meet the minimum qualifications as described in Required Qualifications section.

4. BIDDER'S UNDERSTANDING

Each Proposer must inform himself of the conditions relating to the execution of the work and make himself thoroughly familiar with all the Contract Documents. Failure to do so will not relieve the successful Proposer of his obligation to enter into a Contract and complete the contemplated work in strict accordance with the Contract Documents.

Each Proposer shall inform himself of, and the Proposer awarded a Contract shall comply with, federal, state, and local laws, statutes, and ordinances relative to the execution of the work. This requirement includes, but is not limited to, applicable regulations concerning minimum wage rates, nondiscrimination in the employment of labor, protection of public and employee safety and health, environmental protection, the protection of natural

resources, fire protection, permits, fees, and similar subjects.

5. TYPE OF BID

UNIT PRICE

The Proposal for the work is to be submitted on a unit price basis. All items required to complete the work specified or shown on the Drawings but not included in the Proposal shall be considered incidental to those set forth in the Proposal. Payment to the Contractor will be made on the measurement of the work actually performed by the Contractor, as specified in the Contract Documents.

The Bidder further proposes to accept as full payment for the Work proposed herein, the amounts computed under the provisions of the Contract Documents and based on the following unit price amounts. The Bidder agrees that the unit prices include all allowances for overhead and profit for each type and unit of work called for in these Contract Documents.

Total allowable cost for Mobilization, General/Supp Conditions and Demobilization (bid schedule line item 1) shall be 10% maximum of total construction costs (bid schedule line items 4 through 12).

6. PREPARATION OF BIDS

A. GENERAL

All blank spaces in the BID form must be filled in for all schedules and associated parts, as required, preferably in BLACK INK. All price information shall be clearly shown in both words and figures where required. No changes shall be made in the phraseology of the forms. Written amounts shall govern in case of discrepancy between the amounts stated in writing and the amounts stated in figures. In case of discrepancy between unit prices and extended totals, unit prices shall prevail.

Any BID shall be deemed informal which contains omissions, erasures, alterations, or additions of any kind, or prices uncalled for, or in which any of the prices are obviously unbalanced, or which in any manner shall fail to conform to the conditions of the published Invitation to BID.

Only one BID from any individual, firm, partnership, or corporation, under the same or different names, will be considered. Should it appear to the Owner that any Bidder is interested in more than one BID for work contemplated; all Bids in which such Bidder is interested will be rejected.

B. SIGNATURE

The Bidder shall sign his BID in the blank space provided therefor. If Bidder is a corporation, the legal name of the corporation shall be set forth above together with the signature of the officer or officers authorized to sign Contracts on behalf of the corporation. If Bidder is a partnership, the true name of the firm shall be set forth above together with the

signature of the partner or partners authorized to sign Contracts in behalf of the partnership. If signature is by an agent, other than an officer of a corporation or a member of a partnership, a notarized power-of-attorney must be on file with the Owner prior to opening of Bids or submitted with the Bid otherwise the Bid will be regarded as not properly authorized.

C. SPECIAL BIDDING REQUIREMENTS

The Bidder's attention is brought to the hiring practices and licenses and permits of the City of Key West. These are defined in the addition to Article 39, ORDINANCES, PERMITS, AND LICENSES, as set forth in the Supplementary Conditions.

The Bidder shall submit with his Bid his experience record showing his experience and expertise in site construction and related work. Such experience record shall provide at least five current or recent projects of similar work, not more than 5 years old within the State Florida and preferably Monroe County. For each project the following information shall be provided:

1. Description and location of work.
2. Contract amount.
3. Dates work was performed.
4. Owner.
5. Name of Owner's contact person and phone number.
6. Engineer.
7. Name of Engineer's contact person and phone number.

The bidder shall submit at least 3 references from the above work experience.

The bidder shall submit with his bid a list of items to be performed by his own labor and that performed by subcontractors or others.

D. ATTACHMENTS

Bidder shall complete and submit the following forms with his bid:

1. Anti-Kickback Affidavit
2. Public Entity Crimes Form
3. City of Key West Indemnification Form
4. Equal Benefits for Domestic Partners Affidavit
5. Cone of Silence
6. Local Vendor Certification
7. Non-Collusion Affidavit
8. Proof of Required Insurance

E. CITY OF KEY WEST LICENSE REQUIRED

Contractor is required to have a Certified or Registered General Contractors City of Key West license. License fees not to exceed \$410.00. License shall be obtained within ten (10) days of Notice of Award.

7. STATE AND LOCAL SALES AND USE TAXES

Unless the Supplementary Conditions contains a statement that the CITY is exempt from state sales tax on materials incorporated into the work due to the qualification of the work under this Contract, all state and local sales and use taxes as required by the laws and statutes of the state and its political subdivisions shall be paid by the Contractor. Prices quoted in the Bid shall include all nonexempt sales and use taxes, unless provision is made in the Bid form to separately itemize the tax.

8. SUBMISSION OF BID

All BIDS must be submitted no later than the time prescribed, at the place, and in the manner set forth in the Invitation to Bid. Bids must be made on the Bid forms provided herewith **submit one (1) ORIGINAL bid package and two (2) FLASH DRIVES containing a single PDF file of the entire bid package.**

Each Bid must be submitted in a sealed envelope, so marked as to indicate the Bidder's name and its contents without being opened, and addressed in conformance with the instructions in the Invitation to Bid.

9. MODIFICATION OR WITHDRAWAL OF BID

Prior to the time and date designated for receipt of Bids, any Bid submitted may be withdrawn by notice to the party receiving Bids at the place designated for receipt of Bids. Such notice shall be in writing over the signature of the Bidder or by telegram. If by telegram, written confirmation over the signature of the Bidder shall be mailed and postmarked on or before the date and time set for receipt of Bids. No Bid may be withdrawn after the time scheduled for opening of Bids unless the time specified in paragraph AWARD OF CONTRACT of these Instructions to Bidders shall have elapsed.

10. BID SECURITY

BIDS must be accompanied by cash, a certified check, or cashier's check drawn on a bank in good standing, or a bid bond issued by a Surety authorized to issue such bonds in the state where the work is located, in the amount of five (5) percent of the total amount of the Proposal submitted. This bid security shall be given as a guarantee that the Bidder will not withdraw his BID for a period of ninety (90) days after bid opening, and that if awarded the Contract, the successful Bidder will execute the attached Contract and furnish properly executed Performance and Payment Bonds, each in the full amount of the Contract price within the time specified. Agent and Surety phone numbers must be provided.

The Attorney-in-Fact who executes this bond in behalf of the Surety must attach a notarized copy of his power-of-attorney as evidence of his authority to bind the Surety on the date of execution of the bond. Where State Statute requires, certification by a resident agent shall also be provided.

If the Bidder elects to furnish a Bid Bond, he shall use the Bid Bond form bound herewith, or one conforming substantially thereto in form and content.

11. RETURN OF BID SECURITY

Within 15 days after the award of the Contract, the CITY will return the bid securities to all Bidders whose BIDS are not to be further considered in awarding the Contract. Retained bid securities will be held until the Contract has been finally executed, after which all bid securities, other than Bidders' bonds and any guarantees, which have been forfeited, will be returned to the respective Bidders whose Proposals they accompanied.

12. AWARD OF CONTRACT

The Award will be made under one Contract by the Owner on the basis of the Bid from the lowest, responsive, responsible Bidder. The Owner may award entire Bid or selected line items based on the CRA's best interest and available funds a time of Award.

Within 90 calendar days after the opening of Bids, the Owner will accept one of the Bids or will act in accordance with the following paragraphs. The acceptance of the Bid will be by written notice of award, mailed to the office designated in the Bid, or delivered to the Bidder's representative. In the event of failure of the lowest responsive, responsible Bidder to sign the Contract and provide an acceptable Performance Bond, Payment Bond, insurance certificate(s) and evidence of holding required licenses and certificates, the Owner may award the Contract to the next lowest responsive, responsible Bidder. Such award, if made, will be made within 120 days after the opening of Bids. Bidders will guarantee their Bid price(s) for up to 120 calendar days after Bid opening.

The CRA reserves the right to accept or reject any or all Bids and to waive any formalities and irregularities in said Bids.

13. BASIS OF AWARD

The award will be made by the Owner on the basis of the BID from the lowest, responsive, responsible BIDDER which, in the Owner's sole and absolute judgment will best serve the interest of the Owner.

14. EXECUTION OF CONTRACT

The successful Bidder shall, within 10 working days after receiving Notice of Award, sign and deliver to the Owner a Contract in the form hereto attached together with the insurance certificate examples of the bonds as required in the Contract Documents and evidence of holding required licenses and certificates. Within 10 working days after receiving the signed Contract from the successful Bidder, the Owner's authorized agent will sign the Contract. Signature by both parties constitutes execution of the Contract.

15. CONTRACT BONDS

A. PERFORMANCE AND PAYMENT BONDS

The successful Bidder shall file with the CITY, at the time of delivery of the signed Contract, a Performance Bond and Payment Bond on the form bound herewith, each

in the full amount of the Contract price in accordance with the requirements of Florida Statutes Section 255.05 or 713.23, as applicable, as security for the faithful performance of the Contract and the payment of all persons supplying labor and materials for the construction of the work, and to cover all guarantees against defective workmanship or materials, or both, during the warranty period following the date of final acceptance of the work by the CITY. The Surety furnishing this bond shall have a sound financial standing and a record of service satisfactory to the CITY, shall be authorized to do business in the State of Florida, and shall be listed on the current U.S. Department of Treasury Circular Number 570, or amendments thereto in the Federal Register, of acceptable Sureties for federal projects. The CONTRACTOR shall supply the OWNER with phone numbers, addresses, and contacts for the Surety and their agents. Pursuant to Section 255.05(7), Florida Statutes, in lieu of the bond required by law, the contractor may file with the city an alternative form of security in the form of cash, a money order, a certified check, a cashier's check or an irrevocable letter of credit.

C. POWER-OF-ATTORNEY

The Attorney-in-Fact (Resident Agent) who executes this Performance and Payment Bond in behalf of the Surety must attach a notarized copy of his power-of-attorney as evidence of his authority to bind the Surety on the date of execution of the bond. All Contracts, Performance and Payment Bonds, and respective powers-of-attorney will have the same date.

16. FAILURE TO EXECUTE CONTRACT AND FURNISH BOND

The Bidder who has a Contract awarded to him and who fails to promptly and properly execute the Contract or furnish the required Bonds shall forfeit the bid security that accompanied his bid, and the bid security shall be retained as liquidated damages by the CITY, and it is agreed that this said sum is a fair estimate of the amount of damages the CITY will sustain in case the Bidder fails to enter into a Contract or furnish the required Bonds. Bid security deposited in the form of cash, a certified check, or cashier's check shall be subject to the same requirement as a Bid Bond.

17. TIME OF COMPLETION

The time of completion of the work to be performed under this Contract is the essence of the Contract. Delays and extensions of time may only be allowed in accordance with the provisions stated in the General Conditions. Time allowed for completion of the work authorized is stated in Bid.

When the Contractor receives a Notice to Proceed, he shall commence work as soon as possible and shall complete all work within the number of calendar days stipulated in the Contract.

The term of this contract will be seventy (70) calendar days.

Contractor shall not work the week of Fantasy Fest, October 19 – 28, 2018.

18. PUBLIC RECORDS REQUIREMENTS

In addition to other contract requirements provided by law, each public agency contract for services must include a provision that requires the contractor to comply with public records laws, specifically to (a) keep and maintain public records that ordinarily and necessarily would be required by the public agency in order to perform the service; (b) provide the public with access to public records on the same terms and conditions that the public agency would provide the records and at a cost that does not exceed the cost provided in this chapter or as otherwise provided by law; (c) ensure that public records that are exempt or confidential and exempt from public records disclosure requirements are not disclosed except as authorized by law; and (d) meet all requirements for retaining public records and transfer, at no cost, to the public agency all public records in possession of the contractor upon termination of the contract and destroy any duplicate public records that exempt or confidential and exempt from public records disclosure requirements. All records stored electronically must be provided to the public agency in a format that is compatible with the information technology systems of the public agency. If a contractor does not comply with a public records request, the public agency shall enforce the contract provisions in accordance with the contract.

19. PERMITS AND FEES

The Bidder awarded this project shall procure and pay all permits and licenses, charges, and fees, and give notices necessary and incidental to the due and lawful prosecution of the work, the cost of which shall be included in the fee received for the work, except where separately agreed.

20. BIDDER'S DECLARATION AND UNDERSTANDING

The undersigned, hereinafter called the Bidder, declares that the only persons or parties interested in this Bid are those named herein, that this Bid is, in all respects, fair and without fraud, that it is made without collusion with any official of the Owner, and that the Bid is made without any connection or collusion with any person submitting another Bid on this Contract.

The Bidder further declares that he has carefully examined the Contract Documents and that this Bid is made according to the provisions and under the terms of the Contract Documents, which Documents are hereby made a part of this Bid.

21. SALES AND USE TAXES

The Bidder agrees that all federal, state, and local sales and use taxes are included in the stated unit prices for the work.

* * * * *

BID FORM

To: City of Key West, Florida

Address: 1300 White Street, Key West, Florida 33040

Project Title: **DOCK REPAIR & PILING REPLACEMENT, D-DOCK
KEY WEST HISTORIC SEAPORT**

Project No.: ITB #18-005

Bidder's person to contact for additional information on this Bid:

Company Name: _____

Contact Name & Telephone #: _____

Email Address: _____

BIDDER'S DECLARATION AND UNDERSTANDING

The undersigned, hereinafter called the Bidder, declares that the only persons or parties interested in this Bid are those named herein, that this Bid is, in all respects, fair and without fraud, that it is made without collusion with any official of the Owner, and that the Bid is made without any connection or collusion with any person submitting another Bid on this Contract.

The Bidder further declares that he has carefully examined the Contract Documents, that he has personally inspected the Project, that he has satisfied himself as to the quantities involved, including materials and equipment, and conditions of work involved, including the fact that the description of the quantities of work and materials, as included herein, is brief and is intended only to indicate the general nature of the work and to identify the said quantities with the detailed requirements of the Contract Documents, and that this Bid is made according to the provisions and under the terms of the Contract Documents, which Documents are hereby made a part of this Proposal.

The Bidder further agrees that the Owner may “non-perform” the work in the event that the low bid is in excess of available funding. Non-performance will be determined prior to Notice of Award.

The intent of the Bid Documents is to describe a functionally complete project (or part thereof) to be constructed in accordance with the Contract Documents. Any work, materials, or equipment that may reasonably be inferred from the Contract Documents, as being required to produce the intended result shall be supplied, whether or not specifically called for in the Contract Documents.

CONTRACT EXECUTION

The Bidder agrees that if this Bid is accepted, he will, within 10 days, not including Sundays and legal holidays, after Notice of Award, sign the Contract in the form annexed hereto, and will at that time, deliver evidence of holding required licenses and certificates, and will, to the extent of his Bid,

furnish all machinery, tools, apparatus, and other means of construction and do the work and furnish all the materials necessary to complete all work as specified or indicated in the Contract Documents.

CERTIFICATES OF INSURANCE

Bidder agrees to furnish the Owner, before commencing the work under this Contract, the certificates of insurance as specified in these Documents.

Type of Insurance	Limits	Comments
Commercial General Liability	\$1,000,000	The proposers may have these coverages combined in 1 policy
Watercraft Liability	\$1,000,000	
Business Automobile Liability	\$1,000,000	
Workers' Compensation	Statutory	
Employers Liability	\$1,000,000/\$1,000,000/\$1,000,000	
USL&H and Jones Act Coverage	\$1,000,000	

START OF CONSTRUCTION AND CONTRACT COMPLETION TIME

The Bidder agrees to begin work within fourteen (14) calendar days after the date of the Notice to Proceed and to fully complete all work under this contract within seventy (70) calendar days, including construction of the foundation and assembly of the structure.

LIQUIDATED DAMAGES

In the event the Bidder is awarded the Contract and fails to complete the work within the time limit or extended time limit agreed upon, as more particularly set forth in the Contract Documents, liquidated damages shall be paid to the Owner at the rate of **\$500.00** per day for all work awarded until the work has been satisfactorily completed as provided by the Contract Documents. Sundays and legal holidays shall be excluded in determining days in default.

Owner will recover such liquidated damages by deducting the amount owed from the final payment or any retainage held by Owner.

ADDENDA

The Bidder hereby acknowledges that he has received Addenda No's. _____, _____, _____, _____ (Bidder shall insert No. of each Addendum received) and agrees that all addenda issued are hereby made part of the Contract Documents, and the Bidder further agrees that his Bid(s) includes all impacts resulting from said addenda.

SALES AND USE TAXES

The Bidder agrees that all federal, state, and local sales and use taxes are included in the stated bid prices for the work.

UNIT PRICE WORK ITEMS

The Bidder further proposes to accept as full payment for the Work proposed herein the amounts computed under the provisions of the Contract Documents and based on the following unit price amounts.

The Bidder agrees that the unit price represent a true measure of labor and materials required to perform the Work, including all allowances for overhead and profit for each type of work called for in these Contract Documents. The amounts shall be shown in both words and figures. In case of discrepancy, the amount shown in words shall govern.

* * * * *

BID SCHEDULE

DOCK REPAIR & PILING REPLACEMENT KEY WEST HISTORIC SEAPORT

UNIT PRICE BID

Bid unit prices stated in this proposal include all costs and expenses for labor, equipment, materials, disposal and contractor's overhead and profit. Unit prices for the various work items are intended to establish a total price for completing the project in its entirety. All work and incidental costs shall be included for payment under the several scheduled items of the overall contract, and no separate payment will be made therefore.

1. Mobilization, General/Supp Conditions and Demobilization

- | | | | | | |
|----|--------------------------------------|---|------|----------|----------|
| a. | Mobilization | 1 | each | \$ _____ | |
| b. | General/Supp. Conditions | 1 | each | \$ _____ | |
| c. | Demobilization | 1 | each | \$ _____ | |
| | 1 LS (10% of Construction Cost Max.) | | | | \$ _____ |

2. Payment and Performance Bonds

	1 LS		\$ _____	
--	------	--	----------	--

3. Permit Fees (to be paid at cost)

	1 LS		\$ <u>15,000.00</u>	
--	------	--	----------------------------	--

4. 14" dia. x 35' Piles (includes all labor, equipment, disposal and material)

Dock Pile	55	EA	Unit Price \$ _____	Sub-total \$ _____	
-----------	----	----	---------------------	--------------------	--

Fender/Mooring Pile	3	EA	Unit Price \$ _____	Sub-total \$ _____	
---------------------	---	----	---------------------	--------------------	--

TOTAL \$ _____

5. 3x8 Horizontal Timbers (includes all labor, equipment, disposal and material)

11'L	2	EA	Unit Price \$ _____	TOTAL \$ _____	
------	---	----	---------------------	----------------	--

6. 3x8 Diagonal Timbers (includes all labor, equipment, disposal and material)

13'L	6	EA	Unit Price \$ _____	TOTAL \$ _____	
------	---	----	---------------------	----------------	--

7. 26" x 1/2" dia. SS All-Thread Hardware Assembly w/ 2x Nuts and Washers (includes all labor, equipment, disposal and material)

79 EA Unit Price \$ _____ TOTAL \$ _____

8. 8" x 1/2" dia. SS Epoxy Anchor Bolts (includes all labor, equipment, disposal and material)

4 EA Unit Price \$ _____ TOTAL \$ _____

9. Conical PVC/HDPE Pile Caps (includes all labor, equipment, disposal and material)

20 EA Unit Price \$ _____ TOTAL \$ _____

10. Remove and Re-install Utility Pedestal (includes all labor, equipment and material)

3 EA Unit Price \$ _____ TOTAL \$ _____

11. Remove and Re-install Electrical Transformer (includes all labor, equipment and material)

1 EA Unit Price \$ _____ TOTAL \$ _____

12. General Allowance (only to be used with Owner's written approval)

1 LS \$ 25,000.00

TOTAL OF ALL EXTENDED LINE ITEMS LISTED ABOVE:

Total of lump sum items 1 - 12 \$ _____

_____ Dollars & _____ Cents
(amount written in words)

NOTE: THE TOTAL BID WILL BE THE BASIS OF EVALUATING LOW BIDDER AND BASIS OF AWARD

SUBCONTRACTORS

The Bidder further proposes that the following subcontracting firms or businesses will be awarded subcontracts for the following portions of the work in the event that the Bidder is awarded the Contract:

Portion of Work

Name

Street City State Zip

Portion of Work

Name

Street City State Zip

Portion of Work

Name

Street City State Zip

Portion of Work

Name

Street City State Zip

SURETY

_____ whose address is

Street, City, State Zip

Phone Resident Agent

BIDDER

The name of the Bidder submitting this Bid is _____
_____ doing business
at

Street, City, State Zip

_____ email address

which is the address to which all communications concerned with this Bid and with the Contract shall be sent.

The names of the principal officers of the corporation submitting this Bid, or of the partnership, or of all persons interested in this Bid as principals are as follows:

Name	Title
_____	_____
_____	_____
_____	_____
_____	_____

If Sole Proprietor or Partnership

IN WITNESS hereto the undersigned has set his (its) hand this _____ day of _____ 20____.

Signature of Bidder

Title

If Corporation

IN WITNESS WHEREOF the undersigned corporation has caused this instrument to be executed and its seal affixed by its duly authorized officers this _____ day of _____ 20____.

(SEAL)

Name of Corporation

By _____

Title _____

Attest _____
Secretary

FLORIDA BID BOND

BOND NO. _____

AMOUNT: \$ _____

KNOW ALL MEN BY THESE PRESENTS, that _____

_____ hereinafter called the PRINCIPAL, and _____

_____ a corporation duly organized under the laws of the State of _____

having its principal place of business at _____

_____ in the State of _____,

and authorized to do business in the State of Florida, as SURETY, are held and firmly bound unto

_____ hereinafter CITY OF KEY WEST called the OBLIGEE, in the sum of _____

_____ DOLLARS (\$ _____) for

the payment for which we bind ourselves, our heirs, executors, administrators, successors, and assigns, jointly and severally, firmly by these present.

THE CONDITION OF THIS BOND IS SUCH THAT:

WHEREAS, the PRINCIPAL is herewith submitting his or its Bid Proposal for **Dock Repair & Piling Replacement, D-Dock – Key West Historic Seaport**, said Bid Proposal, by reference thereto, being hereby made a part hereof.

WHEREAS, the PRINCIPAL contemplates submitting or has submitted a bid to the OBLIGEE for the furnishing of all labor, materials (except those to be specifically furnished by the CITY), equipment, machinery, tools, apparatus, means of transportation for, and the performance of the work covered in the Proposal and the detailed Specifications, entitled:

ITB #18-005

DOCK REPAIR & PILING REPLACEMENT

D - DOCK

KEY WEST HISTORIC SEAPORT

WHEREAS, it was a condition precedent to the submission of said bid that a cashier's check, certified check, or bid bond in the amount of 5 percent of the base bid be submitted with said bid as a guarantee that the Bidder would, if awarded the Contract, enter into a written Contract with the CITY for the performance of said Contract, within 10 working days after written notice having been given of the award of the Contract.

NOW, THEREFORE, the conditions of this obligation are such that if the PRINCIPAL within 10 consecutive calendar days after written notice of such acceptance, enters into a written Contract with the OBLIGEE and furnishes the Performance and Payment Bonds, each in an amount equal to 100 percent of the base bid, satisfactory to the CITY, then this obligation shall be void; otherwise the sum herein stated shall be due and payable to the OBLIGEE and the Surety herein agrees to pay said sum immediately upon demand of the OBLIGEE in good and lawful money of the United States of America, as liquidated damages for failure thereof of said PRINCIPAL.

Signed and sealed this _____ day of _____, 2018.

By _____
PRINCIPAL

SURETY

By _____
Attorney-In-Fact

ANTI-KICKBACK AFFIDAVIT

STATE OF _____)

: SS

COUNTY OF _____)

I, the undersigned hereby duly sworn, depose and say that no portion of the sum herein bid will be paid to any employees of the City of Key West as a commission, kickback, reward or gift, directly or indirectly by me or any member of my firm or by an officer of the corporation.

By: _____

Sworn and subscribed before me this _____ day of _____ 20__.

NOTARY PUBLIC, State of Florida at Large

My Commission Expires:

* * * * *

**SWORN STATEMENT UNDER SECTION 287.133(3)(A)
FLORIDA STATUTES, ON PUBLIC ENTITY CRIMES**

THIS FORM MUST BE SIGNED IN THE PRESENCE OF A NOTARY PUBLIC OR OTHER OFFICER AUTHORIZED TO ADMINISTER OATHS.

1. This sworn statement is submitted with Bid or Proposal for _____

2. This sworn statement is submitted by _____
(name of entity submitting sworn statement)

whose business address is _____

and (if applicable) its Federal Employer Identification Number (FEIN) is _____

(If the entity has no FEIN, include the Social Security Number of the individual
signing this sworn statement _____

3. My name is _____
(please print name of individual signing)

and my relationship to the entity named above is _____

4. I understand that a “public entity crime” as defined in Paragraph 287.133(1)(g), Florida Statutes, means a violation of any state or federal law by a person with respect to and directly related to the transaction of business with any public entity or with an agency or political subdivision of any other state or with the United States, including but not limited to, any bid or contract for goods or services to be provided to any public or an agency or political subdivision of any other state or of the United States and involving antitrust, fraud, theft, bribery, collusion, racketeering, conspiracy, material misrepresentation.

5. I understand that “convicted” or “conviction” as defined in Paragraph 287.133(1)(b), Florida Statutes, means a finding of guilt or a conviction of a public entity crime, with or without an adjudication of guilt, in any federal or state trial court of record relating to charges brought by indictment information after July 1, 1989, as a result of a jury verdict, nonjury trial, or entry of a plea of guilty or nolo contendere.

6. I understand that an “affiliate” as defined in Paragraph 287.133(1)(a), Florida Statutes, means

1. A predecessor or successor of a person convicted of a public entity crime; or
2. An entity under the control of any natural person who is active in the management of the entity and who has been convicted of a public entity crime. The term “affiliate” includes those officers, directors, executives, partners, shareholders, employees, members, and agents who are active in the management of an affiliate. The ownership by one person of shares constituting controlling interest in another person, or a pooling of equipment or income among persons when not for fair market value under an arm’s length agreement, shall be a prima facie case that one person controls another person. A person who knowingly enters into a joint venture with a person who has been convicted of a public entity crime in Florida during the preceding 36 months shall be considered an affiliate.

7. I understand that a “person” as defined in Paragraph 287.133(1)(8), Florida Statutes, means any natural person or entity organized under the laws of any state or of the United States with the legal power to enter into a binding contract and which bids or applies to bid on contracts for the provision of goods or services let by a public entity, or which otherwise transacts or applies to transact business with public entity. The term “person” includes those officers, directors, executives, partners, shareholders, employees, members, and agents who are active in management of an entity.
8. Based on information and belief, the statement which I have marked below is true in relation to the entity submitting this sworn statement. (Please indicate which statement applies).

_____ Neither the entity submitting this sworn statement, nor any officers, directors, executives, partners, shareholders, employees, members, or agents who are active in management of the entity, nor any affiliate of the entity have been charged with and convicted of a public entity crime subsequent to July 1, 1989, AND (Please indicate which additional statement applies.)

_____ There has been a proceeding concerning the conviction before a hearing of the State of Florida, Division of Administrative Hearings. The final order entered by the hearing officer did not place the person or affiliate on the convicted vendor list. (Please attach a copy of the final order.)

_____ The person or affiliate was placed on the convicted vendor list. There has been a subsequent proceeding before a hearing officer of the State of Florida, Division of Administrative Hearings. The final order entered by the hearing officer determined that it was in the public interest to remove the person or affiliate from the convicted vendor list. (Please attach a copy of the final order.)

_____ The person or affiliate has not been put on the convicted vendor list. (Please describe any action taken by or pending with the Department of General Services.)

(signature)

(date)

STATE OF _____

COUNTY OF _____

PERSONALLY APPEARED BEFORE ME, the undersigned authority,

_____ Who, after first being sworn by me, affixed his/her
(name of individual signing)

signature in the space provided above on this _____ day of _____, 20__.

My commission expires:

NOTARY PUBLIC

CITY OF KEY WEST INDEMNIFICATION FORM

To the fullest extent permitted by law, the CONTRACTOR expressly agrees to indemnify and hold harmless the City of Key West, their officers, directors, agents and employees *(herein called the "indemnitees") from liabilities, damages, losses and costs, including but not limited to, reasonable attorney's fees and court costs, such legal expenses to include costs incurred in establishing the indemnification and other rights agreed to in this Paragraph, to persons or property, to the extent caused by the negligence, recklessness, or intentional wrongful misconduct of the CONTRACTOR, its Subcontractors or persons employed or utilized by them in the performance of the Contract. Claims by indemnitees for indemnification shall be limited to the amount of CONTRACTOR's insurance or \$1 million per occurrence, whichever is greater. The parties acknowledge that the amount of the indemnity required hereunder bears a reasonable commercial relationship to the Contract and it is part of the project specifications or the bid documents, if any.

The indemnification obligations under the Contract shall not be restricted in any way by any limitation on the amount or type of damages, compensation, or benefits payable by or for the CONTRACTOR under Workers' Compensation acts, disability benefits acts, or other employee benefits acts, and shall extend to and include any actions brought by or in the name of any employee of the CONTRACTOR or of any third party to whom CONTRACTOR may subcontract a part or all of the Work. This indemnification shall continue beyond the date of completion of the work.

CONTRACTOR: _____

SEAL:

Address

Signature

Print Name

Title

DATE: _____

EQUAL BENEFITS FOR DOMESTIC PARTNERS AFFIDAVIT

STATE OF _____)

: SS

COUNTY OF _____)

I, the undersigned hereby duly sworn, depose and say that the firm of _____

_____ provides benefits to domestic partners of its employees on the same basis as it provides benefits to employees' spouses, per City of Key West Code of Ordinances Sec. 2-799.

By: _____

Sworn and subscribed before me this _____ day of _____ 20 ____.

NOTARY PUBLIC, State of Florida at Large

My Commission Expires:

* * * * *

CONE OF SILENCE AFFIDAVIT

STATE OF _____)

: SS

COUNTY OF _____)

I, the undersigned hereby duly sworn, depose and say that all owner(s), partners, officers, directors, employees and agents representing the firm of _____ have read and understand the limitations and procedures regarding communications concerning City of Key West Code of Ordinances Sec. 2-773 Cone of Silence.

By: _____

Sworn and subscribed before me this

_____ day of _____ 20_____.

NOTARY PUBLIC, State of _____ at Large

My Commission Expires: _____

**LOCAL VENDOR CERTIFICATION
PURSUANT TO CITY OF KEY WEST CODE OF ORDINANCES SECTION 2-798**

The undersigned, as a duly authorized representative of the vendor listed herein, certifies to the best of his/her knowledge and belief, that the vendor meets the definition of a "Local Business." For purposes of this section, "local business" shall mean a business which:

- a. Principle address as registered with the FL Department of State located within 30 miles of the boundaries of the city, listed with the chief licensing official as having a business tax receipt with its principle address within 30 miles of the boundaries of the city for at least one year immediately prior to the issuance of the solicitation.
- b. Maintains a workforce of at least 50 percent of its employees from the city or within 30 miles of its boundaries.
- c. Having paid all current license taxes and any other fees due the city at least 24 hours prior to the publication of the call for bids or request for proposals.
 - Not a local vendor pursuant to Code of Ordinances Section 2-798
 - Qualifies as a local vendor pursuant to Code of Ordinances Section 2-798

If you qualify, please complete the following in support of the self-certification & submit copies of your County and City business licenses. Failure to provide the information requested will result in denial of certification as a local business.

Business Name _____ Phone: _____
 Current Local Address: _____ Fax: _____
 (P.O Box numbers may not be used to establish status)
 Length of time at this address _____

 Signature of Authorized Representative _____ Date _____

STATE OF _____
 COUNTY OF _____

The foregoing instrument was acknowledged before me this _____ day of _____, 20__.
 By _____, of _____
 (Name of officer or agent, title of officer or agent) Name of corporation acknowledging)
 or has produced _____ as identification
 (type of identification)

 Signature of Notary

 Print, Type or Stamp Name of Notary

 Title or Rank

Return Completed form with
 Supporting documents to:
 City of Key West Purchasing

BIDDER'S CHECKLIST

(Note: The purpose of this checklist is to serve as a reminder of major items to be addressed in submitting a bid and is not intended to be all inclusive. It does not alleviate the Bidder from the responsibility of becoming familiar with all aspects of the Contract Documents and Proper completion and submission of his bid.)

1. All Contract Documents thoroughly read and understood
2. All blank spaces in Bid filled in black ink.
3. Total and unit Prices added correctly.
4. Addenda acknowledged.
5. Subcontractors are named as indicated in the Bid.
6. Experience record included.
7. Bid signed by authorized officer.
8. Bid Bond completed and executed, including power-of-attorney, dated the same date as Bid Bond.
9. Bidder familiar with federal, state, and local laws, ordinances, rules and regulations affecting performance of the work.
10. Bidder, if successful, able to obtain and/or demonstrate possession of required licenses and certificates within (10) ten days after receiving a Notice of Award.
11. Bid submitted intact with the volume containing the Bidding Requirements, Contract Forms and Conditions of the Contract, one (1) original, two (2) USB drives.
12. Bid Documents submitted in sealed envelope and addressed and labeled in conformance with the instructions in the Invitation to Bid.
13. Anti-kickback Affidavit; Public Entity Crime Form; City of Key West Indemnification
Equal Benefits for Domestic Partners Affidavit; Local Vendor Certification;
Non-Collusion Affidavit; Proof of Required Insurance

* * * * *

PART 2

CONTRACT FORMS

CONTRACT AGREEMENT

This Contract, made and entered into _____ day of _____, 20____, by and between the City of Key West, hereinafter called the "Owner", and _____, hereinafter called the "Contractor";

WITNESSETH:

The Contractor, in consideration of the sum to be paid him by the Owner and of the covenants and agreements herein contained, hereby agrees at his own proper cost and expense to do all the work and furnish all the materials, tools, labor, and all appliances, machinery, and appurtenances for **ITB #18-005 DOCK REPAIR & PILING REPLACEMENT, D-DOCK – KEY WEST HISTORIC SEAPORT**

Key West, Florida to the extent of the Bid made by the Contractor, dated the _____ day of _____, 20____, all in full compliance with the Contract Documents referred to herein.

The PROCUREMENT REQUIREMENTS, including the signed copy of the BID FORM, the CONTRACT FORMS, the CONDITIONS OF THE CONTRACT, and the SPECIFICATIONS, DRAWINGS and/or SUPPLEMENTAL INFORMATION (if any), are hereby referred to and by reference made part of this Contract as fully and completely as if the same were fully set forth herein and are mutually cooperative therewith.

In consideration of the performance of the work as set forth in these Contract Documents, the Owner agrees to pay to the Contractor the amount bid in the Bid as adjusted in accordance with the Contract Documents, or as otherwise herein provided, and to make such payments in the manner and at the times provided in the Contract Documents.

The Contractor agrees to complete the work within one seventy (70) calendar days and to accept as full payment hereunder the amounts computed as determined by the Contract Documents and based on the said Bid.

The Contractor agrees to remedy all defects appearing in the work or developing in the materials furnished and the workmanship performed under this Contract during the warranty period after the date of final acceptance of the work by the Owner, and further agrees to indemnify and save the Owner harmless from any costs encountered in remedying such defects.

Liquidated Damages: The Contractor recognizes that time is of the essence and that the Owner will suffer financial loss if the Work is not completed within the dates specified in the paragraphs above, plus any extensions thereof allowed, in accordance with Article 58 of the General Conditions.

In the event the Contractor fails to complete the work within the time limit or extended time limit agreed upon, as more particularly set forth in the Contract Documents, liquidated damages shall be paid at a rate of **\$500.00** per day. Sundays and legal holidays shall be included in determining days in default.

This contract will automatically expire upon completion of the project. Contractors warranty obligations remain in affect.

IN WITNESS WHEREOF, we, the parties hereto, each herewith subscribe the same this

_____ day of _____, A.D., 20_____.

CITY OF KEY WEST

By _____

Printed _____

Title _____

CONTRACTOR

By _____

Printed _____

Title _____

APPROVED AS TO FORM

Attorney for Owner

* * * * *

FLORIDA PERFORMANCE BOND

BOND NO. _____

AMOUNT: \$ _____

KNOW ALL MEN BY THESE PRESENTS, that in accordance with Florida Statutes Section 255.05 _____

with offices at _____

hereinafter called the CONTRACTOR (Principal), and

_____ with offices at _____

a corporation duly organized and existing under and by virtue of the laws of the State of Florida, hereinafter called the SURETY, and authorized to transact business within the State of Florida, as SURETY, are held and firmly bound unto the **CITY OF KEY WEST**, hereinafter called the CITY (Obligee), in the sum of:

_____ DOLLARS (\$ _____), lawful money of the United States of America, for the payment of which, well and truly be made to the CITY, the CONTRACTOR and the SURETY bind themselves and each of their heirs, executors, administrators, successors, and assigns, jointly and severally, firmly by these presents as follows:

THE CONDITION OF THE ABOVE OBLIGATION IS SUCH THAT:

WHEREAS, the CONTRACTOR has executed and entered into a certain Contract hereto attached, with the CITY, dated _____, 20__, to furnish at his own cost, charges, and expense all the necessary materials, equipment, and/or labor in strict and express accordance with said Contract and the Contract Documents as defined therein, all of which is made a part of said Contract by certain terms and conditions in said Contract more particularly mentioned, which Contract, consisting of the various Contract Documents is made a part of this Bond as fully and completely as if said Contract Documents were set forth herein;

NOW THEREFORE, the conditions of this obligation are such that if the above bounden CONTRACTOR:

1. Shall in all respects comply with the terms and conditions of said Contract and his obligation there under, including the Contract Documents (which include the scope of work and conditions as prepared by the CITY, invitation to bid, instructions to bidders, the CONTRACTOR'S bid as accepted by the above CITY, the bid and contract performance and payment bonds (Not required

as part of this contract), and all addenda, if any, issued prior to the opening of bids), being made a part of this bond by reference, at the times and in the manner prescribed in the contract; and

2. Promptly makes payments to all claimants, as defined in Section 255.05(1), Florida Statutes, supplying PRINCIPAL with labor, materials, or supplies, used directly or indirectly by PRINCIPAL in the prosecution of the work provided for in the contract; and

3. Pays CITY all losses, costs, expenses, damages, attorney's fees, including appellate proceedings, injury or loss of whatever kind and however arising including, without limitation, delay damages to which said CITY may be subject by reason of any wrongdoing, misconduct, want of care or skill, negligence, failure of performance, breach, failure to petition within the prescribed time, or default, including patent infringements, on the part of said CONTRACTOR, his agents or employees, in the execution or performance of said Contract; and

4. Performs the guarantee of all work and materials furnished under the contract for the time specified in the contract, then this obligation shall be void; otherwise, to remain in full force and effect for the term of said Contract.

AND, the said Surety for value received, hereby stipulates and agrees that no change involving any extension of time, or addition to the terms of the Contract Documents, or to the work to be performed, or materials to be furnished there under shall affect said obligation of said Surety on this Bond, and the said Surety does hereby waive notice of any such changes, extension of time, alterations, or additions of the terms of the Contract Documents, or to the work.

Any action instituted by a claimant under this bond for payment must be in accordance with the notice and time limitation provisions in Section 255.05(2), Florida Statutes.

IN WITNESS WHEREOF, the above parties bonded together have executed this instrument

this _____ day of _____, 20__ , the name and corporate seal of each corporate party being hereto affixed and those presents duly signed by its undersigned representative, pursuant to authority of its governing body.

CONTRACTOR

By: _____

(SEAL)

ATTEST

SURETY

By: _____

(SEAL)

ATTEST

FLORIDA PAYMENT BOND

BOND NO. _____

AMOUNT: \$ _____

KNOW ALL MEN BY THESE PRESENTS, that in accordance with Florida Statutes Section 255.05, _____

with offices at _____
hereinafter called the CONTRACTOR, (Principal), and

with offices at _____
a corporation duly organized and existing under and by virtue of the laws of the State of _____

_____, hereinafter called the SURETY, and authorized to transact business within the State of Florida, as SURETY, are held and firmly bound unto CITY OF KEY WEST, hereinafter called the City (Obligee), in the sum of:

_____ DOLLARS(_____),
lawful money of the United States of America, for the payment of which, well and truly be made to the CITY, and the CONTRACTOR and the SURETY bind themselves and each of their heirs, executors, administrators, successors, and assigns, jointly and severally, firmly by these presents as follows:

THE CONDITION OF THE ABOVE OBLIGATION IS SUCH THAT:

WHEREAS, the CONTRACTOR has executed and entered into a certain Contract for

ITB #18-005 DOCK REPAIR & PILING REPLACEMENT, D-DOCK – KEY WEST HISTORIC SEAPORT attached hereto, with

the CITY, dated _____

_____, 20___, to furnish at his own cost, charges, and expense the necessary materials, equipment, and/or labor in strict and express accordance with said Contract and the plans, drawings (if any), and specifications prepared by the CITY, all of which is made a part of said Contract by certain terms and conditions in said Contract more particularly mentioned, which Contract, consisting of the various Contract Documents specifically mentioned herein and relative hereto, is made a part of this Bond as fully and completely as if said Contract Documents were set forth herein.

NOW THEREFORE, the conditions of this obligation are such that if the above bounden CONTRACTOR shall in all respects comply with the terms and conditions of said Contract and his obligation thereunder, including the Contract Documents, which include Scope of work and conditions prepared by the CITY, invitation to bid, instructions to bidders, the

CONTRACTOR'S bid as accepted by the CITY, the bid and contract and payment bonds (Not required as part of this contract), and all addenda, if any, issued prior to the opening of bids), and further that if said CONTRACTOR shall promptly make payments to all persons supplying materials, equipment, and/or labor, used directly or indirectly by said CONTRACTOR or subcontractors in the prosecution of the work for said contract in accordance with Florida Statutes, Section 255.05 or Section 713.23, then this obligation shall be void; otherwise to remain in full force and effect for the term of said contract, including and all guarantee periods as specifically mentioned in said Contract Documents.

AND, the said SURETY for value received, hereby stipulates and agrees that no change involving any extension of time, or addition to the terms of the Contract or to the work to be performed, or materials to be furnished thereunder, or in the Contract Documents and specifications accompanying the said contract shall affect said obligation of said SURETY on this Bond, and the said SURETY does hereby waive notice of any such changes, extension of time, alternations, or additions of the terms of the Contract, or to the work, to the Contract Documents, or to the specifications.

Claimant shall give written notice to the CONTRACTOR and the SURETY as required by Section 255.05 or Section 713.23, Florida Statutes. Any action instituted against the CONTRACTOR or SURETY under this bond for payment must be in accordance with the notice and time limitation provisions in Section 255.05(2) or Section 713.23, Florida Statutes.

IN WITNESS WHEREOF, the above parties bounded together have executed this instrument

this _____ day of _____, 20__, the name and corporate seal of each corporate party being hereto affixed and those presents duly signed by its undersigned representative, pursuant to authority of its governing body.

CONTRACTOR

By: _____

(SEAL)

ATTEST

SURETY

By: _____

(SEAL)

ATTEST

LICENSE REQUIREMENT AND COST

License required for this Project. Contractor must be general contractor or building contractor.

Cost Not To Exceed \$410.00.

CITY OF KEY WEST BUSINESS LICENSE TAX RECEIPT

A City of Key West Business License Tax Receipt is required for this project. Contractor must be general contractor, building contractor or engineering contractor. Cost not to exceed \$410.00.

City of Key West Business License Tax Receipt may be found on the city website.

<http://www.keywestcity.com/egov/docs/1162843921181.htm>

PART 3

CONDITIONS OF CONTRACT

GENERAL CONDITIONS

Article

DEFINITIONS

1. AS APPROVED
2. AS SHOWN, AND AS INDICATED
3. BIDDER
4. CONTRACT DOCUMENTS
5. CONTRACTOR
6. CONTRACT COMPLETION
7. DAYS
8. DRAWINGS
9. ENGINEER
10. NOTICE
11. OR EQUAL
12. OWNER
13. PLANS
14. SPECIFICATIONS
15. NOTICE TO PROCEED
16. SUBSTANTIAL COMPLETION
17. WORK

CONTRACT DOCUMENTS

18. INTENT OF CONTRACT DOCUMENTS
19. DISCREPANCIES AND OMISSIONS
20. CHANGES IN THE WORK
21. EXAMINATION AND VERIFICATION OF CONTRACT DOCUMENTS
22. DOCUMENTS TO BE KEPT ON THE JOBSITE
23. ADDITIONAL CONTRACT DOCUMENTS
24. OWNERSHIP OF CONTRACT DOCUMENTS

THE ENGINEER

25. AUTHORITY OF THE ENGINEER
26. DUTIES AND RESPONSIBILITIES OF THE ENGINEER
27. LIMITATIONS ON ENGINEER'S RESPONSIBILITIES
28. REJECTED WORK
29. LINES AND GRADES
30. SUBMITTALS
31. DETAIL DRAWINGS AND INSTRUCTIONS

THE CONTRACTOR AND HIS EMPLOYEES

32. CONTRACTOR, AN INDEPENDENT AGENT
33. SUBCONTRACTING
34. INSURANCE AND LIABILITY
 - A. GENERAL
 - B. CONTRACTOR AND SUB-CONTRACTOR INSURANCE
 - C. COMPENSATION AND EMPLOYER'S LIABILITY INSURANCE
 - D. GENERAL LIABILITY INSURANCE (INCLUDING AUTOMOBILE)

- E. BUILDER'S RISK ALL RISK INSURANCE
- F. NO PERSONAL LIABILITY OF PUBLIC OFFICIALS

35. INDEMNITY
36. EXCLUSION OF CONTRACTOR CLAIMS
37. TAXES AND CHARGES
38. REQUIREMENTS OF STATE LAW FOR PUBLIC WORKS PROJECTS
39. CODES, ORDINANCES, PERMITS, AND LICENSES
40. SUPERINTENDENCE
41. RECEPTION OF ENGINEER'S COMMUNICATIONS
42. SAFETY
43. PROTECTION OF WORK AND PROPERTY
44. RESPONSIBILITY OF CONTRACTOR TO ACT IN AN EMERGENCY
45. MATERIALS AND APPLIANCES
46. CONTRACTOR'S AND MANUFACTURERS' COMPLIANCE WITH STATE SAFETY, OSHA, AND OTHER CODE REQUIREMENTS
47. SUBSTITUTION OF MATERIALS
48. TESTS, SAMPLES, AND OBSERVATIONS
49. ROYALTIES AND PATENT
50. CONTRACTOR'S RIGHT TO TERMINATE CONTRACT
51. CORRECTION OF DEFECTIVE WORK DURING WARRANTY PERIOD

PROGRESS OF THE WORK

52. BEGINNING OF THE WORK
53. SCHEDULES AND PROGRESS REPORTS
54. PROSECUTION OF THE WORK
55. OWNER'S RIGHT TO RETAIN IMPERFECT WORK
56. OWNER'S RIGHT TO DO WORK
57. OWNER'S RIGHT TO TRANSFER EMPLOYMENT
58. DELAYS AND EXTENSION OF TIME
59. DIFFERING SITE CONDITIONS

Article

- 60. LIQUIDATED DAMAGES
- 61. OTHER CONTRACTS
- 62. USE OF PREMISES
- 63. SUBSTANTIAL COMPLETION DATE
- 64. PERFORMANCE TESTING
- 65. OWNER'S USE OF PORTION OF THE WORK
- 66. CUTTING AND PATCHING
- 67. CLEANING UP

PAYMENT

- 68. CHANGE ORDERS
 - A. UNIT PRICE
 - B. LUMP SUM
 - C. COST REIMBURSEMENT WORK
- 69. PARTIAL PAYMENTS
 - A. GENERAL
 - B. ESTIMATE
 - C. DEDUCTION FROM ESTIMATE
 - D. QUALIFICATIONS FOR PARTIAL
PAYMENT FOR MATERIALS DELIVERED
 - E. PAYMENT
- 70. CLAIMS FOR EXTRA WORK
- 71. RELEASE OF LIENS OR CLAIMS
- 72. FINAL PAYMENT
- 73. NO WAIVER OF RIGHTS
- 74. ACCEPTANCE OF FINAL PAYMENT
CONSTITUTES RELEASE

* * * * *

DEFINITIONS

Whenever in the Contract Documents the following terms are used, the intent and meaning shall be interpreted as follows:

1. AS APPROVED

The words “as approved”, unless otherwise qualified, shall be understood to be followed by the words “by the ENGINEER for conformance with the Contract Document”.

2. AS SHOWN, AND AS INDICATED

The words “as shown” and “as Indicated” shall be understood to be followed by the words “on the Drawings”.

3. BIDDER

The person or persons, partnership, firm, or corporation submitting a Bid for the work contemplated.

4. CONTRACT DOCUMENTS

The “Contract Documents” consist of the Bidding Requirements, Contract Forms, Conditions of the Contract, Specifications, Drawings, all modifications thereof incorporated into the Documents before their execution, Change Orders, and all other requirements incorporated by specific reference thereto. These form the Contract.

5. CONTRACTOR

The person or persons, partnership, firm, or corporation who enters into the Contract awarded him by the OWNER.

6. CONTRACT COMPLETION

The “Contract Completion” is the date the OWNER accepts the entire work as being in compliance with the Contract Documents, or formally waives nonconforming work to extent of nonconformity, and issues the final payment in accordance with the requirements set forth in Article, “Final Payment” of these General Conditions.

7. DAYS

Unless otherwise specifically stated, the term “days” will be understood to mean calendar days. Business day or working day means any day other than Saturday,

Sunday, or legal holiday.

8. DRAWINGS

The term “Drawings” refers to the official Drawings, profiles, cross sections, elevations, details, and other working drawings and supplementary drawings, or reproductions thereof, signed by the ENGINEER, which shows the location, character, dimensions, and details of the work to be performed. Drawings may either be bound in the same book as the balance of the Contract Documents, or bound in separate sets, and are a part of the Contract Documents, regardless of the method of binding.

9. ENGINEER

The person or organization identified as such in the Contract Documents. The Term “ENGINEER” means ENGINEER or his authorized representative.

10. NOTICE

The term “notice” or the requirement to notify, as used in the Contract Documents or applicable state or federal statutes, shall signify a written communication delivered in person or by registered mail to the individual, or to a member of the firm, or to an officer of the corporation for whom it is intended. Certified or registered mail shall be addressed to the last business address known to him who gives the notice.

11. OR EQUAL

The term “or equal” shall be understood to indicate that the “equal” product is equivalent to or better than the product named in function, performance, reliability, quality, and general configuration. Determination of equality in reference to the project design requirements will be made by the ENGINEER. Such equal products shall not be purchased or installed by the CONTRACTOR without written authorization.

12. OWNER

The person, organization, or public body identified as such in the Contract Documents.

13. PLANS (See Drawings)

14. SPECIFICATIONS

The term “Specifications” refers to those portions of the Contract Documents consisting of written technical

descriptions of materials, equipment, construction systems, standards, and workmanship as applied to the work and certain

administrative details applicable thereto. Where standard specifications, such as those of ASTM, AASHTO, etc., have been referred to, the applicable portions of such standard specifications shall become a part of these Contract Documents. If referenced specifications conflict with specifications contained herein, the requirements contained herein shall prevail.

15. NOTICE TO PROCEED

A written notices given by the OWNER to the CONTRACTOR (with a copy to the ENGINEER) fixing the date on which the Contract time will commence to run and on which the CONTRACTOR shall start to perform his obligation under the Contract Documents. The Notice to Proceed will be given within 30 days following the execution of the Contract by the OWNER.

16. SUBSTANTIAL COMPLETION

“Substantial Completion” shall be that degree of completion of the Project or a defined portion of the Project, as evidenced by the ENGINEER’s written notice of Substantial Completion, sufficient to provide the OWNER, at his discretion, the full-time use of the Project or defined portion of the Project for the purposes for which it was intended. “Substantial Completion” of an operating facility shall be that degree of completion that has provided a minimum of 7 continuous days of successful, trouble-free, operation, which period shall begin after all performance and acceptance testing has been successfully demonstrated to the ENGINEER. All equipment contained in the work, plus all other components necessary to enable the OWNER to operate the facility in a manner that was intended, shall be complete on the substantial completion date.

17. WORK

The word “work” within these Contract Documents shall include all material, labor, tools, and all appliances, machinery, transportation, and appurtenances necessary to perform and complete the Contract, and such additional items not specifically indicated or described which can be reasonably inferred as belonging to the item described or indicated and as required by good practice to provide a complete and satisfactory system or structure. As used herein, “provide” shall be understood to mean “furnish and install, complete in-place”.

CONTRACT DOCUMENTS

18. INTENT OF CONTRACT DOCUMENTS

The Contract Documents are complementary, and what is called for by one shall be as binding as if called for by all. The intent of the Documents is to describe a functionally complete Project (or part thereof) to be constructed in accordance with the Contract Documents. Any work, materials, or equipment that may reasonably be inferred from the Contract Documents as being required to produce the intended result shall be supplied whether or not specifically called for. When words which have a well-known technical or trade meaning are used to describe work, materials, or equipment, such words shall be interpreted in accordance with that meaning.

Reference to standard specifications, manuals, or codes of any technical society, organization or association, or to the laws or regulations of any governmental authority, whether such reference be specific or by implication, shall mean the latest standard specification, manual, code or laws or regulations in effect on the first published date of the Invitation to Bid, except as may be otherwise specifically stated. However, no provision of any referenced standard specification, manual or code (whether or not specifically incorporated by reference in the Contract Documents) shall be effective to change the duties and responsibilities of OWNER, CONTRACTOR, or ENGINEER, or any of their consultants, agents, or employees from those set forth in the Contract Documents, nor shall it be effective to assign to ENGINEER, or any ENGINEER’s consultants, agents, or employees, any duty or authority to supervise or direct the furnishing or performance of the work or any duty or authority to undertake responsibility contrary to the provisions of Article LIMITATIONS ON ENGINEER’S RESPONSIBILITIES.

19. DISCREPANCIES AND OMISSIONS

Any discrepancies or omissions found in the Contract Documents shall be reported to the ENGINEER immediately. The ENGINEER will clarify discrepancies or omissions, in writing, within a reasonable time.

In resolving inconsistencies among two or more sections of the Contract Documents, precedence shall be given in the following order:

- A. CONTRACT
- B. BID
- C. SUPPLEMENTARY CONDITIONS
- D. INVITATION TO BID
- E. INSTRUCTIONS TO BIDDERS

- F. GENERAL CONDITIONS
- G. SPECIFICATIONS
- H. DRAWINGS

Addenda shall take precedence over all sections referenced therein. Figure dimensions on Drawings shall take precedence over scale dimensions. Detailed Drawings shall take precedence over general Drawings.

20. CHANGES IN THE WORK

The OWNER, without notice to the Sureties and without invalidating the Contract, may order changes in the work within the general scope of the Contract by altering, adding to, or deducting from the work, the Contract being adjusted accordingly. All such work shall be executed under the conditions of the original Contract, except as specifically adjusted at the time of ordering such change.

In giving instructions, the ENGINEER may order minor changes in the work not involving extra cost and not inconsistent with the purposes of the Project, but otherwise, except in an emergency endangering life and property, additions or deductions from the work shall be performed only in pursuance of an approved Change Order from the OWNER, countersigned by the ENGINEER.

If the work is reduced by alterations, such action shall not constitute a claim for damages based on loss of anticipated profits.

21. EXAMINATION AND VERIFICATION OF CONTRACT DOCUMENTS

The CONTRACTOR shall thoroughly examine and become familiar with all of the various parts of these Contract Documents and determine the nature and location of the work, the general and local conditions, and all other matters, which can in any way affect the work under this Contract. Failure to make an examination necessary for this determination shall not release the CONTRACTOR from the obligations of this Contract. No verbal agreement or conversation with any officer, agent, or employee of the OWNER or with the ENGINEER either before or after the execution of this Contract shall affect or modify any of the terms or obligations herein contained.

22. DOCUMENTS TO BE KEPT ON THE JOBSITE

The CONTRACTOR shall keep one copy of the Contract

Documents on the job- site, in good order, available to the ENGINEER and to his representatives.

The CONTRACTOR shall maintain on a daily basis at the jobsite, and make available to the ENGINEER on request, one current record set of the Drawings which have been accurately marked to indicate all modifications in the completed work that differ from the design information shown on the Drawings. Upon Substantial completion of the work, the CONTRACTOR shall give the ENGINEER one complete set of these marked up record Drawings.

23. ADDITIONAL CONTRACT DOCUMENTS

Copies of Contract Documents or Drawings may be obtained on request from the ENGINEER and by paying the actual cost of reproducing the Contract Documents or Drawings.

24. OWNERSHIP OF CONTRACT DOCUMENTS

All portions of the Contract Documents, and copies thereof furnished by the ENGINEER are instruments of service for this Project. They are not to be used on other work and are to be returned to the ENGINEER on request at the completion of the work. Any reuse of these materials without specific written verification or adaptation by the ENGINEER will be at the risk of the user and without liability or legal expense to the ENGINEER. Such user shall hold the ENGINEER harmless from any and all damages, including reasonable attorneys' fees, from any and all claims arising from any such reuse. Any such verification and adaptation shall entitle the ENGINEER to further compensation at rates to be agreed upon by the user and the ENGINEER.

THE ENGINEER

25. AUTHORITY OF THE ENGINEER

The ENGINEER will be the OWNER's representative during the construction period. His authority and responsibility will be limited to the provisions set forth in these Contract Documents. The ENGINEER will have the Authority to reject work that does not conform to the Contract Documents. However, neither the ENGINEER's authority to act under this provision, nor any decision made by him in good faith either to exercise or not to exercise such authority, shall give rise to any duty or responsibility of the ENGINEER to the CONTRACTOR, any SUBCONTRACTOR, their

respective Sureties, any of their agents or employees, or any other person performing any of the work.

26. DUTIES AND RESPONSIBILITIES OF THE ENGINEER

The ENGINEER will make visits to the site at intervals appropriate to the various stages of construction to observe the progress and quality of the work and to determine, in general, if the work is proceeding in accordance with the intent of the Contract Documents. He will not make comprehensive or continuous review or observation to check quality or quantity of the work, and he will not be responsible for construction means, methods, techniques, sequences, or procedures, or for safety precautions and programs in connection with the work. Visits and observations made by the ENGINEER shall not relieve the CONTRACTOR of his obligation to conduct comprehensive inspections of the work and to furnish materials and perform acceptable work, and to provide adequate safety precautions, in conformance with the intent of the Contract.

The ENGINEER will make recommendations to the OWNER, in writing, on all claims of the OWNER or the CONTRACTOR arising from interpretation or execution of the Contract Documents. Such recommendations will be of factual and/or technical nature, and will not include the legal interpretation of the Contract Documents. Any necessary legal interpretation of the Contract Document will be made by the OWNER. Such recommendation shall be necessary before the CONTRACTOR can receive additional money under the terms of the Contract. Changes in work ordered by the ENGINEER shall be made in compliance with Article CHANGES IN THE WORK.

One or more project representatives may be assigned to observe the work. It is understood that such project representatives shall have the authority to issue notice of nonconformance and make decisions within the limitations of the authority of the ENGINEER. The CONTRACTOR shall furnish all reasonable assistance required by the ENGINEER or project representatives for proper observation of the work. The above-mentioned project representatives shall not relieve the CONTRACTOR of his obligations to conduct comprehensive inspections of the work and to furnish materials and perform acceptable work, and to provide adequate safety precautions, in conformance with the intent of the Contract.

27. LIMITATIONS ON ENGINEER'S RESPONSIBILITIES

ENGINEER will not be responsible for CONTRACTOR's means, methods, techniques, sequences, or procedures of construction, or the safety precautions and programs incident thereto, and ENGINEER will not be responsible for CONTRACTOR's failure to perform or furnish the work in accordance with the Contract Documents.

ENGINEER will not be responsible for the acts or omissions of CONTRACTOR or of any SUBCONTRACTOR, any supplier, or of any other person or organization performing or furnishing any of the work.

Whenever in the Contract Documents the terms "as ordered", "as directed", "as required", "as allowed", "as approved", or terms of like effect or import are used, or the adjectives "reasonable", "suitable", "acceptable", "proper", or "satisfactory", or adjectives of like effect or import are used to describe a requirement, direction, review or judgment of ENGINEER as to the work, it is intended that such requirement, direction, review or judgment will be solely to evaluate the work for compliance with the Contract Documents (unless there is a specific statement indicating otherwise). The use of any such term or adjective shall not be effective to assign to ENGINEER any duty or authority to supervise or direct the furnishing or performance of the work or any duty or authority to undertake responsibility contrary to the provisions of this Article.

28. REJECTED WORK

Any defective work or nonconforming materials or equipment that may be discovered at any time prior to expiration of the warranty period shall be removed and replaced by work which shall conform to the provisions of the Contract Documents. Any material condemned or rejected shall be removed at once from the project site.

Failure on the part of the ENGINEER to condemn or reject bad or inferior work or to note nonconforming materials or equipment on CONTRACTOR submittals shall not be construed to imply acceptance of such work. The OWNER shall reserve and retain all of its rights and remedies at law against the CONTRACTOR and its Surety for correction of any and all latent defects discovered after the guarantee period.

29. LINES AND GRADES

Lines and grades shall be established as provided in the supplementary conditions. All stakes, marks, and other

reference information shall be carefully preserved by the CONTRACTOR, and in case of their careless or unnecessary destruction or removal by him or his employees, such stakes, marks, and other information shall be replaced at the CONTRACTOR's expense.

30. SUBMITTALS

After checking and verifying all field measurements and after complying with applicable procedures specified in Division I, GENERAL REQUIREMENTS, CONTRACTOR shall submit to ENGINEER, in accordance with the schedule for submittals for review, shop drawings, electrical diagrams, and catalog cuts for fabricated items and manufactured items (including mechanical and electrical equipment), which shall bear a stamp or specific written indication that CONTRACTOR has satisfied CONTRACTOR's responsibilities under the Contract Documents with respect to the review of the submittal. All submittals shall be identified as ENGINEER may require. The data shown shall be complete with respect to quantities, dimensions specified, performance and design criteria, materials, and similar data to enable ENGINEER to review the information. CONTRACTOR shall also submit to ENGINEER for review, with such promptness as to cause no delay in work, all samples required by the Contract Documents. All samples shall have been checked by and accompanied by a specific written indication that CONTRACTOR has satisfied CONTRACTOR's responsibilities under the Contract Documents with respect to the review of the submission and shall be identified clearly as to material, supplier, pertinent data such as catalog numbers and the use for which intended.

Before submission of each submittal, CONTRACTOR shall have determined and verified all quantities, dimensions, specified performance criteria, installation requirements, materials, catalog numbers, and similar data with respect thereto and reviewed or coordinated each submittal with other submittals and with the requirements of the work and the Contract Documents.

At the time of each submission, CONTRACTOR shall give ENGINEER specific written notice of each variation that the submittal may have from the requirements of the Contract Documents, and, in addition, shall cause a specific notation to be made on each shop drawing submitted to ENGINEER for review and approval of each variation.

ENGINEER will review submittals with reasonable promptness, but ENGINEER's review will be only for

conformance with the design concept of the Project and for compliance with the information given in the Contract Documents and shall not extend to means, methods, techniques, sequences, or procedures of construction (except where a specific means, method, technique, sequence, or procedure of construction is indicated in or required by the Contract Documents) or to safety precautions or programs incident thereto. The review of a separate item as such will not indicate review of the assembly in which the item functions. CONTRACTOR shall make corrections required by ENGINEER, and shall return the required number of corrected copies of shop drawings and submit as required new samples for review. CONTRACTOR shall direct specific attention in writing to revisions other than the corrections called for by ENGINEER on previous submittals.

ENGINEER's review of submittals shall not relieve CONTRACTOR from the responsibility for any variation from the requirements of the Contract Documents unless CONTRACTOR has in writing called ENGINEER's attention to each such variation at the time of submission and ENGINEER has given written approval of each such variation by a specific written notation thereof incorporated therein or accompanying the shop drawing or sample approval; nor will any approval by ENGINEER relieve CONTRACTOR from responsibility for errors or omissions in the shop drawings or from responsibility for having complied with the provisions herein.

Where a shop drawing or sample is required by the specifications, any related work performed prior to ENGINEER's review and approval of the pertinent submission shall be at the sole expense and responsibility of the CONTRACTOR.

31. DETAIL DRAWINGS AND INSTRUCTIONS

The ENGINEER will furnish, with reasonable promptness, additional instructions by means of Drawings or otherwise, if, in the ENGINEER's opinion, such are required for the proper execution of the work. All such Drawings and instructions will be consistent with the Contract Documents, true developments thereof, and reasonably inferable there from.

THE CONTRACTOR AND HIS EMPLOYEES

32. CONTRACTOR, AN INDEPENDENT AGENT

The CONTRACTOR shall independently perform all

work under this Contract and shall not be considered as an agent of the OWNER or of the ENGINEER, nor shall the CONTRACTOR's SUBCONTRACTOR's or employees be subagents of the OWNER or of the ENGINEER.

33. SUBCONTRACTING

Unless modified in the Supplementary Conditions, within 10 days after the execution of the Contract, the CONTRACTOR shall submit to the ENGINEER the names of all SUBCONTRACTORS proposed for the work, including the names of any SUBCONTRACTORS that were submitted with the Bid. The CONTRACTOR shall not employ any SUBCONTRACTORS to which the OWNER may object to as lacking capability to properly perform work of the type and scope anticipated.

The CONTRACTOR is as fully responsible to the OWNER for the acts and omissions of his SUBCONTRACTORS and of persons either directly or indirectly employed by them as he is for the acts and omissions of persons directly employed by him.

Nothing contained in the Contract Documents shall create any contractual relationship between any SUBCONTRACTOR and the OWNER or ENGINEER.

34. INSURANCE AND LIABILITY

A. GENERAL

The CONTRACTOR shall provide (from insurance companies acceptable to the OWNER) the insurance coverage designated hereinafter and pay all costs.

Before commencing work under this Contract, the CONTRACTOR shall furnish the OWNER with certificates of insurance specified herein showing the type, amount class of operations covered, effective dates, and date of expiration of policies, and containing substantially the following statement:

"The insurance covered by this certificate shall not be canceled or materially altered, except after 30 days' written notice has been received by the OWNER."

In case of the breach of any provision of this Article, the OWNER, at his option, may take out and maintain, at the expense of the CONTRACTOR, such insurance as the OWNER may deem proper and may deduct the cost of such insurance from any monies which may be due or become due the CONTRACTOR under this Contract.

B. CONTRACTOR AND SUBCONTRACTOR INSURANCE

The CONTRACTOR shall not commence work under this Contract until he has obtained all the insurance required hereunder and such insurance has been reviewed by the OWNER, nor shall the CONTRACTOR allow any SUBCONTRACTOR to commence work on his subcontract until insurance specified below has been obtained. Review of the insurance by the OWNER shall not relieve or decrease the liability of the CONTRACTOR hereunder.

C. COMPENSATION AND EMPLOYER'S LIABILITY INSURANCE

The CONTRACTOR shall maintain during the life of this Contract the statutory amount of Workmen's Compensation Insurance, in addition, Employer's Liability Insurance in an amount as specified in the Supplementary Conditions, for each occurrence, for all of his employees to be engaged in work on the project under this Contract. In case any such work is subcontracted, the Contractor shall require the Subcontractor to provide similar Worker's Compensation and Employer's Liability Insurance for all of the Subcontractor's employees to be engaged in such work.

D. GENERAL LIABILITY INSURANCE (INCLUDING AUTOMOBILE)

The CONTRACTOR shall maintain during the life of this Contract such general liability, completed operations and products liability, and automobile liability insurance as will provide coverage for claims for damages for personal injury, including accidental death, as well as for claims for property damage, which may arise directly or indirectly from performance of the work under this Contract. The general liability policy shall include contractual liability assumed by the CONTRACTOR under Article **INDEMNITY**. Coverage for property damage shall be on a "broad form" basis with no exclusions for "X, C & U". The amount of insurance to be provided shall be as specified in the Supplementary Conditions.

In the event any work under this Contract is performed by a SUBCONTRACTOR, the CONTRACTOR shall be responsible for any liability directly or indirectly arising out of the work performed by the SUBCONTRACTOR, to the extent such liability is not covered by the SUBCONTRACTOR's insurance.

The OWNER and ENGINEER, their officers, agents, and employees shall be named as Additional Insured's on the CONTRACTOR's and any SUBCONTRACTOR's general liability and automobile liability insurance policies for any claims arising out of work performed under this Contract.

E. BUILDERS RISK ALL RISK INSURANCE

Unless otherwise modified in the Supplementary Conditions, the CONTRACTOR shall secure and maintain during the life of this Contract, Builders Risk All Risk Insurance coverage in an amount equal to the full value of the facilities/ work performed under this Contract/ construction. Such insurance shall include coverage for earthquake, landslide, flood, collapse, loss due to the results of faulty workmanship or design, and all other normally covered risks, and shall provide for losses to be paid to the CONTRACTOR, OWNER, and ENGINEER as their interests may appear.

The OWNER and ENGINEER, their officers, agents, and employees shall be named as additional insured's on the CONTRACTOR's and any SUBCONTRACTOR's Builders Risk All Risk insurance policies for any claims arising out of work performed under this Contract.

This insurance shall include a waiver of subrogation as to the ENGINEER, the OWNER, the CONTRACTOR, and their respective officers, agents, employees and SUBCONTRACTORS.

F. NO PERSONAL LIABILITY OF PUBLIC OFFICIALS

In carrying out any of the provisions hereof in exercising any authority granted by the Contract, there will be no personal liability upon any public official.

35. INDEMNITY

To the maximum extent permitted by law, the Contractor shall indemnify and defend the Owner and the Engineer, and their officers, employees, agents, and sub-consultants, from all claims and losses, including attorney's fees and litigation costs arising out of property losses or health, safety, personal injury, or death claims by the Contractor, its subcontractors of any tier, and their employees, agents, or invitees regardless of the fault, breach of Contract, or negligence of the Owner or Engineer, excepting only such claims or losses that have been adjudicated to have been caused solely by the negligence of the Owner or the Engineer and regardless of whether or not the Contractor is or can be named a

party in a litigation.

36. EXCLUSION OF CONTRACTOR CLAIMS

In performing its obligations, the ENGINEER and its consultants may cause expense for the CONTRACTOR or its SUBCONTRACTORS and equipment or material suppliers. However, those parties and their sureties shall maintain no direct action against the ENGINEER, its officers, employees, agents, and consultants for any claim arising out of, in connection with, or resulting from the engineering services performed or required to be performed.

37. TAXES AND CHARGES

The CONTRACTOR shall withhold and pay any and all sales and use taxes and all withholding taxes, whether State or Federal, and pay all Social Security charges and also all State Unemployment Compensation charges, and pay or cause to be withheld, as the case may be, any and all taxes, charges, or fees or sums whatsoever, which are now or may hereafter be required to be paid or withheld under any laws.

38. REQUIREMENTS OF STATE LAW FOR PUBLIC WORKS PROJECTS

When the Contract Documents concern public works of the state or any county, municipality, or political subdivision created by its laws, the applicable statutes shall apply. All parties to this Contract shall determine the contents of all applicable statutes and comply with their provisions throughout the performance of the Contract.

39. CODES, ORDINANCES, PERMITS AND LICENSES

The CONTRACTOR shall keep himself fully informed of all local codes and ordinances, as well as state and federal laws, which in any manner affect the work herein specified. The CONTRACTOR shall at all times comply with said codes and ordinances, laws, and regulations, and protect and indemnify the OWNER, the ENGINEER and their respective employees, and its officers and agents against any claim or liability arising from or based on the violation of any such laws, ordinances, or regulations. All permits, licenses and inspection fees necessary for prosecution and completion of the work shall be secured and paid for by the CONTRACTOR, unless otherwise specified.

40. SUPERINTENDENCE

The CONTRACTOR shall keep at the project site, competent supervisory personnel. The CONTRACTOR shall designate, in writing, before starting work, a project superintendent who shall be an employee of the CONTRACTOR and shall have complete authority to represent and to act for the CONTRACTOR. ENGINEER shall be notified in writing prior to any change in superintendent assignment. The CONTRACTOR shall give efficient supervision to the work, using his best skill and attention. The CONTRACTOR shall be solely responsible for all construction means, methods, techniques, and procedures, and for providing adequate safety precautions and coordinating all portions of the work under the Contract. It is specifically understood and agreed that the ENGINEER, its employees and agents, shall not have control or charge of and shall not be responsible for the construction means, methods, techniques, procedures, or for providing adequate safety precautions in connection with the work under Contract.

41. RECEPTION OF ENGINEER'S COMMUNICATIONS

The superintendent shall receive for the CONTRACTOR all communications from the ENGINEER. Communications of major importance will be confirmed in writing upon request from the CONTRACTOR.

The ENGINEER may schedule project meetings for the purposes of discussing and resolving matters concerning the various elements of the work. Time and place for these meetings and the names of persons required to be present shall be as determined by the ENGINEER. CONTRACTOR shall comply with these attendance requirements and shall also require his SUBCONTRACTORS to comply.

42. SAFETY

The CONTRACTOR shall be solely and completely responsible for conditions of the jobsite, including safety of all persons (including employees) and property during performance of the work. This requirement shall apply continuously and not be limited to normal working hours. Safety provisions shall conform to U.S. Department of Labor (OSHA), and all other applicable federal, state, county, and local laws, ordinances, codes, and regulations. Where any of these are in conflict, the more stringent requirement shall be followed. The CONTRACTOR's failure to thoroughly familiarize himself with the aforementioned safety provisions shall

not relieve him from compliance with the obligations and penalties set forth therein.

The CONTRACTOR shall develop and maintain for the duration of this Contract, a safety program that will effectively incorporate and implement all required safety provisions. The CONTRACTOR shall appoint an employee who is qualified and authorized to supervise and enforce compliance with the safety program.

The duty of the ENGINEER to conduct construction review of the work does not include review or approval of the adequacy of the CONTRACTOR's safety program, safety supervisor, or any safety measures taken in, on, or near the construction site.

The CONTRACTOR, as a part of his safety program, shall maintain at his office or other well-known place at the jobsite, safety equipment applicable to the work as prescribed by the aforementioned authorities, all articles necessary for giving first-aid to the injured, and shall establish the procedure for the immediate removal to a hospital or a doctor's care of persons (including employees) who may be injured on the jobsite.

If death or serious injuries or serious damages are caused, the accident shall be reported immediately by telephone or messenger to both the ENGINEER and the OWNER. In addition, the CONTRACTOR must promptly report in writing to the ENGINEER all accidents whatsoever arising out of, or in connection with, the performance of the work whether on, or adjacent to, the site, giving full details and statements of witnesses.

If a claim is made by anyone against the CONTRACTOR or any SUBCONTRACTOR on account of any accident, the CONTRACTOR shall promptly report the facts in writing to the ENGINEER, giving full details of the claim.

43. PROTECTION OF WORK AND PROPERTY

The CONTRACTOR shall at all times safely guard and protect from damage the OWNER's property, adjacent property, and his own work from injury or loss in connection with this Contract. All facilities required for protection by federal, state, or municipal laws and regulations and local conditions must be provided and maintained.

The CONTRACTOR shall protect his work and materials from damage due to the nature of the work, the

elements, carelessness of other CONTRACTORS, or from any cause whatever until the completion and acceptance of the work. All loss or damages arising out of the nature of the work to be done under these Contract Documents, or from any unforeseen obstruction or defects which may be encountered in the prosecution of the work, or from the action of the elements, shall be sustained by the CONTRACTOR.

44. RESPONSIBILITY OF CONTRACTOR TO ACT IN AN EMERGENCY

In case of an emergency which threatens loss or injury of property, and/or safety of life, the CONTRACTOR shall act, without previous instructions from the OWNER or ENGINEER, as the situation may warrant. The CONTRACTOR shall notify the ENGINEER thereof immediately thereafter. Any claim for compensation by the CONTRACTOR, together with substantiating documents in regard to expense, shall be submitted to the OWNER through the ENGINEER and the amount of compensation shall be determined by agreement.

45. MATERIALS AND APPLIANCES

Unless otherwise stipulated, the CONTRACTOR shall provide and pay for all materials, labor, water, tools, equipment, heat, light, fuel, power, transportation, construction equipment and machinery, appliances, telephone, sanitary facilities, temporary facilities and other facilities and incidentals necessary for the execution and completion of the work.

Unless otherwise specified, all materials shall be new, and both workmanship and materials shall be of good quality. The CONTRACTOR shall, if required, furnish satisfactory evidence as to the kind and quality of materials.

In selecting and/or approving equipment for installation in the Project, the OWNER and ENGINEER assume no responsibility for injury or claims resulting from failure of the equipment to comply with applicable federal, state, and local safety codes or requirements, or the safety requirements of a recognized agency, or failure due to faulty design concepts, or defective workmanship and materials.

46. CONTRACTORS' AND MANUFACTURERS' COMPLIANCE WITH STATE SAFETY, OSHA, AND OTHER CODE REQUIREMENTS

The completed work shall include all necessary permanent safety devices, such as machinery guards and similar ordinary safety items required by the state and federal (OSHA) industrial authorities and applicable local and national codes. Further, any features of the work subject to such safety regulations shall be fabricated, furnished, and installed (including OWNER-furnished equipment) in compliance with these requirements. CONTRACTORS and manufacturers of equipment shall be held responsible for compliance with the requirements included herein. CONTRACTORS shall notify all equipment suppliers and SUBCONTRACTORS of the provisions of this Article.

47. SUBSTITUTION OF MATERIALS

Except for OWNER-selected equipment items, and items where no substitution is clearly specified, whenever any material, article, device, product, fixture, form, type of construction, or process is indicated or specified by patent or proprietary name, by name of manufacturer, or by catalog number, such specifications shall be deemed to be used for the purpose of establishing a standard of quality and facilitating the description of the material or process desired. This procedure is not to be construed as eliminating from competition other products of equal or better quality by other manufacturers where fully suitable in design, and shall be deemed to be followed by the words "or equal". The CONTRACTOR may, in such cases, submit complete data to the ENGINEER for consideration of another material, type, or process that shall be substantially equal in every respect to that so indicated or specified. Substitute materials shall not be used unless approved in writing. The ENGINEER will be the sole judge of the substituted article or material.

48. TESTS, SAMPLES, AND OBSERVATIONS

The CONTRACTOR shall furnish, without extra charge, the necessary test pieces and samples, including facilities and labor for obtaining the same, as requested by the ENGINEER. When required, the CONTRACTOR shall furnish certificates of tests of materials and equipment made at the point of manufacture by a recognized testing laboratory.

The OWNER, ENGINEER, and authorized government agents, and their representatives shall at all times be provided safe access to the work wherever it is in

preparation or progress, and the CONTRACTOR shall provide facilities for such access and for observations, including maintenance of temporary and permanent access.

If the Specifications, laws, ordinances, or any public authority require any work, to be specially tested or approved, the CONTRACTOR shall give timely notice of its readiness for observations. If any work should be covered up without approval or consent of the ENGINEER, it shall, if required by the ENGINEER, be uncovered for examination at the CONTRACTOR's expense.

Reexamination of questioned work may be ordered by the ENGINEER, and, if so ordered, the work shall be uncovered by the CONTRACTOR. If such work is found to be in accordance with the Contract Documents, the OWNER will pay the cost of uncovering, exposure, observation, inspection, testing and reconstruction. If such work is found to be not in accordance with the Contract Documents, the CONTRACTOR shall correct the defective work, and the cost of reexamination and correction of the defective work shall be paid by the CONTRACTOR.

49. ROYALTIES AND PATENTS

The CONTRACTOR shall pay all royalty and licenses fees, unless otherwise specified. The CONTRACTOR shall defend all suits or claims for infringement of any patent rights and shall save the OWNER and the ENGINEER harmless from any and all loss, including reasonable attorneys' fees, on account thereof.

50. CONTRACTOR'S RIGHT TO TERMINATE CONTRACT

If the work should be stopped under an order of any court or other public authority for a period of more than 3 months, through no act or fault of the CONTRACTOR, its SUBCONTRACTORS, or respective employees or if the ENGINEER should fail to make recommendation for payment to the OWNER or return payment request to CONTRACTOR for revision within 30 days after it is due, or if the OWNER should fail to pay the CONTRACTOR within 30 days after time specified in Article PARTIAL PAYMENTS, any sum recommended by the ENGINEER, then the CONTRACTOR may, upon 15 days' written notice to the OWNER and the ENGINEER, stop work or terminate this Contract and recover from the OWNER payment for all acceptable work performed and reasonable termination expenses, unless said default has been remedied.

51. CORRECTION OF DEFECTIVE WORK DURING WARRANTY PERIOD

The CONTRACTOR hereby agrees to make, at his own expense, all repairs or replacements necessitated by defects in materials or workmanship, provided under terms of this Contract, and pay for any damage to other works resulting from such defects, which become evident within 2 years after the date of final acceptance of the work or within 2 years after the date of substantial completion established by the ENGINEER for specified items of equipment, or within such longer period as may be prescribed by law or by the terms of any applicable special guarantee required by the Contract Documents. Un-remedied defects identified for correction during the warranty period but remaining after its expiration shall be considered as part of the obligations of the warranty. Defects in material, workmanship, or equipment which are remedied as a result of obligations of the warranty shall subject the remedied portion of the work to an extended warranty period of 2 years after the defect has been remedied.

The CONTRACTOR further assumes responsibility for a similar guarantee for all work and materials provided by SUBCONTRACTORS or manufacturers of packaged equipment components. The effective date for the start of the guarantee or warranty period for equipment qualifying as substantially complete is defined in Article SUBSTANTIAL COMPLETION, AND Article SUBSTANTIAL COMPLETION DATE, in these General Conditions.

The CONTRACTOR also agrees to hold the OWNER and the ENGINEER harmless from liability of any kind arising from damage due to said defects. The CONTRACTOR shall make all repairs and replacements promptly upon receipt of written order for same from the OWNER. If the CONTRACTOR fails to make the repairs and replacements promptly, or in an emergency where delay would cause serious risk, or loss, or damage, the OWNER may have the defective work corrected or the rejected work removed and replaced, and the CONTRACTOR and his Surety shall be liable for the cost thereof.

PROGRESS OF THE WORK

52. BEGINNING OF THE WORK

Following execution of the Contract, the CONTRACTOR shall meet with the OWNER and ENGINEER relative to his arrangements for prosecuting the work.

53. SCHEDULES AND PROGRESS REPORTS

Prior to starting the construction, the CONTRACTOR shall prepare and submit to the ENGINEER, a progress schedule showing the dates on which each part or division of the work is expected to be started and finished, and a preliminary schedule for submittals. The progress schedule for submittals shall be brought up to date and submitted to the ENGINEER at the end of each month or at such other times the ENGINEER may request.

The CONTRACTOR shall forward to the ENGINEER, at the end of each month, an itemized report of the delivery status of major and critical items of purchased equipment and material, including shop drawings and the status of shop and field fabricated work. These progress reports shall indicate the date of the purchase order, the current percentage of completion, estimated delivery, and cause of delay, if any.

If the completion of any part of the work or the delivery of materials is behind the submitted progress schedule, the CONTRACTOR shall submit in writing a plan acceptable to the OWNER and ENGINEER for bringing the work up to schedule.

The OWNER shall have the right to withhold progress payments for the work if the CONTRACTOR fails to update and submit the progress schedule and reports as specified.

54. PROSECUTION OF THE WORK

It is expressly understood and agreed that the time of beginning, rate of progress, and time of completion of the work are the essence of this Contract. The work shall be prosecuted at such time, and in or on such part or parts of the Project as may be required, to complete the Project as contemplated in the Contract Documents and the progress schedule.

If the CONTRACTOR desires to carry on work at night or outside the regular hours, he shall give timely notice to the ENGINEER to allow satisfactory arrangements to be made for observing the work in progress.

55. OWNER'S RIGHT TO RETAIN IMPERFECT WORK

If any part or portion of the work completed under this Contract shall prove defective and not in accordance with the Drawings and Specifications, and if the imperfection in the same shall not be of sufficient magnitude or

importance as to make the work dangerous or unsuitable, or if the removal of such work will create conditions which are dangerous or undesirable, the OWNER shall have the right and authority to retain such work but will make such deductions in the final payment therefore as may be just and reasonable.

56. OWNER'S RIGHT TO DO WORK

Should the CONTRACTOR neglect to prosecute the work in conformance with the Contract Documents or neglect or refuse at his own cost to remove and replace work rejected by the ENGINEER, then the OWNER may notify the Surety of the condition, and after 10 days' written notice to the CONTRACTOR and the Surety, or without notice if an emergency or danger to the work or public exists, and without prejudice to any other right which the OWNER may have under Contract, or otherwise, take over that portion of the work which has been improperly or non-timely executed, and make good the deficiencies and deduct the cost thereof from the payments then or thereafter due the CONTRACTOR.

57. OWNER'S RIGHT TO TRANSFER EMPLOYMENT

If the CONTRACTOR should abandon the work or if he should persistently or repeatedly refuse or should fail to make prompt payment to SUBCONTRACTORS for material or labor, or to persistently disregard laws, ordinances, or to prosecute the work in conformance with the Contract Documents, or otherwise be guilty of a substantial violation of any provision of the Contract or any laws or ordinance, then the OWNER may, without prejudice to any other right or remedy, and after giving the CONTRACTOR and Surety 10 days' written notice, transfer the employment for said work from the CONTRACTOR to the Surety. Upon receipt of such notice, such Surety shall enter upon the premises and take possession of all materials, tools, and appliances thereon for the purpose of completing the work included under this Contract and employ by Contract or otherwise, any qualified person or persons to finish the work and provide the materials therefore, in accordance with the Contract Documents, without termination of the continuing full force and effect of this Contract. In case of such transfer of employment to such Surety, the Surety shall be paid in its own name on estimates according to the terms hereof without any right of the CONTRACTOR to make any claim for the same or any part thereof.

If, after the furnishing of said written notice to the Surety, the CONTRACTOR and the Surety still fail to

make reasonable progress on the performance of the work, the OWNER may terminate the employment of the CONTRACTOR and take possession of the premises and of all materials, tools, and appliances thereon and finish the work by whatever method he may deem expedient and charge the cost thereof to the CONTRACTOR and the Surety. In such case, the CONTRACTOR shall not be entitled to receive any further payment until the work is finished. If the expense of completing the Contract, including compensation for additional managerial and administrative services, shall exceed such unpaid balance, the CONTRACTOR and the Surety shall pay the difference to the OWNER.

58. DELAYS AND EXTENSION OF TIME

If the CONTRACTOR is delayed in the progress of the work by any act or neglect of the OWNER or the ENGINEER, or by any separate CONTRACTOR employed by the OWNER, or by strikes, lockouts, fire, adverse weather conditions not reasonably anticipated, or acts of Nature, and if the CONTRACTOR, within 48 hours of the start of the occurrence, gives written notice to the OWNER of the cause of the potential delay and estimate of the possible time extension involved, and within 10 days after the cause of the delay has been remedied, the CONTRACTOR gives written notice to the OWNER of any actual time extension requested as a result of the aforementioned occurrence, then the Contract time may be extended by change order for such reasonable time as the ENGINEER determines. It is agreed that no claim shall be made or allowed for any damages, loss, or expense which may arise out of any delay caused by the above referenced acts or occurrences other than claims for the appropriate extension of time.

No extension of time will be granted to the CONTRACTOR for delays occurring to parts of the work that have no measurable impact on the completion of the total work under this Contract. No extension of time will be considered for weather conditions reasonably anticipated for the area in which the work is being performed. Reasonably anticipated weather conditions will be based on official records of monthly precipitation and other historical data. Adverse weather conditions, if determined to be of a severity that would impact progress of the work, may be considered as cause for an extension of Contract completion time.

Delays in delivery of equipment or material purchased by the CONTRACTOR or his SUBCONTRACTORS, including OWNER-selected equipment shall not be considered as a just cause for delay, unless the OWNER determines that for good cause the delay is beyond the

control of the CONTRACTOR. The CONTRACTOR shall be fully responsible for the timely ordering, scheduling, expediting, delivery, and installation of all equipment and materials.

Within a reasonable period after the Contractor submits to the Owner a written request for an extension of time, the Engineer will present his written opinion to the Owner as to whether an extension of time is justified, and, if so, his recommendation as to the number of days for time extension. The Owner will make the final decision on all requests for extension of time.

59. DIFFERING SITE CONDITIONS

The CONTRACTOR shall promptly, and before the conditions are disturbed, give a written notice to the OWNER and ENGINEER of:

- A. Subsurface or latent physical conditions at the site which differ materially from those indicated in this contract,
- B. Unknown physical conditions at the site, of an unusual nature, which differ materially from those ordinarily encountered and generally recognized as inherent in work of the character provided for in the Contract.

The ENGINEER will investigate the site conditions promptly after receiving the notice. If the conditions do materially so differ and cause an increase or decrease in the CONTRACTOR's cost of, or the time required for, performing any part of the work under this Contract, whether or not changed as a result of the conditions, and equitable adjustment shall be made under this Article and the Contract modified in writing accordingly.

No request by the CONTRACTOR for an equitable adjustment to the Contract under this Article will be allowed, unless the CONTRACTOR has given the written notice required; provided that the time prescribed above for giving written notice may be extended by the OWNER.

No request by the CONTRACTOR for an equitable adjustment to the Contract for differing site conditions will be allowed if made after final payment under this Contract.

60. LIQUIDATED DAMAGES

Should the CONTRACTOR fail to complete the work, or any part thereof, in the time agreed upon in the Contract or within such extra time as may have been allowed for

delays by extensions granted as provided in the Contract, the CONTRACTOR shall reimburse the OWNER for the additional expense and damage for each calendar day, Sundays and legal holidays included, that the Contract remains uncompleted after the Contract completion date. It is agreed that the amount of such additional expense and damage incurred by reason of failure to complete the work is the per-diem rate, as stipulated in the Bid. The said amount is hereby agreed upon as a reasonable estimate of the costs which may be accrued by the OWNER after the expiration of the time of completion. It is expressly understood and agreed that this amount is not to be considered in the nature of a penalty, but as liquidated damages which have accrued against the CONTRACTOR. The OWNER shall have the right to deduct such damages from any amount due, or that may become due the CONTRACTOR, or the amount of such damages shall be due and collectible from the CONTRACTOR or Surety.

61. OTHER CONTRACTS

The OWNER reserves the right to let other Contracts in connection with the work. The CONTRACTOR shall afford other CONTRACTORS reasonable opportunity for the introduction and storage of their materials and the execution of their work and shall properly connect and coordinate his work with theirs.

If any part of the work under this Contract depends for proper execution or results upon the work of any other CONTRACTOR, utility service company or OWNER, the CONTRACTOR shall inspect and promptly report to the ENGINEER in writing any patent or apparent defects to deficiencies in such work that render it unsuitable for such proper execution and results. The CONTRACTOR's failure to so report shall constitute and acceptance of the work by others as being fit and proper for integration with work under this Contract, except for latent or non-apparent defects and deficiencies in the work.

62. USE OF PREMISES

The CONTRACTOR shall confine his equipment, the storage of materials and the operation of his workers to limits shown on the Drawings or indicated by law, ordinances, permits, or directions of the ENGINEER, and shall not unreasonably encumber the premises with his materials. The CONTRACTOR shall provide, at his own expense, the necessary rights-of-way and access to the work, which may be required outside the limits of the OWNER's property and shall furnish the ENGINEER copies of permits and agreements for use of the property

outside that provided by the OWNER.

The CONTRACTOR shall not load nor permit any part of the structure to be loaded in any manner that will endanger the structure, nor shall CONTRACTOR subject any part of the work or adjacent property to stresses or pressures that will endanger it.

63. SUBSTANTIAL COMPLETION DATE

The ENGINEER may issue a written notice of substantial completion for the purpose of establishing the starting date for specific equipment guarantees, and to establish the date that the OWNER will assume the responsibility for the cost of operating such equipment. Said notice shall not be considered as final acceptance of any portion of the work or relieve the CONTRACTOR from completing the remaining work within the specified time and in full compliance with the Contract Documents. See SUBSTANTIAL COMPLETION under DEFINITIONS of these General Conditions.

64. PERFORMANCE TESTING

Operating equipment and systems shall be performance tested in the presence of the ENGINEER to demonstrate compliance with the specified requirements. Performance testing shall be conducted under the specified design operating conditions or under such simulated operating conditions as recommended or approved by the ENGINEER. Schedule such testing with the ENGINEER at least one week in advance of the planned date for testing.

65. OWNER'S USE OF PORTIONS OF THE WORK

Following issuance of the written notice of Substantial Completion, the OWNER may initiate operation of the facility. Such use shall not be considered as final acceptance of any portion of the work, nor shall such use be considered as cause for an extension of the Contract completion time, unless authorized by a Change Order issued by the OWNER.

66. CUTTING AND PATCHING

The CONTRACTOR shall do all cutting, fitting, or patching of his work that may be required to make its several parts come together properly and fit it to receive or be received by work of other CONTRACTORS shown upon or reasonably implied by the Drawings.

67. CLEANING UP

The CONTRACTOR shall, at all times, keep property on which work is in progress and the adjacent property free from accumulations of waste material or rubbish caused by employees or by the work. Upon completion of the construction, the CONTRACTOR shall remove all temporary structures, rubbish, and waste materials resulting from his operations.

PAYMENT

68. PAYMENT FOR CHANGE ORDERS

The OWNER’s request for quotations on alterations to the work shall not be considered authorization to proceed with the work prior to the issuance of a formal Change Order, nor shall such a request justify any delay in existing work. Quotations for alterations to the work shall include substantiating documentation with an itemized breakdown of CONTRACTOR and SUBCONTRACTOR costs, including labor, material, rentals, approved services, overhead, and profit. OWNER may require detailed cost data in order to substantiate the reasonableness of the proposed costs.

Any compensation paid in conjunction with the terms of a Change Order shall comprise total compensation due the CONTRACTOR for the work or alteration defined in the Change Order. By signing the Change Order, the CONTRACTOR acknowledges that the stipulated compensation includes payment for the work or alteration plus all payment for the interruption of schedules, extended overhead, delay, or any other impact claim or ripple effect, and by such signing specifically waives any reservation or claim for additional compensation in respect to the subject Change Order.

At the OWNER’s option, payment or credit for any alterations covered by a Change Order shall be determined by one or a combination of the methods set forth in A, B, or C below, as applicable:

A. UNIT PRICES

Those unit prices stipulated in the Bid shall be utilized where they are applicable. In the event the Change Order results in a change in the original quantity that is materially and significantly different from the original bid quantity, a new unit price shall be negotiated upon demand of either party. Unit prices for new items included in the Change Order shall be negotiated and mutually agreed upon.

B. LUMP SUM

A total lump sum for the work negotiated and mutually acceptable to the CONTRACTOR and the OWNER.

Lump sum quotations for modifications to the work shall include substantiating documentation with an itemized breakdown of CONTRACTOR and SUBCONTRACTOR costs, including labor, material, rentals, approved services, overhead, and profit, all calculated as specified under “C” below.

C. COST REIMBURSEMENT WORK

The term “cost reimbursement” shall be understood to mean that payment for the work will be made on a time and expense basis, that is, on an accounting of the CONTRACTOR’s forces, materials, equipment, and other items of cost as required and used to do the work.

If the method of payment cannot be agreed upon prior to the beginning of the work, and the OWNER directs by written Change Order that the work be done on a cost reimbursement basis, then the CONTRACTOR shall furnish labor, and furnish and install equipment and materials necessary to complete the work in a satisfactory manner and within a reasonable period of time. For the work performed, payment will be made for the documented actual cost of the following:

1. Labor including foremen for those hours they are assigned and participating in the cost reimbursement work (actual payroll cost, including wages, fringe benefits as established by negotiated labor agreements, labor insurance, and labor taxes as established by law). No other fixed labor burdens will be considered, unless approved in writing by the OWNER.
2. Material delivered and used on the designated work, including sales tax, if paid by the CONTRACTOR or his SUBCONTRACTOR.
3. Rental or equivalent rental cost of equipment, including necessary transportation for items having a value in excess of \$100.

Rental or equivalent rental cost will be allowed for only those days or hours during which the equipment is in actual use. Rental and transportation allowances shall not exceed the current rental rates prevailing in the locality. The rentals allowed for equipment will, in all cases, be understood to cover all fuel, supplies, repairs, and renewals, and no further allowances

will be made for those items, unless specific agreement to that effect is made.

4. Additional bond, as required and approved by the OWNER.
5. Additional insurance (other than labor insurance) as required and approved by the OWNER.

In addition to items 1 through 5 above, an added fixed fee for general overhead and profit shall be negotiated and allowed for the CONTRACTOR (or approved SUBCONTRACTOR) actually executing the Cost Reimbursement work.

An additional fixed fee shall be negotiated and allowed the CONTRACTOR for the administrative handling of portions of the work that are executed by an approved SUBCONTRACTOR. No additional fixed fee will be allowed for the administrative handling of work executed by a SUBCONTRACTOR of a SUBCONTRACTOR, unless by written permission from the OWNER.

The added fixed fees shall be considered to be full compensation, covering the cost of general supervision, overhead, profit, and any other general expense. The CONTRACTOR's records shall make clear distinction between the direct costs of work paid for on a cost reimbursement basis and the costs of other work. The CONTRACTOR shall furnish the ENGINEER report sheets in duplicate of each day's cost reimbursement work no later than the working day following the performance of said work. The daily report sheets shall itemize the materials used, and shall cover the direct cost of labor and the charges for equipment rental, whether furnished by the CONTRACTOR, SUBCONTRACTOR or other forces. The daily report sheets shall provide names or identifications and classifications of workers, the hourly rate of pay and hours worked, and also the size, type, and identification number of equipment and hours operated.

Material charges shall be substantiated by valid copies of vendors' invoices. Such invoices shall be submitted with the daily report sheets, or, if not available, they shall be submitted with subsequent daily report sheets. Said daily report sheets shall be signed by the CONTRACTOR or his authorized agent.

The OWNER reserves the right to furnish such materials and equipment as he deems expedient and the CONTRACTOR shall have no claim for profit or added fees on the cost of such materials and equipment. To receive partial payments and final payment for cost reimbursement work, the CONTRACTOR shall submit

to the ENGINEER, detailed and complete documented verification of the CONTRACTOR's and any of his SUBCONTRACTORS' actual costs involved in the cost reimbursement work. Such costs shall be submitted within 30 days after said work has been performed.

69. PARTIAL PAYMENTS

A. GENERAL

Nothing in this Article shall be construed to affect the right, hereby reserved, to reject the whole or any part of the aforesaid work, should such work be later found not to comply with the provisions of the Contract Documents. All estimated quantities of work for which partial payments have been made are subject to review and correction on the final estimate. Payment by the OWNER and acceptance by the CONTRACTOR of partial payments based on periodic estimates of quantities of work performed shall not, in any way, constitute acceptance of the estimated quantities used as a basis for computing the amounts of the partial payments.

B. ESTIMATE

At least 30 days before each progress payment falls due, as specified in the Supplementary Conditions, the CONTRACTOR shall submit to the ENGINEER a detailed estimate of the amount earned during the preceding month for the separate portions of the work, and request payment. As used in this Article, the words "amount earned" means the value, on the date of the estimate for partial payment, of the work completed in accordance with the Contract Documents, and the value of approved materials delivered to the project site suitable stored and protected prior to incorporation into the work.

ENGINEER will, within 7 days after receipt of each request for payment, either indicate in writing a recommendation of payment and present the request to OWNER, or return the request to CONTRACTOR indicating in writing ENGINEER's reasons for refusing to recommend payment. In the latter case, CONTRACTOR may, within 7 days, make the necessary corrections and resubmit the request.

ENGINEER may refuse to recommend the whole or any part of any payment if, in his opinion, it would be incorrect to make such representations to OWNER. ENGINEER may also refuse to recommend any such payment, or, because of subsequently discovered evidence or the results of subsequent inspections or tests,

nullify any such payment previously recommended to such an extent as may be necessary in ENGINEER's opinion to protect the OWNER from loss because:

1. The work is defective, or completed work has been damaged requiring correction or replacement;
2. Written claims have been made against OWNER or Liens have been filed in connection with the work;
3. The Contract Price has been reduced because of Change Orders;
4. OWNER has been required to correct defective work or complete the work in accordance with Article OWNER'S RIGHT TO DO WORK;
5. Of CONTRACTOR's unsatisfactory prosecution of the work in accordance with the Contract Documents; or
6. CONTRACTOR's failure to make payment to SUBCONTRACTORS or for labor, materials, or equipment.

C. DEDUCTION FROM ESTIMATE

Unless modified in the Supplementary Conditions, deductions from the estimate will be as described below:

1. The OWNER will deduct from the estimate, and retain as part security, 10 percent of the amount earned for work satisfactorily completed. A deduction and retainage of 10 percent will be made on the estimated amount earned for approved items of material delivered to and properly stored at the jobsite but not incorporated into the work. When the work is 50 percent complete, the OWNER may reduce the retainage to 5 percent of the dollar value of all work satisfactorily completed to date provided the CONTRACTOR is making satisfactory progress and there is no specific cause for a greater retainage. The OWNER may reinstate the retainage up to 10 percent if the OWNER determines, at his discretion, that the CONTRACTOR is not making satisfactory progress or where there is other specific cause for such withholding.

D. QUALIFICATION FOR PARTIAL PAYMENT FOR MATERIALS DELIVERED

Unless modified in the Supplementary Conditions, qualification for partial payment for materials delivered but not yet incorporated into the work shall be as described below:

1. Materials, as used herein, shall be considered to be those items which are fabricated and manufactured material and equipment. No consideration shall be given to individual purchases of less than \$200 for any one item.
2. To receive partial payment for materials delivered to the site, but not incorporated in the work, it shall be necessary for the CONTRACTOR to include a list of such materials on the Partial Payment Request. At his sole discretion, the ENGINEER may approve items for which partial payment is to be made. Partial payment shall be based on the CONTRACTOR's actual cost for the materials as evidenced by invoices from the supplier. Proper storage and protection shall be provided by the CONTRACTOR, and as approved by the ENGINEER. Final payment shall be made only for materials actually incorporated in the work and, upon acceptance of the work, all materials remaining for which advance payments had been made shall revert to the CONTRACTOR, unless otherwise agreed, and partial payments made for these items shall be deducted from the final payment for the work.

3. CONTRACTOR warrants and guarantees that title to all work, materials, and equipment covered by any Application for Payment, whether incorporated in the Project or not, will pass to OWNER at the time of payment free and clear of all liens, claims, security interests, and encumbrances.
4. If requested by the ENGINEER, the CONTRACTOR shall provide, with subsequent pay requests, invoices receipted by the supplier showing payment in full has been made.

E. PAYMENT

After deducting the retainage and the amount of all previous partial payments made to the CONTRACTOR from the amount earned, the amount due will be made payable to the CONTRACTOR. Recommendations for payment received by the OWNER less than 9 days prior to the scheduled day for payment will not be processed or paid until the following month.

70. CLAIMS FOR EXTRA WORK

In any case where the CONTRACTOR deems additional time or compensation will become due him under this Contract for circumstances other than those defined in Article DELAYS AND EXTENSION OF TIME, the CONTRACTOR shall notify the ENGINEER, in writing, of his intention to make claim for such time or compensation before he begins the work on which he bases the claim, in order that such matters may be settled, if possible, or other appropriate action taken. The notice of claim shall be in duplicate, in writing, and shall state the circumstances and the reasons for the claim, but need not state the amount. If such notification is not given or if the ENGINEER is not afforded proper facilities by the CONTRACTOR for keeping strict account of actual cost, then the CONTRACTOR hereby agrees to waive the claim for such additional time or compensation. Such notice by the CONTRACTOR, and fact that the ENGINEER has kept account of the cost as aforesaid, shall not in any way be construed as proving the validity of the claim.

No extension of time will be granted to the CONTRACTOR for delays resulting from extra work that have no measurable impact on the completion of the total Work under this Contract. Claims for additional time or compensation shall be made in itemized detail and submitted, in writing, to the OWNER and ENGINEER within 10 days following completion of that portion of the work for which the CONTRACTOR bases his claim. Failure to make the claim for additional compensation in the manner and within the time specified above shall constitute waiver of that claim. In case the claim is found to be just, it shall be allowed and paid for as provided in Article PAYMENT FOR CHANGE ORDERS.

71. RELEASE OF LIENS OR CLAIMS

The CONTRACTOR shall indemnify and hold harmless the OWNER from all claims for labor and materials furnished under this Contract. Prior to the final payment, the CONTRACTOR shall furnish to the OWNER, as part of his final payment request, a certification that all of the CONTRACTOR's obligations on the Project have been satisfied and that all monetary claims and indebtedness have been paid. The CONTRACTOR shall furnish complete and legal effective releases or waivers, satisfactory to the OWNER, of all liens arising out of or filed in connection with the work.

72. FINAL PAYMENT

Upon completion of all the work under this Contract, the CONTRACTOR shall notify the ENGINEER, in writing, that he has completed his part of the Contract and shall request final payment. Upon receipt of such notice the ENGINEER will inspect and, if acceptable, submit to the OWNER his recommendation as to acceptance of the completed work and as to the final estimate of the amount due the CONTRACTOR. Upon approval of this final estimate by the OWNER and compliance by the CONTRACTOR with provisions in Article RELEASE OF LIENS OR CLAIMS, and other provisions as may be applicable, the OWNER shall pay to the CONTRACTOR all monies due him under the provisions of these Contract Documents.

73. NO WAIVER OF RIGHTS

Neither the inspection by the OWNER, through the ENGINEER or any of his employees, nor any order by the OWNER for payment of money, nor any payment for, or acceptance of, the whole or any part of the work by the OWNER or ENGINEER, nor any extension of time, nor any possession taken by the OWNER or its employees, shall operate as a waiver of any provision of this Contract, or any power herein reserved to the OWNER, or any right to damages herein provided, nor shall any waiver of any breach in this Contract be held to be a waiver of any other or subsequent breach. Acceptance or final payment shall not be final and conclusive with regards to latent defects, fraud, or such gross mistakes as may amount to fraud, or as regards the OWNER's rights under the warranty.

74. ACCEPTANCE OF FINAL PAYMENT CONSTITUTES RELEASE

The acceptance by the CONTRACTOR of the final payment shall release the OWNER and the ENGINEER, as representatives of the OWNER, from all claims and all liability to the CONTRACTOR for all things done or furnished in connection with the work, and every act of the OWNER and others relating to or arising out of the work except claims previously made in writing and still unsettled. No payment, however, final or otherwise, shall operate to release the CONTRACTOR or his Sureties from obligations under this Contract and the Performance Bond, Payment Bond, and other bonds and warranties, as herein provided.

SUPPLEMENTARY CONDITIONS

The General Conditions are hereby revised as follows:

ARTICLE 9 "ENGINEER"

Add the following:

Wherever in these Documents the word "Engineer" appears, it shall be understood to mean the City of Key West, Director, Port & Marine Services or authorized representatives.

ARTICLE 12 "OWNER"

Add the following:

Wherever in these Documents the word "Owner" appears, it shall be understood to mean the City of Key West whose address is 1300 White Street, Key West, Florida 33040.

ARTICLE 32 "CONTRACTOR, AN INDEPENDENT AGENT"

Add the following:

Assignment of any part or the whole of this Contract shall be subject to review and approval of the City Commission.

ARTICLE 34 "INSURANCE AND LIABILITY"

Delete Article 34 Sections A, B, C, D & E and replace with the following:

CONTRACTOR is to secure, pay for, and file with the City of Key West, prior to commencing any work under the Contract, all certificates for workers' compensation, public liability, and property damage liability insurance, and such other insurance coverages as may be required by specifications and addenda thereto, in at least the following minimum amounts with specification amounts to prevail if greater than minimum amounts indicated. Notwithstanding any other provision of the Contract, the CONTRACTOR shall provide the minimum limits of liability insurance coverage as follows:

Type of Insurance	Limits	Comments
Commercial General Liability	\$1,000,000	The proposers may have these coverages combined in 1 policy
Watercraft Liability	\$1,000,000	
Business Automobile Liability	\$1,000,000	
Workers' Compensation	Statutory	
Employers Liability	\$1,000,000/\$1,000,000/\$1,000,000	
USL&H and Jones Act Coverage	\$1,000,000	

CONTRACTOR shall furnish an original Certificate of Insurance indicating, and such policy providing coverage to, City of Key West named as an additional insured on a PRIMARY and NON CONTRIBUTORY basis utilizing an ISO standard endorsement at least as broad as CG 2010 (11/85) or its equivalent, (combination of CG 20 10 07 04 and CG 20 37 07 04, providing coverage for completed operations, is acceptable) including a waiver of subrogation clause in favor of City of Key West on all policies. CONTRACTOR will maintain the General Liability and Umbrella Liability insurance coverages summarized above with coverage continuing in full force including the additional insured endorsement until at least 3 years beyond completion and delivery of the work contracted herein.

Notwithstanding any other provision of the Contract, the CONTRACTOR shall maintain complete workers' compensation coverage for each and every employee, principal, officer, representative, or agent of the CONTRACTOR who is performing any labor, services, or material under the Contract. Further, CONTRACTOR shall additionally maintain the following minimum limits of coverage:

Bodily Injury Each Accident	\$1,000,000
Bodily Injury by Disease Each Employee	\$1,000,000
Bodily Injury by Disease Policy Limit	\$1,000,000

The City of Key West confirms that the scope of services specified in the Contract requires work on or near a navigable waterway. Water description: City of Key West Mooring Field. Therefore the CONTRACTOR's workers' compensation policy shall be endorsed to provide the following:

- Workers Compensation/Employer Liability
USL&H Coverage (Longshore and Harbor Workers' Compensation Act) Endorsement WC 000106A
Jones Act Coverage* Endorsement WC 000201A

Note: Jones Act (Crew) coverage may be provided under the P&I policy, if Contractor is using an OWNED vessel during the course of the work.

CONTRACTOR shall provide the City of Key West with a Certificate of Insurance verifying compliance with the workman's compensation coverage as set forth herein and shall provide as often as required by the City of Key West such certification which shall also show the insurance company, policy number, effective and expiration date, and the limits of workman's compensation coverage under each policy.

CONTRACTOR's insurance policies shall be endorsed to give 30 days written notice to the City of Key West in the event of cancellation or material change, using form CG 02 24, or its equivalent.

Certificates of Insurance submitted to the City of Key West will not be accepted without copies of the endorsements being requested. This includes additional insured endorsements, cancellation/material change notice endorsements, and waivers of subrogation. Copies of USL&H Act and Jones Act endorsements will also be required if necessary. PLEASE ADVISE YOUR INSURANCE AGENT ACCORDINGLY.

CONTRACTOR will comply with any and all safety regulations required by any agency or regulatory body including but not limited to OSHA. CONTRACTOR will notify City of Key West immediately by telephone at (305) 809-3811 any accident or injury to anyone that occurs on the jobsite and is related to any of the work being performed by the CONTRACTOR.

Add the following Section:

G. SURETY AND INSURER QUALIFICATIONS

All bonds, insurance contracts, and certificates of insurance shall be either executed by or countersigned by a licensed resident agent of the Surety or insurance company, having his place of business in the State of Florida, and in all ways complying with the insurance laws of the State of Florida. Further, the said Surety or insurance company shall be duly licensed and qualified to do business in the State of Florida.

ARTICLE 35 "INDEMNITY"

Delete Article 35 in its entirety and replace with the following:

INDEMNITY

To the fullest extent permitted by law, the CONTRACTOR expressly agrees to indemnify and hold harmless the City of Key West, their officers, directors, agents and employees (herein called the "indemnitees") from liabilities, damages, losses and costs, including but not limited to, reasonable attorney's fees and court costs, such legal expenses to include costs incurred in establishing the indemnification and other rights agreed to in this Paragraph, to persons or property, to the extent caused by the negligence, recklessness, or intentional wrongful misconduct of the CONTRACTOR, its Subcontractors or persons employed or utilized by them in the performance of the Contract. Claims by indemnitees for indemnification shall be limited to the amount of CONTRACTOR's insurance or \$1 million per occurrence, whichever is greater. The parties acknowledge that the amount of the indemnity required hereunder bears a reasonable commercial relationship to the Contract and it is part of the project specifications or the bid documents, if any.

The indemnification obligations under the Contract shall not be restricted in any way by any limitation on the amount or type of damages, compensation, or benefits payable by or for the CONTRACTOR under Workers' Compensation acts, disability benefits acts, or other employee benefits acts, and shall extend to and include any actions brought by or in the name of any employee of the CONTRACTOR or of any third party to whom CONTRACTOR may subcontract a part or all of the Work. This indemnification shall continue beyond the date of completion of the work.

ARTICLE 39 "CODES, ORDINANCES, PERMITS, AND LICENSES"

Add the following:

A. NOISE ORDINANCE

City of Key West has a noise ordinance that allows working hours between 8:00 AM to 7:00 PM, Monday through Friday. No work should be performed during weekends or City Holidays, State Holidays and National Holidays. Any construction operations outside these hours and these days will require a variance from the City of Key West Commission.

B. "LICENSES"

Within 10 days of Notice of Award, the successful Bidder must represent that he holds all applicable state, county, and City of Key West licenses and permits required to do business as a contractor with respect to the work described in the Contract Documents.

Further, the successful Bidder must, within 10 days of Notice of Award, furnish documentation showing that, as a minimum, he has complied with the provisions of Chapter 18 of the Code of Ordinances of the City of Key West in order to enter into the Agreement contained in the Contract Documents.

Specifically, within 10 days after Notice of Award, the successful Bidder must demonstrate that he holds, as a minimum, the following licenses and certificates:

1. City of Key West, Engineering Contractor Class I license.
2. Holds a valid occupational license issued by the City of Key West.

ARTICLE 42 "SAFETY"

Add the following sub article:

OCCUPATIONAL SAFETY AND HEALTH

The Contractor shall observe and comply with all applicable local, state, and federal occupational safety and health regulations during the prosecution of work under this Contract. In addition, full compliance by the Contractor with the U.S. Department of Labor's Occupational Safety and Health Standards, as established in Public Law 91-596, will be required under the terms of this Contract.

ARTICLE 43 "PROTECTION OF WORK AND PROPERTY"

Add the following Article:

HISTORIC PRESERVATION

The Contractor shall comply with Florida's Archives and Historic Act (Florida Statutes, Chapter 267) and the regulations of the local historic preservation board as applicable and protect against the potential loss or destruction of significant historical or archaeological data, sites, and properties in connection with the project.

ARTICLE 45 "MATERIALS AND APPLIANCES"

Add the following to the end of the first paragraph:

At contract completion, no equipment purchased by the contractor shall be transferred to state or local ownership.

ARTICLE 57 "OWNERS RIGHT TO TRANSFER EMPLOYMENT"

Add the following Article:

TERMINATION FOR CONVENIENCE AND RIGHT OF SUSPENSION

- A. Owner shall have the right to terminate this Contract without cause by written notice of Termination to the Contractor. In the event of such termination for convenience, the Contractor's recovery against the Owner shall be limited to that portion of the Contract amount earned through the date of termination, together with any retainage withheld and reasonable termination expenses incurred. Contractor shall not be entitled to any other or further recovery against the Owner, including, but not limited to, damages or any anticipated profit on portions of the Work not performed.
- B. Owner shall have the right to suspend all or any portions of the Work upon giving the Contractor prior written notice of such suspension. If all or any portion of the Work is so suspended, the Contractor shall be entitled to reasonable costs, expenses and time extension associated with the suspension.

ARTICLE 60 "LIQUIDATED DAMAGES"

Delete Article "LIQUIDATED DAMAGES" in its entirety and substitute the following:

LIQUIDATED DAMAGES

Should the Contractor fail to complete the work or any part thereof in the time agreed upon in the Contract Documents or within such extra time as may have been allowed for delays by extensions granted as provided in the Contract, the Contractor shall reimburse the Owner for the additional expense and damage for each calendar day, Sundays and legal holidays included, that project outlined in Contract Documents remains uncompleted after the completion date. Liquidated damages shall be assessed. It is agreed that the amount of such additional expense and damage incurred by reason of failure to complete the work is the per diem rate as stipulated in the Proposal. The said amount is hereby agreed upon as a reasonable estimate of the costs which may be accrued by the Owner after the expiration of the time of completion. It is expressly understood and agreed that this amount is not to be considered in the nature of a penalty but as liquidated damages, which have accrued against the Contractor. The Owner shall have the right to deduct such damages from any amount due or that may become due the Contractor or the amount of such damages shall be due and collectible from the Contractor or Surety.

ARTICLE 69 "PARTIAL PAYMENTS"

Delete the first paragraph of Article "PARTIAL PAYMENTS" and substitute the following:

No more than once each month the Contractor shall submit to the Engineer a detailed estimate of the amount earned during the preceding month for the separate portions of the work and request payment. As used in this Article the words "amount earned" means the value, on the date of the estimate, for partial payment of the work completed in accordance with the Contract Documents and the value of approved materials delivered to the project site suitably stored and protected prior to incorporation into the work

Add the following:

Payment will be made by the Owner to the Contractor within 40 days receipt of the written recommendation of payment from the Engineer.

Delete Sub-Article C "DEDUCTION FROM ESTIMATE" in its entirety and substitute the following:

DEDUCTION FROM ESTIMATE

The Owner will deduct from the estimate and retain as part security 10 percent of the amount earned for work satisfactorily completed. A deduction and retainage of 10 percent will be made on the estimated amount earned for approved items of material delivered to and properly stored at the jobsite but not incorporated into the work.

Delete Sub-Article E "PAYMENT" in its entirety and substitute the following:

PAYMENT

After deducting the retainage and the amount of all previous partial payments made to the Contractor from the amount earned the amount due will be made payable to the Contractor. Recommendations for payment received by the Owner less than 40 days prior to the scheduled day for payment will not be processed or paid until the following month.

ARTICLE 72 "FINAL PAYMENT"

Add the following;

A. Acceptance and Final Payment.

Whenever the Contractor has completely performed the work provided for under the Contract and the Engineer has performed a final inspection and made final acceptance and subject to the terms of the Engineer will prepare a final estimate showing the value of the work as soon as the Engineer makes the necessary measurements and computations. The Engineer will correct all prior estimates and payments in the final estimate and payment. The OWNER will pay the estimate, less any sums that the OWNER may have deducted or retained under the provisions of the Contract, as soon as practicable after

final acceptance of the work, provided the Contractor has met the requirements of (1) through (6) below.

- 1 The Contractor has agreed in writing to accept the balance due or refund the overpayment, as determined by the OWNER, as full settlement of his account under the Contract and of all claims in connection therewith, or the Contractor, accepted the balance due or refunded the overpayment, as determined by the OWNER, with the stipulation that his acceptance of such payment or the making of such refund does not constitute any bar, admission, or estoppel, or have any effect as to those payments in dispute or the subject of a pending claim between the Contractor and the OWNER. To receive payment based on a FINAL PAYMENT CERTIFICATE, The Contractor further agrees, by submitting a FINAL PAYMENT CERTIFICATE that any pending or future arbitration claim or suit is limited to those particulars, including the itemized amounts, defined in the original FINAL PAYMENT CERTIFICATE , and that he will commence with any such arbitration claim or suit within 15 calendar days from and after the time of final PAYMENT of the work and that his failure to file a formal claim within this period constitutes his full acceptance of the Engineer's final estimate and payment. The overpayment refund check from the Contractor, if required, will be considered a part of any Acceptance Letter executed.
- 2 The Contractor has properly maintained the project, as specified hereinbefore.
- 3 The Contractor has furnished a sworn affidavit to the effect that the Contractor has paid all bills and no suits are pending (other than those exceptions listed, if any) in connection with work performed under the Contract and that the Contractor has not offered or made any gift or gratuity to, or made any financial transaction of any nature with, any employee of the OWNER in the performance of the Contract.
- 4 The surety on the contract bond consents, by completion of their portion of the affidavit and surety release subsequent to the Contractor's completion of his portion, to final payment to the Contractor and agrees that the making of such payment does not relieve the surety of any of its obligations under the bond.
- 5 The Contractor has furnished all required mill tests and analysis reports to the Engineer.
- 6 The Contractor has furnished as-built drawings in AutoCad and Adobe PDF, in accordance with all supplied data collections and files to be compatible with Esri ArcGIS 10.2.2 Software. The current computing environment consists of:

- Microsoft SQL Server
- Windows 7/Server 2008
- ESRI GIS Platform

Interfaces and Integrations

* * * *

PART 4

SPECIFICATIONS

**SECTION 01001
GENERAL REQUIREMENTS**

PART 1 - GENERAL

1.01 GENERAL

A. The Work under this Contract shall be performed by the Contractor as required by the City. Work will be authorized in the form of a Notice to Proceed issued to the Contractor. The Contractor shall complete all Work in the Contract within the number of calendar days stipulated in the Contract, unless an extension in the time of completion is granted by the City. Upon completion of the Work and compliance with applicable provisions in the Contract Documents, the Contractor will receive final payment for all Work done.

B. Contractor's Duties:

1. In addition to provisions stipulated in other portions of the Contract Documents, Contractor shall secure permits as necessary for proper execution and completion of the work.
2. Contractor shall be totally responsible for all permits required and shall ensure that construction complies with all applicable local, state, and federal codes.
3. Provide an experienced, qualified, and competent Superintendent to oversee the Work. Superintendent shall be expected to remain for the duration of the Project.

1.02 MOBILIZATION AND DEMOBILIZATION

CONTRACTOR shall be responsible for mobilization and demobilization of labor, materials and equipment. Payment for mobilization and demobilization will be included in the lump sum price indicated in the BID.

1.03 CONTRACTOR'S USE OF PREMISES

- A. Work shall be scheduled as to not interfere with on-going area activities.
- B. Coordinate use of premises and requirements with the City.
- C. Assume full responsibility for the protection and safekeeping of products under this Contract, stored on the site.
- E. Contractor shall provide drinking water for construction personnel.
- F. Contractor shall provide waste solutions for construction personnel.

1.04 FINISHING OF SITE AND STORAGE AREAS

Upon completion of the Project, all areas used by the Contractor shall be properly cleared of all temporary structures, rubbish, and waste materials and properly graded to drain and blend in with the abutting property. Areas used for the deposit of waste materials shall be finished to properly drain and blend with the surrounding terrain.

PART 2 - TEMPORARY CONSTRUCTION UTILITIES AND FACILITIES

2.1 TEMPORARY WATER

CONTRACTOR shall make his own arrangements to obtain suitable water and shall pay all costs.

2.2 SANITARY FACILITIES (not applicable)

CONTRACTOR shall provide and maintain sanitary facilities for his employees and his subcontractors' employees that will comply with the regulations of local and state departments of health, and as directed by the City.

2.3 STORAGE OF MATERIALS

A. Materials shall be so stored as to ensure the preservation of their quality and fitness for the work. When considered necessary, materials shall be placed on wooden platforms or other hard, clean surfaces, not on the ground.

PART 3 - PRESERVATION, RESTORATION, AND CLEANUP

3.1 SITE RESTORATION AND CLEANUP

At all times during the work keep the premises clean and orderly. Upon completion of the day's work, repair all damage caused by equipment and leave the project clean and free of rubbish or excess materials of any kind.

Stockpile excavated materials in a manner that will cause the least damage to the area and near shore waters.

Upon completion of the Work, all areas used by the Contractor shall be cleared of temporary structures, rubbish, and waste materials, and properly graded to finished surface similar to the original surface, free-draining and free from holes, ruts, rough spots, leaving the area like original condition.

* * * * *

SECTION 01010 SCOPE OF WORK

The Carolina Street Corridor and Bahama Village Community Redevelopment Agency (CRA) of the City of Key West requests proposals from qualified individuals or firms for wood dock repair and piling replacement. The project contemplated consists of providing all materials, equipment and labor necessary to accomplish the following at the Key West Historic Seaport:

The project includes the removal, disposal and replacement of wooden pilings, 3x8 horizontal timbers, (6) 3x8 diagonal timbers and stainless-steel hardware assemblies as shown in the supplemental information portion of this document. The project also includes, but is not limited to, the following:

- Removal/ replacement of existing 2 x 6 composite wood decking on as necessary to complete timber replacement (incidental to work).
- Removal and disposal of all hardware associated with wood removal,
- Removal and reinstallation existing pile caps, rub rails and bumpers.
- Re-hang electrical & plumbing conduit as needed (incidental to work).
- Hurricane hanger/strap replacement, if necessary for repairs, shall be Simpson Strong-Tie (incidental to work).
- All connections / hardware shall be heavy duty for marine environment conditions.
- All piles embedded 10' minimum into caprock.
- Pile cut-off elevation shall be based on surrounding piles +/- 2-3 inches. Treat cut surfaces in accordance with AWPA M4.
- Treat field cuts, holes, and other pile penetrations with field applied wood preservative, in accordance with AWPA M4.
- Deviation from and angle of batter: ¼ inch per foot of pile length, but no greater than 6 inches.
- Maximum deviation from location of pile top is 6 inches.
- Obtain & pay for all City permits required for the project.
- Comply with all conditions of the ACOE & FDEP permits.

All piles to be southern yellow pine, Wolmanized CCA treated marine grade, 2.50pcf in accordance with AWPA C3 and C18 marine pile. All piles to conform with ASTM D 25, be unused, clean peeled, uniformly tapered, one piece from butt to tip.

All wood members shall be marine lumber CCA treated, 2.50pcf, in accordance with AWPA C3 and C18.

D-Dock is currently a functional pier and must remain so during the construction process. During construction the contractor shall minimize the length of dock that must be closed and coordinate relocation of boats with Seaport Dockmaster.

Bidder shall include in bid a detailed construction sequence narrative explaining how the submitting bidder intends to conduct the work including coordinating of any utilities that may

have to be rerouted or removed and reinstalled. All work required shall be included in the lump sum bid.

The intent of these Documents is to describe a functionally complete project (or part thereof) to be constructed in accordance with the Contract Documents. Any work, materials, or equipment that may reasonably be inferred from the Contract Documents, as being required to produce the intended result shall be supplied whether or not specifically called for.

END OF SECTION

**SECTION 01025
MEASUREMENT AND PAYMENT**

1.1 GENERAL

- A. Contractor shall receive and accept compensation as provided in the Bid and Contract in full payment for performing all operations necessary to complete the work under the Lump Sum portions of this Contract, and also in full payment for all loss or damages arising from the nature of the work, until the final acceptance by the City.

- B. Contractor's attention is called to the fact that the quotations for various items of work are intended to establish a total price for completing the work in its entirety. It is the intent of this Contract that the Contractor provide a completed structure, and any item required to accomplish this shall be included to establish a total cost.

1.2 PAYMENT

- A. Payment for all Work as ordered or specified in the Contract Documents is included in the Contract Price.

1.4 NONPAYMENT FOR REJECTED OR UNUSED PRODUCTS

Payment will not be made for following:

- 1. Defective Work not accepted by the City.

1.5 PARTIAL PAYMENT FOR STORED MATERIALS AND EQUIPMENT

- A. Partial Payment: No partial payments will be made for materials and equipment delivered or stored unless Shop Drawings are acceptable to the City and materials are properly stored at a site as agreed to by the City.

- B. Final Payment: Will be made only for products incorporated in Work. Products for which partial payments have been made will be deducted from final payment.

**SECTION 01300
SUBMITTALS**

PART 1 GENERAL

1.01 GENERAL

- A. Inquiries: Direct to ENGINEER regarding procedure, purpose, or extent of Submittal.
- B. Submittal Submission Procedures: As provided in General Conditions, as specified herein, and as may otherwise be established during the preconstruction conference.
- C. OWNER's Authorization: At any time, OWNER may authorize changes to procedures and requirements for Submittals, as necessary to accomplish specific purpose of each Submittal. Such authorization will be by Field Order or Work Change Directive.
- D. Timeliness: Make submissions in such sequence as to cause no delay in Work or in work of other contractors.
- E. Identification of Submittals:
 - 1. Identify each Submittal with numbering and tracking system reviewed by ENGINEER:
 - a. Sequentially number each Submittal.
 - b. Resubmission of a Submittal will have original number with sequential alphabetic suffix.
 - 2. Show date of submission and dates of previous submissions.
 - 3. Show Project title and OWNER's contract identification and contract number.
 - 4. Show names of CONTRACTOR, Subcontractor or Supplier, and manufacturer as appropriate.
 - 5. Clearly identify revisions from previous submissions.
- F. Incomplete Submittal Submissions:
 - 1. At ENGINEER's sole discretion, ENGINEER will either (i) return the entire Submittal for CONTRACTOR's revision/correction and resubmission, or (ii) retain portions of the Submittal and request submission/resubmission of specified items or as noted thereon.
 - 2. Submittals which do not clearly bear CONTRACTOR's specific written indication of CONTRACTOR review and approval of Submittal will be returned to CONTRACTOR unreviewed for resubmission in accordance with Contract Documents.
 - 3. Delays, resequencing or other impact to Work resulting from CONTRACTOR's submission of unchecked or unreviewed, incomplete, inaccurate or erroneous, or nonconforming Submittals, which will require CONTRACTOR's resubmission of

a Submittal for ENGINEER's review, shall not constitute a basis of claim for adjustment in Contract Price or Contract Times.

- F. Non-specified Submissions: Submissions not required under these Contract Documents and not shown on schedule of Submittals submissions will not be reviewed and will be returned to CONTRACTOR.
- G. Transmit Submittals in accordance with current accepted schedule of Submittal submissions, and deliver as follows:
 - 1. Submittals to: Key West Historic Seaport, Deputy Port and Marine Services Director.
- H. Disposition of Submittals: As specified herein for administrative Submittals. ENGINEER will review, stamp, and indicate requirements for resubmission or acceptance on Submittal as follows:
 - 1. Reviewed as Noted:
 - a. Reference the General Conditions for intent.
 - b. CONTRACTOR may proceed to perform Submittal related Work.
 - c. One copy for ENGINEER's file.
 - d. One copy returned to CONTRACTOR.
 - 2. Revise and Resubmit (Revise/Correct or Develop Replacement and Resubmit):
 - a. Revise/correct in accordance with ENGINEER's comments and resubmit.
 - b. One copy to ENGINEER's file.
 - c. One copy returned to CONTRACTOR appropriately annotated.
- I. ENGINEER's Review: ENGINEER will act upon CONTRACTOR's Submittal and transmit response to CONTRACTOR not later than 30 days after receipt, unless: (i) specified otherwise or (ii) accepted by ENGINEER and identified on current accepted schedule of Submittals submissions. Re-submittals will be subject to the same review time.

1.02 SHOP DRAWINGS

- A. Description: Reference the General Conditions.
- B. Excessive Shop Drawing Review: Review of the first submission and two resubmissions of Shop Drawings will be performed by ENGINEER at no cost to CONTRACTOR. Subsequent additional resubmissions of that Shop Drawing will be reviewed by ENGINEER, however, ENGINEER will document work hours and other expenses required to perform such additional review(s). OWNER shall deduct these costs from Contractor's contract for reimbursement to the ENGINEER.
- C. Copies: Submit two (2) copies.

D. Submit Shop Drawings to ENGINEER for equipment and materials to be furnished under these Contract Documents.

E. Identify and Indicate:

1. Pertinent products, units and assemblies, and system or equipment identification or tag numbers.
2. Critical field dimensions and relationships to other critical features of Work.
 - a. Each deviation or variation from Contract Documents.

F. Resubmissions: Clearly identify each correction or change made.

G. Foreign Manufacturers: When proposed, include following additional information:

1. Names and addresses of at least two companies closest to Project that maintain technical service representatives.
2. Complete inventory of spare parts and accessories for each piece of equipment.

H. Preparation:

1. Format: Whenever possible, schedule for and combine Shop Drawings into a single Submittal package.
2. Present in a clear and thorough manner and of sufficient detail to show kind, size, arrangement, and function of components, materials, and devices and compliance with Contract Documents.

PART 4 PAYMENT

A. Payment for the work in this section will be incidental

**SECTION 01700
CONTRACT CLOSEOUT**

PART 1 - GENERAL

1.01 REQUIREMENTS

Contract completion includes substantial completion, final inspection after completion, final cleaning, contractor's closeout submittals, and final adjustment of accounts.

1.02 SUBSTANTIAL COMPLETION

A. When Contractor considers work has reached substantial completion, he shall submit to the OWNER the following:

a. Written notice that the work is substantially complete in accordance with Contract Documents.

b. A list of items yet to be completed or corrected and explanations thereof.

B. Within a reasonable time upon receipt of such notice, the OWNER will make an inspection, if necessary, to determine the status of completion.

C. Should the OWNER determine that the work is not substantially complete:

a. The OWNER will promptly notify the Contractor in writing, giving the reasons thereof.

b. Contractor shall remedy the deficiencies in the work and send a second written notice of Substantial Completion to the OWNER.

c. Upon receipt of the second notice, the OWNER will review the work.

D. When the OWNER finds that the Work is substantially complete he will issue a Certificate of Substantial Completion with a tentative list of items to be completed or corrected before final inspection.

1.03 FINAL INSPECTION AFTER COMPLETION

A. When Contractor considers the Work is complete with all minor deficiencies completed or corrected, he shall submit written certification that:

a. Contract Document requirements have been met.

- b. Work has been inspected for compliance with Contract Documents.
 - c. Work has been completed in accordance with Contract Documents.
 - d. All minor deficiencies have been corrected or completed and the Work is ready for final inspection.
 - e. Project record documents are complete and submitted.
- B. Within a reasonable time upon receipt of such certification, the OWNER will make an inspection to verify the status of completion.
- C. Should the OWNER determine that the work is incomplete or defective:
- a. The OWNER will promptly notify the Contractor in writing, listing the incomplete or defective work.
 - b. Contractor shall remedy the deficiencies in the work and send a second written certification to the OWNER that the work is complete.
 - c. Upon receipt of the second certification, the OWNER will review the Work.
- D. When the OWNER determines that the work is acceptable, under the Contract Documents, he shall request the Contractor to make closeout submittals.

1.04 FINAL CLEANING

- A. Execute final cleaning prior to final inspection.
- B. Remove waste and surplus materials, rubbish, and construction facilities from the Project and from the site.

1.05 CONTRACTOR'S CLOSEOUT SUBMITTALS

- A. Project Record Documents
 - a. At Contract Closeout, submit documents with transmittal letter containing date, project title, Contractor's name and address, list of documents, and signature of Contractor.
 - b. Changes made by Field Order or by Change Order.
- B. Evidence of payment and Release of Liens.

1.06 FINAL ADJUSTMENT OF ACCOUNTS

- A. Submit a final statement of accounting to the OWNER.
- B. Statement shall reflect all adjustments to the Contract Sum.
 - a. The original Contract sum.

- b. Additions and deductions resulting from:
 - Previous change orders or written amendment.
 - Allowances
 - Unit prices
 - Deductions for uncorrected work.
 - Deductions for liquidated damages
 - Other adjustments
- c. Total contract sum as adjusted
- d. Previous payments
- e. Sum remaining due

PART 5

SUPPLEMENTAL INFORMATION

MATERIALS LIST

Component	Size	Qty	Location/Note (if needed)	
Dock D	14" DIA Pile	-	58	(see map)
	3x8 Horizontal Timber	11'	2	@ D-8,10
	3x8 Diagonal Timber	13'	6	@ D-22,23,29,31,44,101
	26" SS All-thread Assy. w/ x2 Nuts and Washers	1/2" D	79	x78 Galvanized equipment replacements + x1 add'l missing nut/washer
	SS Epoxy Anchor Bolts for BH	1/2" D	4	x4 Galvanized equipment at Bulkhead

PLANS, REPAIR LEGEND AND PHOTOGRAPHS



DOCK D												
	Pile Condition		Horizontal Member		H-Hardware		Diagonal Member		D-Hardware		Misc.	Notes
D-1	OK	-	NA	-	NA	-	NA	-	NA	-	-	
D-2	OK	"s"	NA	-	NA	-	NA	-	NA	-	-	Pile shaved
D-3	OK	-	NA	-	NA	-	NA	-	NA	-	-	
D-4	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-5	OK	-	OK	Note	GA CO	-	NA	-	NA	-	-	A second board was nailed on but has become disconnected
D-6	Poor	Note	OK	Note	GA CO	-	NA	-	NA	-	-	Pile shaved approximately 1-1/2"/rotting; Second board nailed
D-7	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-8	OK	-	Poor	Note	GA SC	-	NA	-	NA	-	-	Horizontal member splitting at edge
D-9	Poor	"s"	OK	-	GA CO	-	NA	-	NA	-	-	Pile shaved approximately 1-1/2"
D-10	OK	-	Poor	Note	GA SC	-	NA	-	NA	-	-	Horizontal member splitting
D-11	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-12	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-13	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-14	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-15	OK	-	OK	-	GA CO	-	NA	-	NA	-	-	
D-16	OK	-	OK	-	SS OK	-	NA	-	NA	-	-	
D-17	OK	-	OK	-	SS OK	-	OK	-	SS OK	Note	-	SS hardware missing nut/washer
D-18	OK	-	OK	-	SS OK	-	NA	-	NA	-	-	
D-19	Rot	Note	OK	-	SS OK	Note	OK	-	SS OK	-	-	Pile rotting at waterline; SS hardware loose
D-20	Rot	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile rotting at waterline
D-21	Rot	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile rotting at waterline
D-22	Rot	Note	OK	-	SS OK	-	Rot	Note	SS OK	-	-	Pile rotting at waterline; Diagonal member bottom rotting
D-23	Rot	Note	OK	-	SS OK	-	Rot	Note	SS OK	-	-	Pile heavily rotting at waterline and splitting at top; Diagonal member bottom rotting
D-24	Poor	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile starting to rot at waterline
D-25	Rot	Note	OK	-	SS OK	-	OK	-	OK	-	-	Pile heavily rotting at waterline
D-26	OK	-	OK	-	SS OK	-	NA	-	NA	-	-	
D-27	OK	-	OK	-	SS OK	-	OK	-	SS OK	-	-	
D-28	OK	-	OK	-	SS OK	-	NA	-	NA	-	-	
D-29	Rot	Note	OK	-	SS OK	-	Poor	Note	CO	Note	-	Pile heavily rotting at waterline; Diagonal bottom rotting; Hardware in water corroded
D-30	OK	-	OK	-	SS OK	-	NA	-	NA	-	-	
D-31	OK	-	OK	-	SS OK	-	Poor	Note	CO	Note	-	Diagonal member bottom rotting; Hardware in water corroded
D-32	Poor	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile starting to rot at waterline; top of pile splitting
D-33	OK	-	OK	-	SS OK	-	OK	-	CO	Note	-	Hardware in water corroded
D-34	Poor	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile starting to rot at waterline
D-35	Rot	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile rotting at waterline
D-36	OK	-	OK	-	SS OK	-	NA	-	NA	-	-	
D-37	Poor	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile starting to rot at waterline
D-38	OK	-	OK	-	SS OK	-	NA	-	NA	-	-	
D-39	Rot	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile heavily rotting at waterline
D-40	Rot	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile rotting at waterline
D-41	Rot	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile heavily rotting at waterline
D-42	Poor	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile starting to rot at waterline
D-43	Rot	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile rotting at waterline
D-44	Rot	Note	OK	-	SS OK	-	Poor	Note	SS OK	-	-	Pile heavily rotting at waterline; Diagonal member bottom rotting
D-45	OK	-	OK	-	SS OK	-	NA	-	NA	-	-	
D-46	OK	-	OK	-	SS OK	-	OK	-	SS OK	-	-	
D-47	OK	-	OK	-	SS OK	-	NA	-	NA	-	-	
D-48	OK	-	OK	-	SS OK	-	OK	-	SS OK	-	-	
D-49	Poor	"s"	OK	-	SS OK	Note	NA	-	NA	-	-	Pile shaved approximately 2-1/2"; x1 SS hardware nut/washer missing to boardwalk
D-50	Poor	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile starting to rot at waterline
D-51	Rot	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile heavily rotting at waterline
D-52	Poor	Note	NA	-	NA	-	NA	-	NA	-	-	Pile starting to rot at waterline/top of pile badly split
D-53	Rot	Note	NA	-	NA	-	NA	-	NA	-	-	Pile heavily rotting at waterline/top of pile badly split
D-54	OK	"s"	NA	-	NA	-	NA	-	NA	-	-	
D-55	OK	"s"	NA	-	NA	-	NA	-	NA	-	-	
D-56	OK	-	OK	-	SS OK	Note	NA	-	NA	-	-	x2 additional GA hardware corroded
D-57	OK	-	OK	-	SS OK	-	OK	-	SS OK	-	-	
D-58	Rot	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile rotting at waterline
D-59	Poor	"s"	NA	-	NA	-	NA	-	NA	-	-	Pile shaved approximately 1" (thin pile)
D-60	OK	"s"	NA	-	NA	-	NA	-	NA	-	-	
D-61	Rot	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile heavily rotting at waterline
D-62	OK	-	OK	-	GA SC	Note	NA	-	NA	-	-	x1 SS OK, x1 GA hardware does not go through
D-63	OK	"s"	NA	-	NA	-	NA	-	NA	-	-	

DOCK D												
	Pile Condition		Horizontal Member		H-Hardware		Diagonal Member		D-Hardware		Misc.	Notes
D-64	Rot	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile heavily rotting at waterline
D-65	OK	-	OK	-	SS OK	-	NA	-	NA	-	-	
D-66	OK	"s"	NA	-	NA	-	NA	-	NA	-	-	
D-67	Rot	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile heavily rotting at waterline
D-68	Rot	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile heavily rotting at waterline; top of pile splitting
D-69	OK	-	NA	-	NA	-	NA	-	NA	-	-	
D-70	Rot	Note	OK	-	SS OK	-	OK	-	CO	Note	-	Pile rotting at waterline; Hardware is corroded or missing
D-71	OK	"s"	NA	-	NA	-	NA	-	NA	-	-	
D-72	Rot	Note	OK	-	SS OK	-	OK	-	GA CO	-	-	Pile rotting at waterline
D-73	Rot	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile heavily rotting at waterline
D-74	OK	"s"	NA	-	NA	-	NA	-	NA	-	-	
D-75	Rot	Note	OK	-	SS OK	-	OK	-	GA CO	-	-	Pile rotting at waterline
D-76	OK	"s"	NA	-	NA	-	NA	-	NA	-	-	
D-77	Rot	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile rotting at waterline
D-78	Poor	Note	OK	-	SS OK	-	OK	-	GA CO	-	-	Pile starting to rot at waterline
D-79	OK	-	NA	-	NA	-	NA	-	NA	-	-	
D-80	Rot	Note	OK	-	SS OK	Note	NA	-	NA	-	-	Pile rotting; SS hardware loose
D-81	OK	"s"	NA	-	NA	-	NA	-	NA	-	-	
D-82	Rot	Note	OK	-	SS OK	-	OK	-	GA CO	-	-	Pile heavily rotting at waterline
D-83	OK	"s"	NA	-	NA	-	NA	-	NA	-	-	
D-84	Rot	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile heavily rotting all around
D-85	OK	-	OK	-	SS OK	-	OK	-	GA CO	-	-	
D-86	Rot	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile heavily rotting at waterline
D-87	OK	"s"	NA	-	NA	-	NA	-	NA	-	-	
D-88	Rot	Note	OK	-	SS OK	-	OK	-	GA CO	-	-	Pile rotting at waterline
D-89	Rot	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile heavily rotting at waterline/top of pile splitting
D-90	Poor	"s"	NA	-	NA	-	NA	-	NA	-	-	Pile shaved approximately 1-1/2"
D-91	Rot	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile almost completely deteriorated
D-92	Rot	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile rotting at waterline
D-93	OK	-	OK	-	SS OK	-	OK	-	SS OK	-	-	
D-94	Poor	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile starting to rot at waterline
D-95	OK	-	OK	-	SS OK	-	OK	-	SS OK	-	-	
D-96	OK	"s"	NA	-	NA	-	NA	-	NA	-	-	
D-97	OK	"s"	NA	-	NA	-	NA	-	NA	-	-	
D-98	OK	-	OK	-	SS OK	-	NA	-	NA	-	-	
D-99	Poor	"s"	NA	-	NA	-	NA	-	NA	-	-	Pile shaved approximately 2"
D-100	OK	"s"	NA	-	NA	-	NA	-	NA	-	-	
D-101	Rot	Note	OK	-	SS OK	-	Rot	Note	SS OK	-	-	Pile heavily rotting at waterline; Diagonal member bottom rotting
D-102	Poor	"s"	NA	-	NA	-	NA	-	NA	-	-	Pile shaved approximately 1-1/2"
D-103	OK	-	OK	-	SS OK	-	NA	-	NA	-	-	
D-104	Poor	"s"	NA	-	NA	-	NA	-	NA	-	-	Pile shaved approximately 2"
D-105	Rot	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile heavily rotting at waterline
D-106	OK	"s"	NA	-	NA	-	NA	-	NA	-	-	
D-107	OK	-	OK	-	GA CO	Note	NA	-	NA	-	-	x1 GA hardware missing nut/washer
D-108	Poor	"s"	NA	-	NA	-	NA	-	NA	-	-	Pile shaved approximately 2-1/2" (thin pile)
D-109	Rot	Note	OK	-	GA CO	-	NA	-	NA	-	-	Pile heavily rotting at waterline
D-110	OK	-	OK	-	SS OK	-	OK	-	SS OK	-	-	
D-111	Poor	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile starting to rot at waterline
D-112	Poor	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile starting to rot at waterline; top of pile splitting
D-113	Poor	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile starting to rot at waterline
D-114	Poor	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile starting to rot at waterline
D-115	Rot	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile rotting at waterline; top of pile splitting
D-116	Poor	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile starting to rot at waterline
D-117	Rot	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile rotting at waterline
D-118	OK	-	OK	-	SS OK	-	OK	-	SS OK	-	-	
D-119	Rot	Note	OK	-	SS OK	-	OK	-	SS OK	-	-	Pile rotting at waterline
D-120	Rot	Note	OK	-	SS OK	-	NA	-	NA	-	-	Pile heavily rotting at waterline
D-121	Poor	Note	OK	-	GA CO	-	NA	-	NA	-	-	Pile starting to rot at waterline
D-121 BH	NA	-	OK	-	GA CO	-	NA	-	NA	-	-	
D-122	OK	-	NA	-	NA	-	NA	-	NA	-	-	
D-123	OK	-	NA	-	NA	-	NA	-	NA	-	-	
D-124	OK	-	NA	-	NA	-	NA	-	NA	-	-	Floating Dock
D-125	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-126	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-127	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-128	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-129	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-130	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-131	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	

DOCK D												
	Pile Condition		Horizontal Member		H-Hardware		Diagonal Member		D-Hardware		Misc.	Notes
D-132	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-133	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-134	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-135	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-136	OK	-	OK	-	GA SC	-	NA	-	NA	-	-	
D-137	Heavily Worn		NA	-	NA	-	NA	-	NA	-	-	Floating Dock
D-138	OK	Note	OK	-	GA CO	-	NA	-	NA	-	-	Pile appears to have been repaired previously
DC-1	OK	-	OK	-	SS OK	"r"	NA	-	NA	-	-	
DC-2	OK	-	OK	-	SS OK	"r"	NA	-	NA	-	-	
DC-3	OK	-	OK	-	SS OK	"r"	NA	-	NA	-	-	
DC-4	OK	-	OK	-	SS OK	"r"	NA	-	NA	-	-	
DC-5	OK	-	OK	-	SS OK	"r"	NA	-	NA	-	-	
DC-6	OK	-	OK	-	SS OK	"r"	NA	-	NA	-	-	

Abbreviations: SS = Staines Steel, GA = Galvanized, CO = Corroded, SC = Surface Corrosion, "s" = Shaved, "r" = Rust Staining/Surface Corrosion, BH = Bulkhead

Color	Description
Red	"Bad" Condition - Needs Replacement
Yellow	"Poor" Condition - May Need Replacement in the Future
Pink	"Noted" - Indicates Item that Should be Checked/Monitored
Grey	Indicates Item Could Become Problematic in the Future

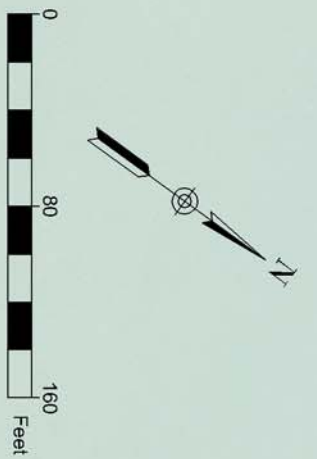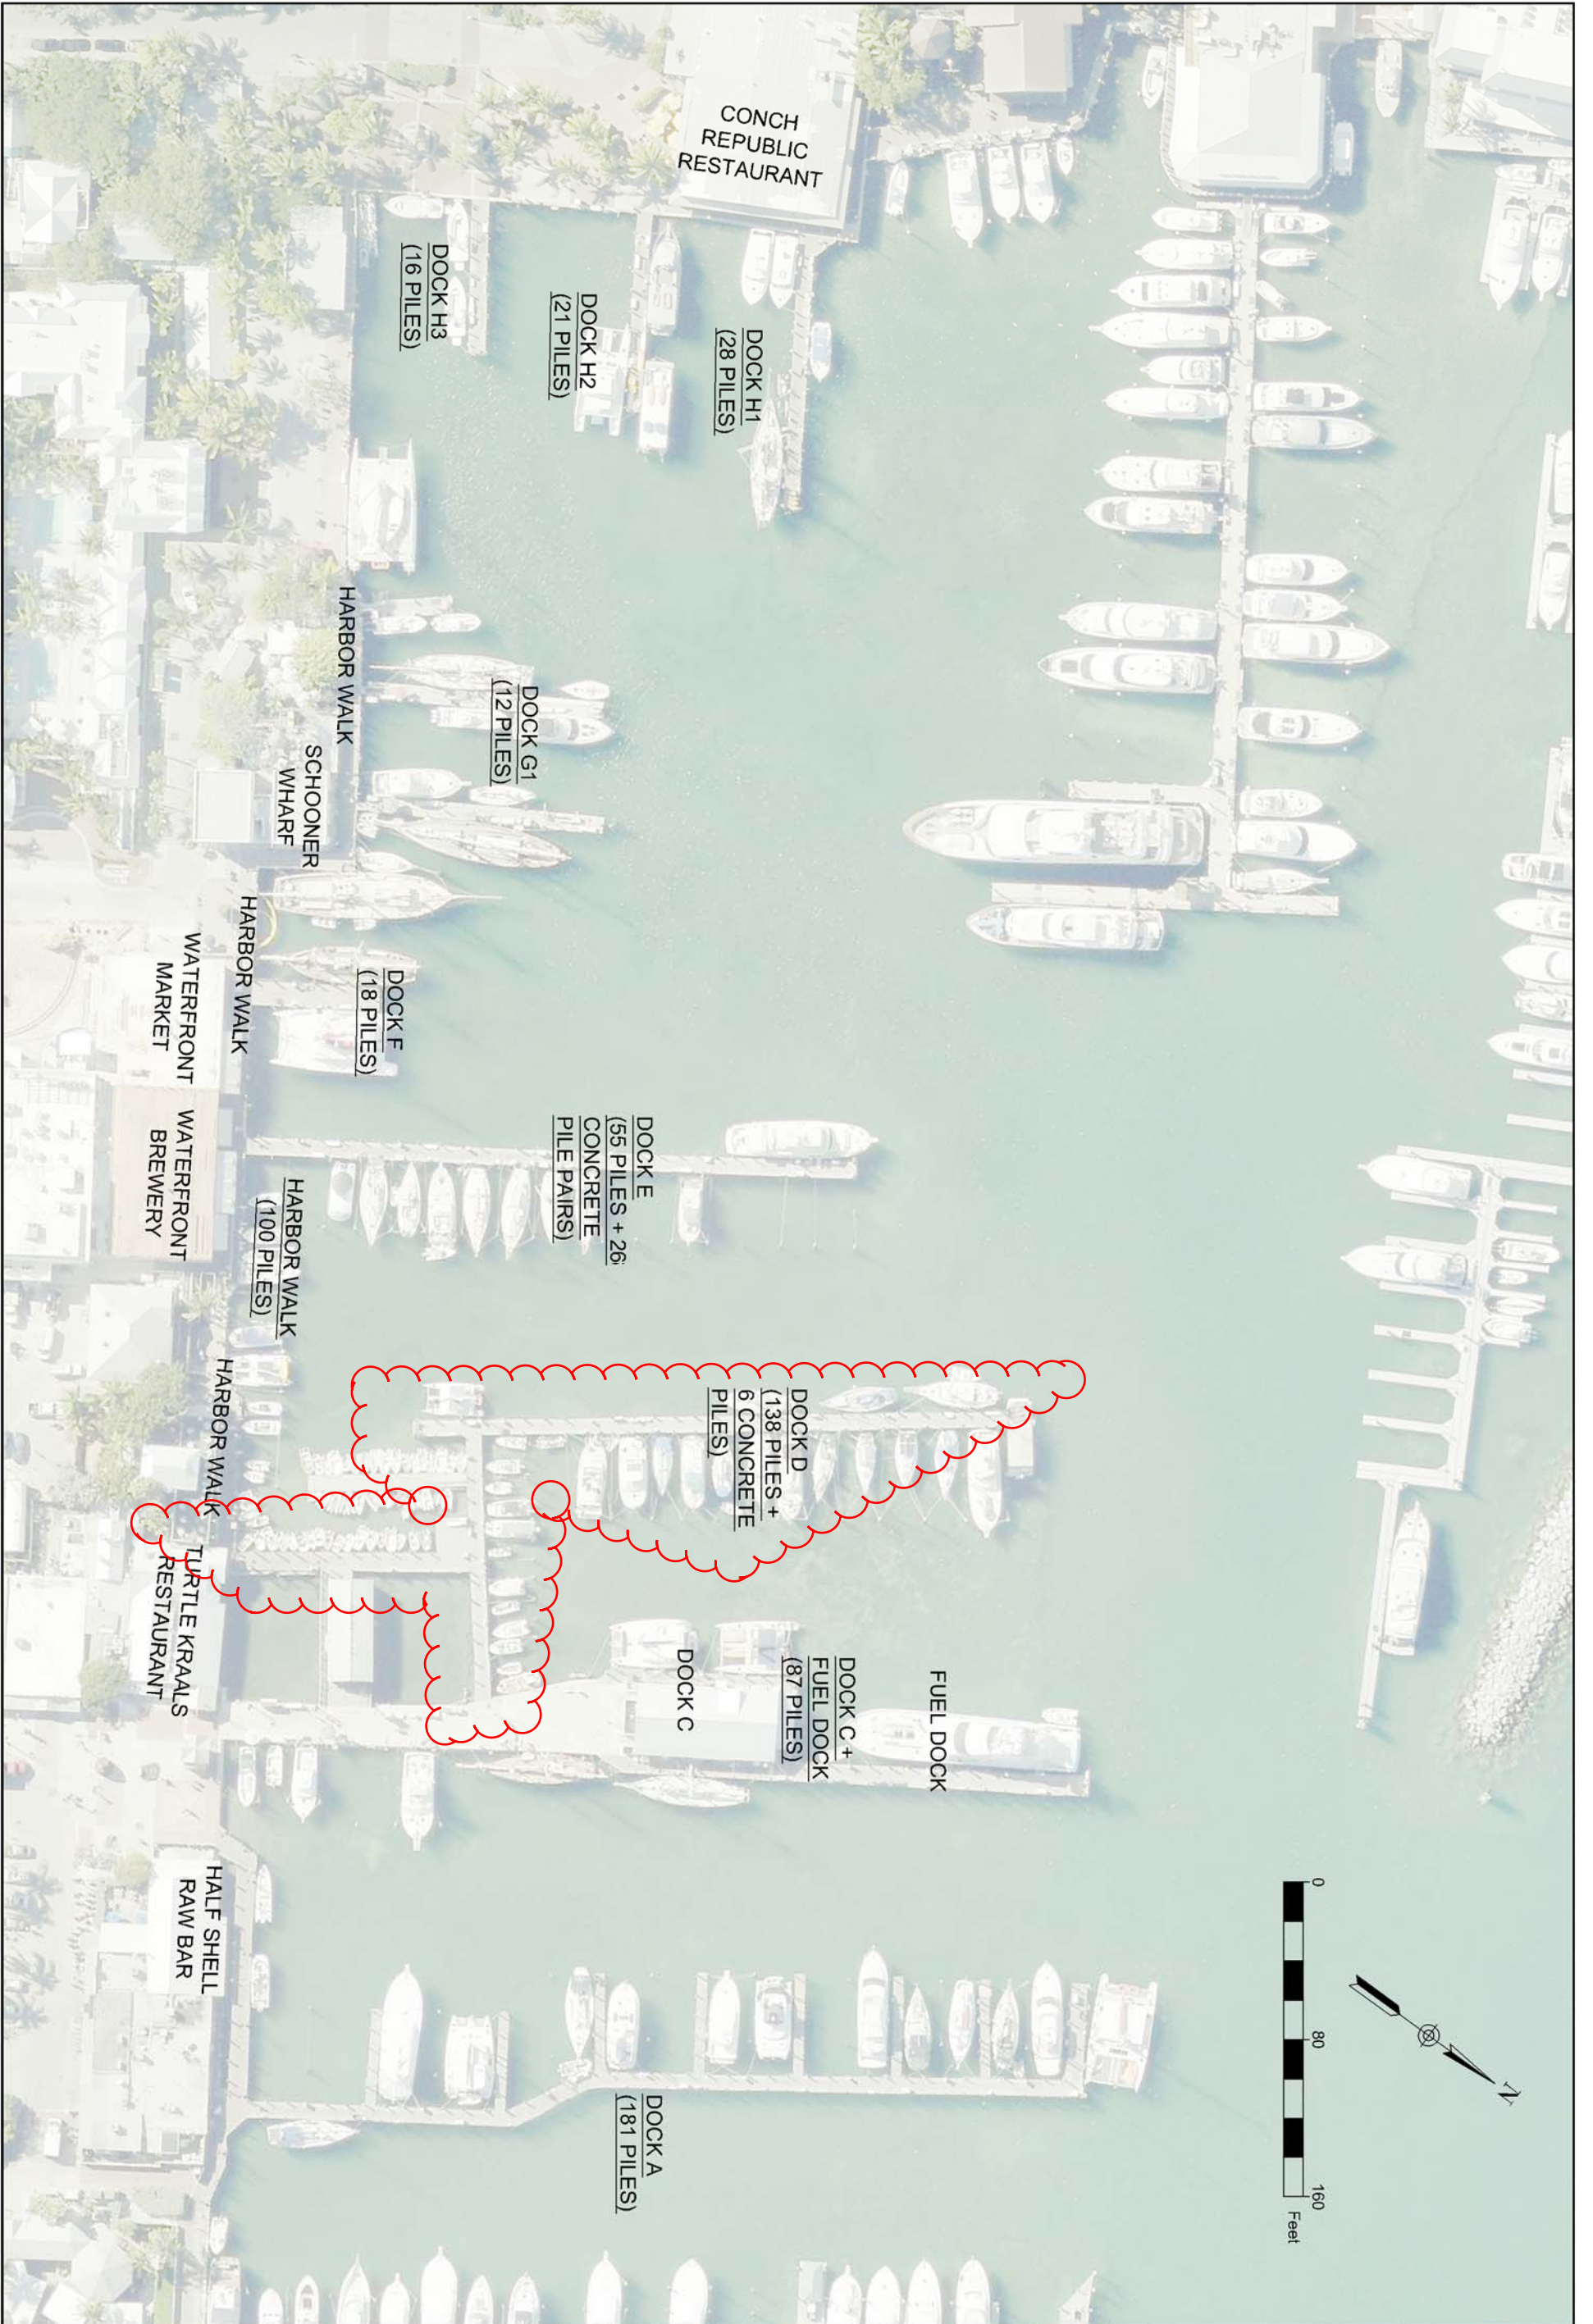


CITY OF KEY WEST
 KEY WEST BIGHT MARINA PILE ASSESSMENT
 DOCK H PLAN VIEW
 KEY WEST, MONROE COUNTY, FLORIDA

TETRA TECH INC.
 759 SOUTH FEDERAL HWY
 SUITE 314
 STUART, FL 34994-2936
 TEL: (772) 781-3400
 FAX: (772) 781-3411
 CERTIFICATE OF AUTHORIZATION
 NO. 2429

Designed by:					
Drawn By:	F. MARTINEZ				
Checked By:					
Reviewed By:					
Design file no:	KW PILE INSPECTION V2.DWG				
Scale:	AS SHOWN				
Mark	Description	Date	Appr.		




Sheet Reference:
G-001
 Sheet 1 of 13

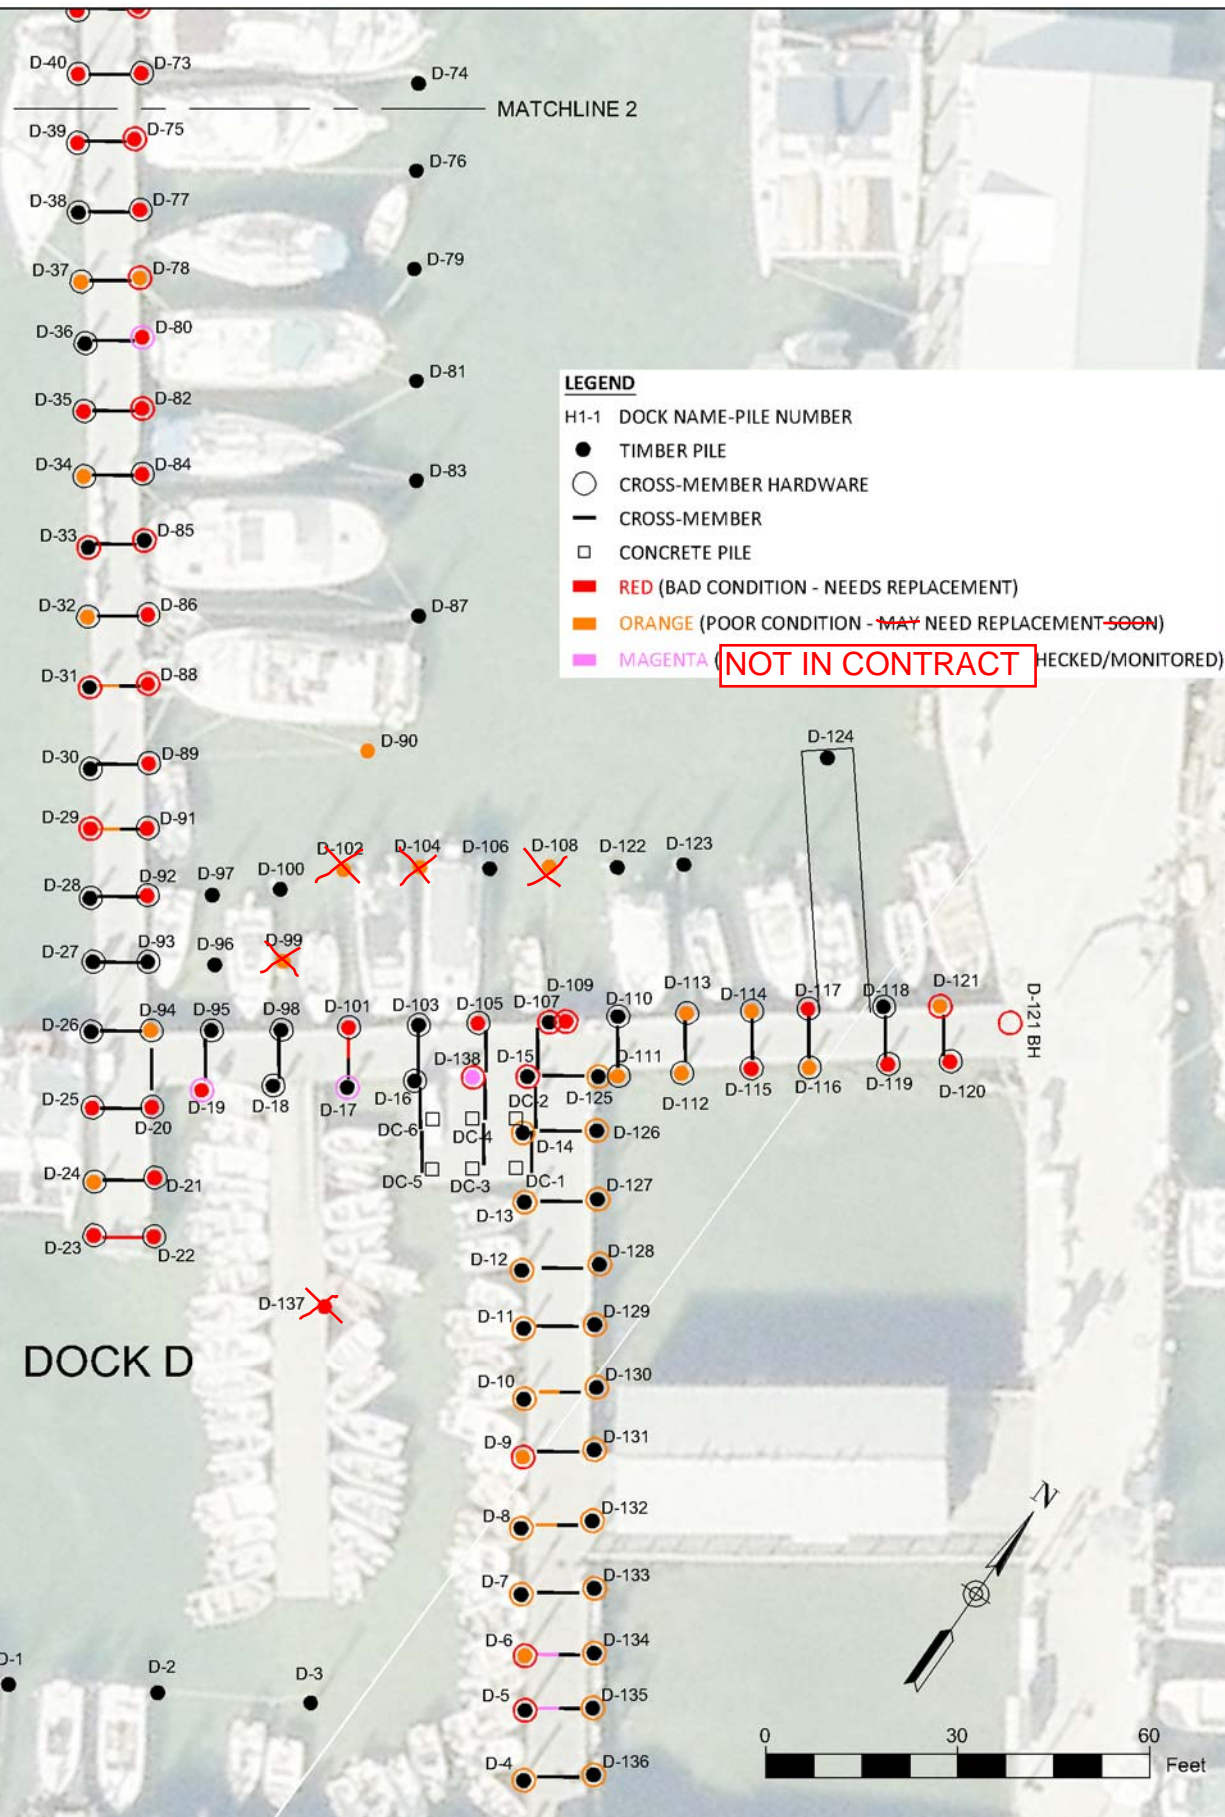

LEGEND

- H1-1 DOCK NAME-PILE NUMBER
- TIMBER PILE
- CROSS-MEMBER HARDWARE
- CROSS-MEMBER
- CONCRETE PILE
- RED (BAD CONDITION - NEEDS REPLACEMENT)
- ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
- MAGENTA (NOT IN CONTRACT CHECKED/MONITORED)

DOCK D

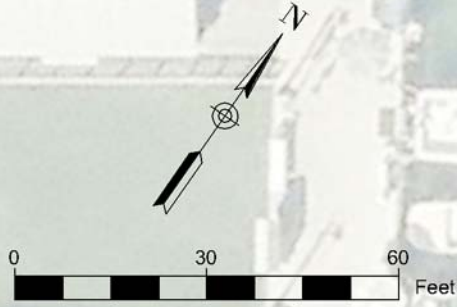

CITY OF KEY WEST
KEY WEST BIGHT MARINA PILE ASSESSMENT

 DOCK D PLAN VIEW

 KEY WEST, MONROE COUNTY, FLORIDA


TETRA TECH INC.
 759 SOUTH FEDERAL HWY
 SUITE 314
 STUART, FL 34994-2936
 TEL: (772) 781-3400
 FAX: (772) 781-3411

 CERTIFICATE OF AUTHORIZATION
 NO. 2429

Designed by: ---
 Drawn By: F. MARTINEZ
 Checked By: ---
 Reviewed By: ---

 Design file no:
 KW PILE INSPECTION V2.DWG
 Scale:
 AS SHOWN

Sheet Reference:
G-005
 Sheet 5 of 13

LEGEND

H1-1 DOCK NAME-PILE NUMBER

● TIMBER PILE

○ CROSS-MEMBER HARDWARE

— CROSS-MEMBER

□ CONCRETE PILE



■ RED (BAD CONDITION - NEEDS REPLACEMENT)

■ ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)

■ MAGENTA (NOT IN CONTRACT CHECKED/MONITORED)

DOCK D

FUEL DOCK

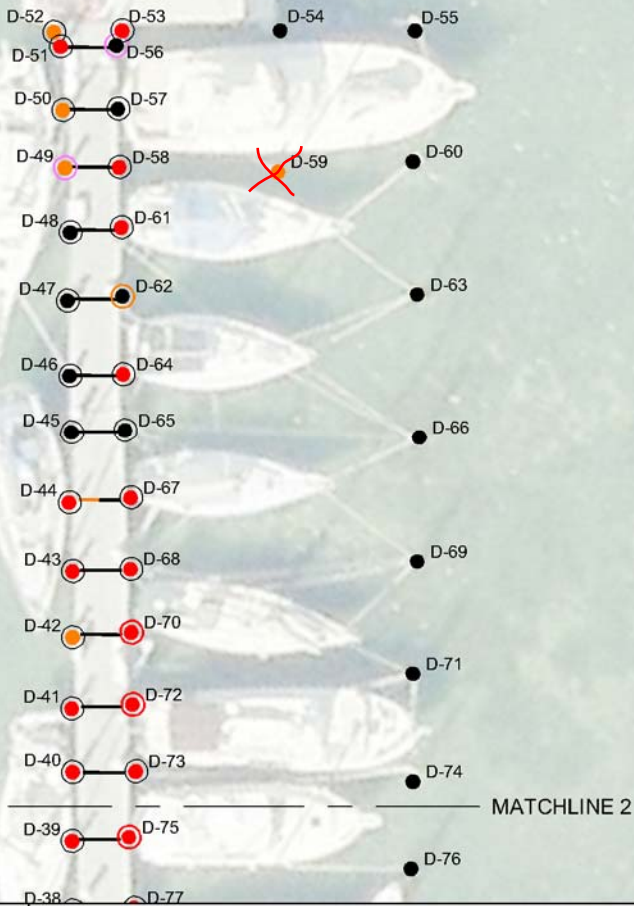

**CITY OF KEY WEST
KEY WEST BIGHT MARINA PILE ASSESSMENT**

DOCK D PLAN VIEW

KEY WEST, MONROE COUNTY, FLORIDA



TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 314
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411

CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:

Drawn By:
F. MARTINEZ

Checked By:

Reviewed By:

Design file no:
KW PILE INSPECTION V2.DWG

Scale:
AS SHOWN

Sheet Reference:

G-006

Sheet 6 of 13

Dock D



D-5.1



D-5.2



D-5.3



D-6.1



D-6.2



D-6.3



D-8.1



D-8.2



D-9.1



D-9.2



D-9.3



D-10.1

Dock D



D-10.2



D-17.1



D-17.2



D-17.3



D-17.4



D-19.1



D-19.2



D-19.3



D-20.1



D-20.2



D-20.3



D-20.4

Dock D



D-22.1



D-22.2



D-22.3



D-22.4



D-22.5



D-22.6



D-23.1



D-23.2



D-23.3



D-23.4



D-23.5



D-23.6

Dock D



D-23.7



D-24.1



D-24.2



D-29.1



D-29.2



D-29.3



D-29.4



D-32.1



D-32.2



D-35.1



D-35.2



D-35.3

Dock D



D-39.1



D-39.2



D-39.3



D-39.4



D-41.1



D-41.2



D-41.3



D-41.4



D-41.5



D-43.1



D-43.2



D-43.3

Dock D



D-43.4



D-43.5



D-44.1



D-44.2




D-44.3



D-44.4



D-44.5

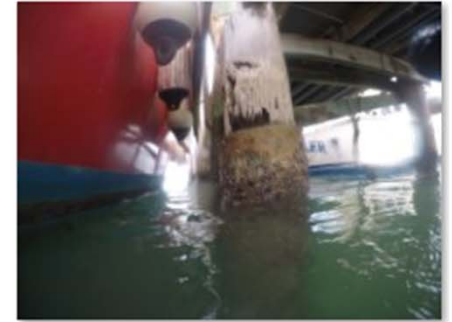

D-49 adjacent-1



D-49 adjacent-2



D-49.1



D-49.2



D-51.1

Dock D



D-51.2



D-51.3



D-51.4



D-52.1



D-53.1



D-53.2



D-53.3



D-53.4



D-58.1



D-58.2



D-58.3



D-59.1

Dock D



D-61.1



D-61.2



D-61.3



D-64.1



D-64.2



D-64.3



D-64.4



D-67.1



D-67.2



D-67.3



D-68.1



D-68.2

Dock D



D-68.3



D-68.4



D-68.5



D-70.1



D-70.2



D-70.3



D-72.1



D-72.2



D-72.3



D-73.1



D-73.2



D-73.3

Dock D



D-75.1



D-75.2



D-75.3



D-77.1



D-77.2



D-77.3



D-80.1



D-80.2



D-80.3



D-82.1



D-82.2



D-82.3

Dock D



D-84.1



D-84.2



D-84.3



D-86.1



D-86.2



D-86.3



D-88.1



D-88.2



D-89.1



D-89.2



D-89.3



D-89.4

Dock D



D-91.1



D-91.2



D-91.3



D-92.1



D-92.2



D-92.3



D-92.4



D-100.1



D-100.2



D-100.3



D-100.4



D-105.1

Dock D



D-105.2



D-105.3



D-108.1



D-109.1



D-109.2



D-109.3



D-112.1



D-115.1



D-115.2



D-115.3



D-115.4



D-117.1

Dock D



D-117.2



D-117.3



D-119.1



D-119.2



D-119.3



D-120.1



D-120.2



D-120.3



D-121 BH.1



D-121 BH.2



D-121 BH.3



D-138.1

Dock D



D-138.2



D-138.3



D-138.4



D-138.5



DC-1.1



DC-1.2



DC-1.3



D-GENERAL (1)



D-GENERAL (2)



D-GENERAL (3)



D-GENERAL (4)



D-GENERAL (5)

Dock D



D-GENERAL (6)



D-GENERAL (7)



D-GENERAL (8)



D-GENERAL (9)



D-GENERAL (10)



D-GENERAL (11)



D-GENERAL (12)



Florida Department of Environmental Protection

South District Branch Office
2796 Overseas Highway, Suite 221
Marathon, Florida 33050
SouthDistrict@dep.state.fl.us

Rick Scott
Governor

Carlos Lopez-Cantera
Lt. Governor

Noah Valenstein
Secretary

November 6, 2017

City of Key West - Key West Bight Pier
c/o Francisco Martinez
Tetra Tech Inc.
Francisco.martinez@tetrattech.com

File No.: 0137939-019-EE, Monroe County
BOT File No.: 440027185

Dear Applicant:

On November 2, 2017, we received your request for verification of exemption to perform the following activities:

To repair/replace structural support pilings and mooring pilings at 201 William Street, Key West, FL 33040. Parcel ID No. 00072082 004200 in Key West Bight, Class III Waters, Section 31, Township 67 South, Range 25 East, Monroe County.

Your request has been reviewed to determine whether it qualifies for (1) a regulatory exemption, (2) proprietary authorization (related to state-owned submerged lands), and (3) federal approval that may be necessary for work in wetlands or waters of the United States.

Your project did not qualify for the federal review portion of this verification request. As of October 1, 2017, separate application must be made to the Army Corps of Engineers (Corps). **You must apply separately to the Corps using the appropriate federal application form.** More information about Corps permitting may be found online in the Jacksonville Regulatory Division Sourcebook. contact information found below). This letter does not relieve you from the responsibility of obtaining other federal, state, or local authorizations that may be required for the activity.

1. Regulatory Review – VERIFIED

Based on the information submitted, the Department has determined that the activity as proposed is exempt, under Section 373.406(6) of the Florida Statutes, from the need to obtain a regulatory permit under Part IV of Chapter 373 of the Florida Statutes. This determination is made because the activity, in consideration of its type, size, nature, location, use and operation, is expected to

have only minimal or insignificant individual or cumulative adverse impacts on the water resources.

This exemption verification is based on the information you provided the Department and the statutes and rules in effect when the information was submitted. This verification may not be valid if site conditions materially change, the project design is modified, or the statutes or rules governing the exempt activity are amended. In the event you need to re-verify the exempt status for the activity, a new request and verification fee will be required. Any substantial modifications to the project design should be submitted to the Department for review, as changes may result in a permit being required.

2. Proprietary Review - GRANTED

The Department acts as staff to the Board of Trustees of the Internal Improvement Trust Fund (Board of Trustees) and issues certain authorizations for the use of sovereign submerged lands. The Department has the authority to review activities on sovereign submerged lands under Chapters 253 and 258 of the Florida Statutes, and Chapters 18-18, 18-20, and 18-21, Florida Administrative Code, as applicable.

The activity appears to be located on sovereign submerged lands owned by the Board of Trustees. The activity is not exempt from the need to obtain the applicable proprietary authorization. As staff to the Board of Trustees, the Department has reviewed the activity described above, and has determined that as long as the work is performed as described in the attached project drawings, is wholly located within the boundaries of the existing Sovereign Submerged Land Lease (BOT No.: 440027185) and is consistent with the terms and conditions therein, we have no objection to the project. Therefore, consider this letter to also constitute the authority sought under Section 253.77 of the Florida Statutes to pursue this project.

3. SPGP Review - NOT APPROVED

Your proposed activity as outlined on your application and attached drawings **does not qualify** for Federal authorization pursuant to the State Programmatic General Permit and a **separate application is required** to the Corps. Please contact the Corps at the Miami Office at 9900 SW 107th Avenue, Suite 203, Miami, FL 33176-2785, or by telephone at (305)-526-7181, or electronically at SEAPPLS@usace.army.mil for further information. **Failure to obtain Corps authorization prior to construction could subject you to federal enforcement action by that agency.**

Authority for review an agreement with the USACOE entitled “Coordination Agreement Between the U. S. Army Corps of Engineers (Jacksonville District) and the Florida Department of Environmental Protection, or Duly Authorized Designee, State Programmatic General Permit”, Section 10 of the Rivers and Harbor Act of 1899, and Section 404 of the Clean Water Act.

Additional Information

Please retain this letter. The activities may be inspected by authorized state personnel in the future to ensure compliance with appropriate statutes and administrative codes. If the activities are not in compliance, you may be subject to penalties under Chapter 373, F.S., and Chapter 18-14, F.A.C.

NOTICE OF RIGHTS

This action is final and effective on the date filed with the Clerk of the Department unless a petition for an administrative hearing is timely filed under Sections 120.569 and 120.57, F.S., before the deadline for filing a petition. On the filing of a timely and sufficient petition, this action will not be final and effective until further order of the Department. Because the administrative hearing process is designed to formulate final agency action, the filing of a petition means that the Department's final action may be different from the position taken by it in this notice.

Petition for Administrative Hearing

A person whose substantial interests are affected by the Department's action may petition for an administrative proceeding (hearing) under Sections 120.569 and 120.57, F.S. Pursuant to Rule 28-106.201, F.A.C., a petition for an administrative hearing must contain the following information:

- (a) The name and address of each agency affected and each agency's file or identification number, if known;
- (b) The name, address, any email address, any facsimile number, and telephone number of the petitioner; the name, address, and telephone number of the petitioner's representative, if any, which shall be the address for service purposes during the course of the proceeding; and an explanation of how the petitioner's substantial interests are or will be affected by the agency determination;
- (c) A statement of when and how the petitioner received notice of the agency decision;
- (d) A statement of all disputed issues of material fact. If there are none, the petition must so indicate;
- (e) A concise statement of the ultimate facts alleged, including the specific facts that the petitioner contends warrant reversal or modification of the agency's proposed action;
- (f) A statement of the specific rules or statutes that the petitioner contends require reversal or modification of the agency's proposed action, including an explanation of how the alleged facts relate to the specific rules or statutes; and
- (g) A statement of the relief sought by the petitioner, stating precisely the action that the petitioner wishes the agency to take with respect to the agency's proposed action.

The petition must be filed (received by the Clerk) in the Office of General Counsel of the Department at 3900 Commonwealth Boulevard, Mail Station 35, Tallahassee, Florida 32399-3000 or by email to Agency_clerk@dep.state.fl.us. Also, a copy of the petition shall be mailed to the applicant at the address indicated above at the time of filing.

Time Period for Filing a Petition

In accordance with Rule 62-110.106(3), F.A.C., petitions for an administrative hearing by the applicant must be filed within 21 days of receipt of this written notice. Petitions filed by any persons other than the applicant, and other than those entitled to written notice under Section 120.60(3), F.S. must be filed within 21 days of publication of the notice or within 21 days of receipt of the written notice, whichever occurs first. Under Section 120.60(3), F.S., however, any person who has asked the Department for notice of agency action may file a petition within 21 days of receipt of such notice, regardless of the date of publication. The failure to file a petition within the appropriate time period shall constitute a waiver of that person's right to request an administrative determination (hearing) under Sections 120.569 and 120.57, F.S., or to intervene in this proceeding and participate as a party to it. Any subsequent intervention (in a proceeding initiated by another party) will be only at the discretion of the presiding officer upon the filing of a motion in compliance with Rule 28-106.205, F.A.C.

Extension of Time

Under Rule 62-110.106(4), F.A.C., a person whose substantial interests are affected by the Department's action may also request an extension of time to file a petition for an administrative hearing. The Department may, for good cause shown, grant the request for an extension of time. Requests for extension of time must be filed with the Office of General Counsel of the Department at 3900 Commonwealth Boulevard, Mail Station 35, Tallahassee, Florida 32399-3000, before the applicable deadline for filing a petition for an administrative hearing. A timely request for extension of time shall toll the running of the time period for filing a petition until the request is acted upon.

Mediation

Mediation is not available in this proceeding.

FLAWAC Review

The applicant, or any party within the meaning of Section 373.114(1)(a) or 373.4275, F.S., may also seek appellate review of this order before the Land and Water Adjudicatory Commission under Section 373.114(1) or 373.4275, F.S. Requests for review before the Land and Water Adjudicatory Commission must be filed with the Secretary of the Commission and served on the Department within 20 days from the date when the order is filed with the Clerk of the Department.

Judicial Review

Any party to this action has the right to seek judicial review pursuant to Section 120.68, F.S., by filing a Notice of Appeal pursuant to Rules 9.110 and 9.190, Florida Rules of Appellate Procedure, with the Clerk of the Department in the Office of General Counsel, 3900 Commonwealth Boulevard, M.S. 35, Tallahassee, Florida 32399-3000; and by filing a copy of the Notice of Appeal accompanied by the applicable filing fees with the appropriate District

Court of Appeal. The Notice of Appeal must be filed within 30 days from the date this action is filed with the Clerk of the Department.

Thank you for applying to the Submerged Lands and Environmental Resource Permit Program. If you have any questions regarding this matter, please contact us by telephone at (239) 344-5600 or by e-mail at SouthDistrict@dep.state.fl.us. When referring to this project, please reference the file number listed above.

Executed in Orlando, Florida

STATE OF FLORIDA DEPARTMENT OF ENVIRONMENTAL PROTECTION



Megan Mills
Permitting Program Administrator
South District

CERTIFICATE OF SERVICE

The undersigned duly designated deputy clerk hereby certifies that this document and authorization to use sovereignty submerged lands, including all copies, were sent to the addressee and to the following listed persons:

U.S. Army Corps of Engineers, Miami Office, SEAppls@usace.army.mil
Kathy Griffin, Division of State Lands, BOT # 440027185, Kathy.Griffin@dep.state.fl.us

FILING AND ACKNOWLEDGMENT

FILED, on this date, pursuant to Section 120.52(7), F.S., with the designated Department clerk, receipt of which is hereby acknowledged.



Clerk

November 6, 2017
Date

Enclosures:



20 Project drawings
373.406(6), F.S.



CITY OF KEY WEST

KEY WEST BIGHT MARINA MAINTENANCE (PILING REPLACEMENT DOCK REPAIR)

PILE REPLACEMENT PERMITTING

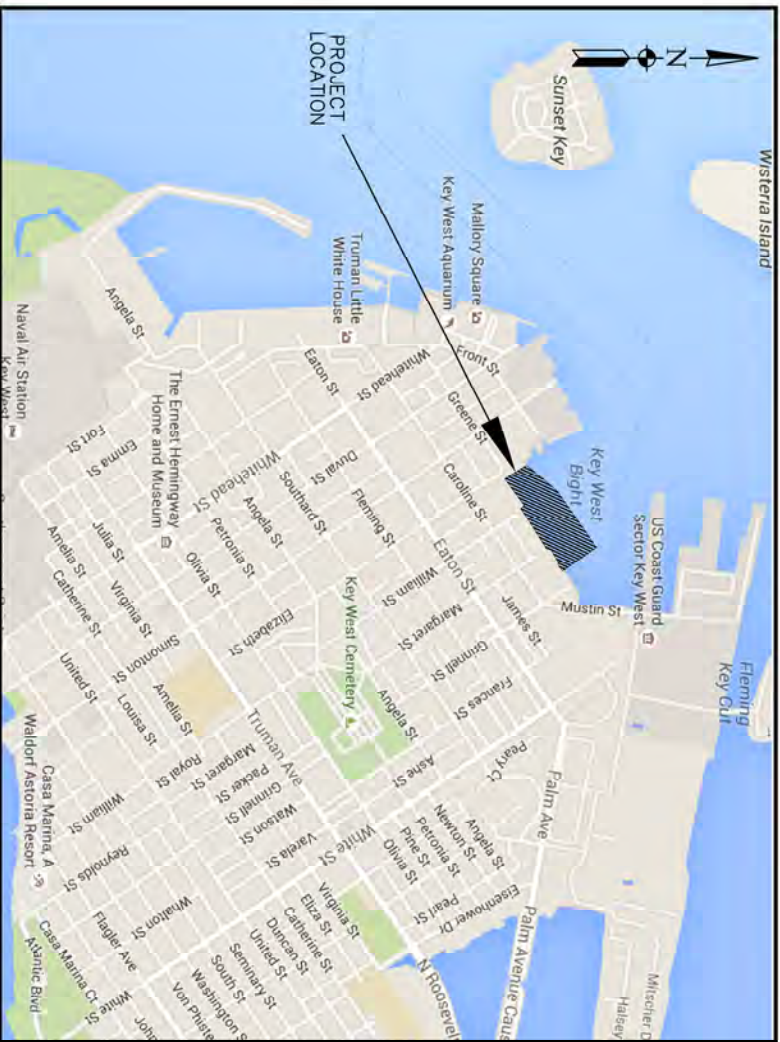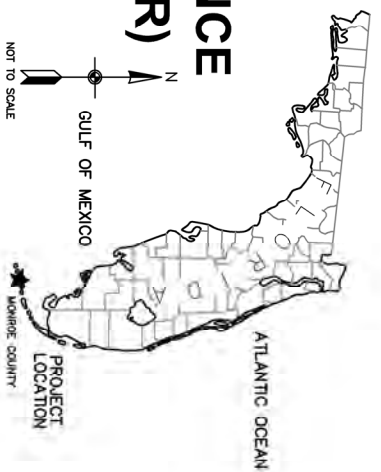

VICINITY MAP

KEY WEST BIGHT MARINA, KEY WEST, FLORIDA

INDEX OF SHEETS

SHEET #	TITLE	LATEST UPDATE	REV.
G-001	COVER SHEET AND VICINITY MAP	10/18/2017	0
G-002	KEY WEST BIGHT LOCATION AND ACCESS	10/18/2017	0
G-003	VICINITY MAP AND DIRECTIONS TO SITE	10/18/2017	0
G-004	USDA/NRCS SOIL MAP	10/18/2017	0
C-101	KEY WEST BIGHT MARINA PLAN VIEW	10/18/2017	0
C-102	DOCK A PLAN VIEW	10/18/2017	0
C-103	DOCK A PLAN VIEW	10/18/2017	0
C-104	DOCK C AND FUEL DOCK PLAN VIEW	10/18/2017	0
C-105	DOCK D PLAN VIEW	10/18/2017	0
C-106	DOCK D PLAN VIEW	10/18/2017	0
C-107	DOCK E PLAN VIEW	10/18/2017	0
C-108	DOCK F PLAN VIEW	10/18/2017	0
C-109	DOCK G PLAN VIEW	10/18/2017	0
C-110	DOCK H PLAN VIEW	10/18/2017	0
C-111	HARBOR WALK PLAN VIEW	10/18/2017	0
C-112	HARBOR WALK PLAN VIEW	10/18/2017	0
C-113	HARBOR WALK PLAN VIEW	10/18/2017	0
C-114	CROSS-SECTION DETAIL	10/18/2017	0
C-115	CROSS-SECTION DETAIL	10/18/2017	0
C-116	CROSS-SECTION DETAIL	10/18/2017	0

FOR PERMITTING
NOT FOR CONSTRUCTION


TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 314
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411
CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:
Drawn By:
Checked By:
Date:
Design file no:
Scale:



EXEMPT
File Number:
0137939-019-EE



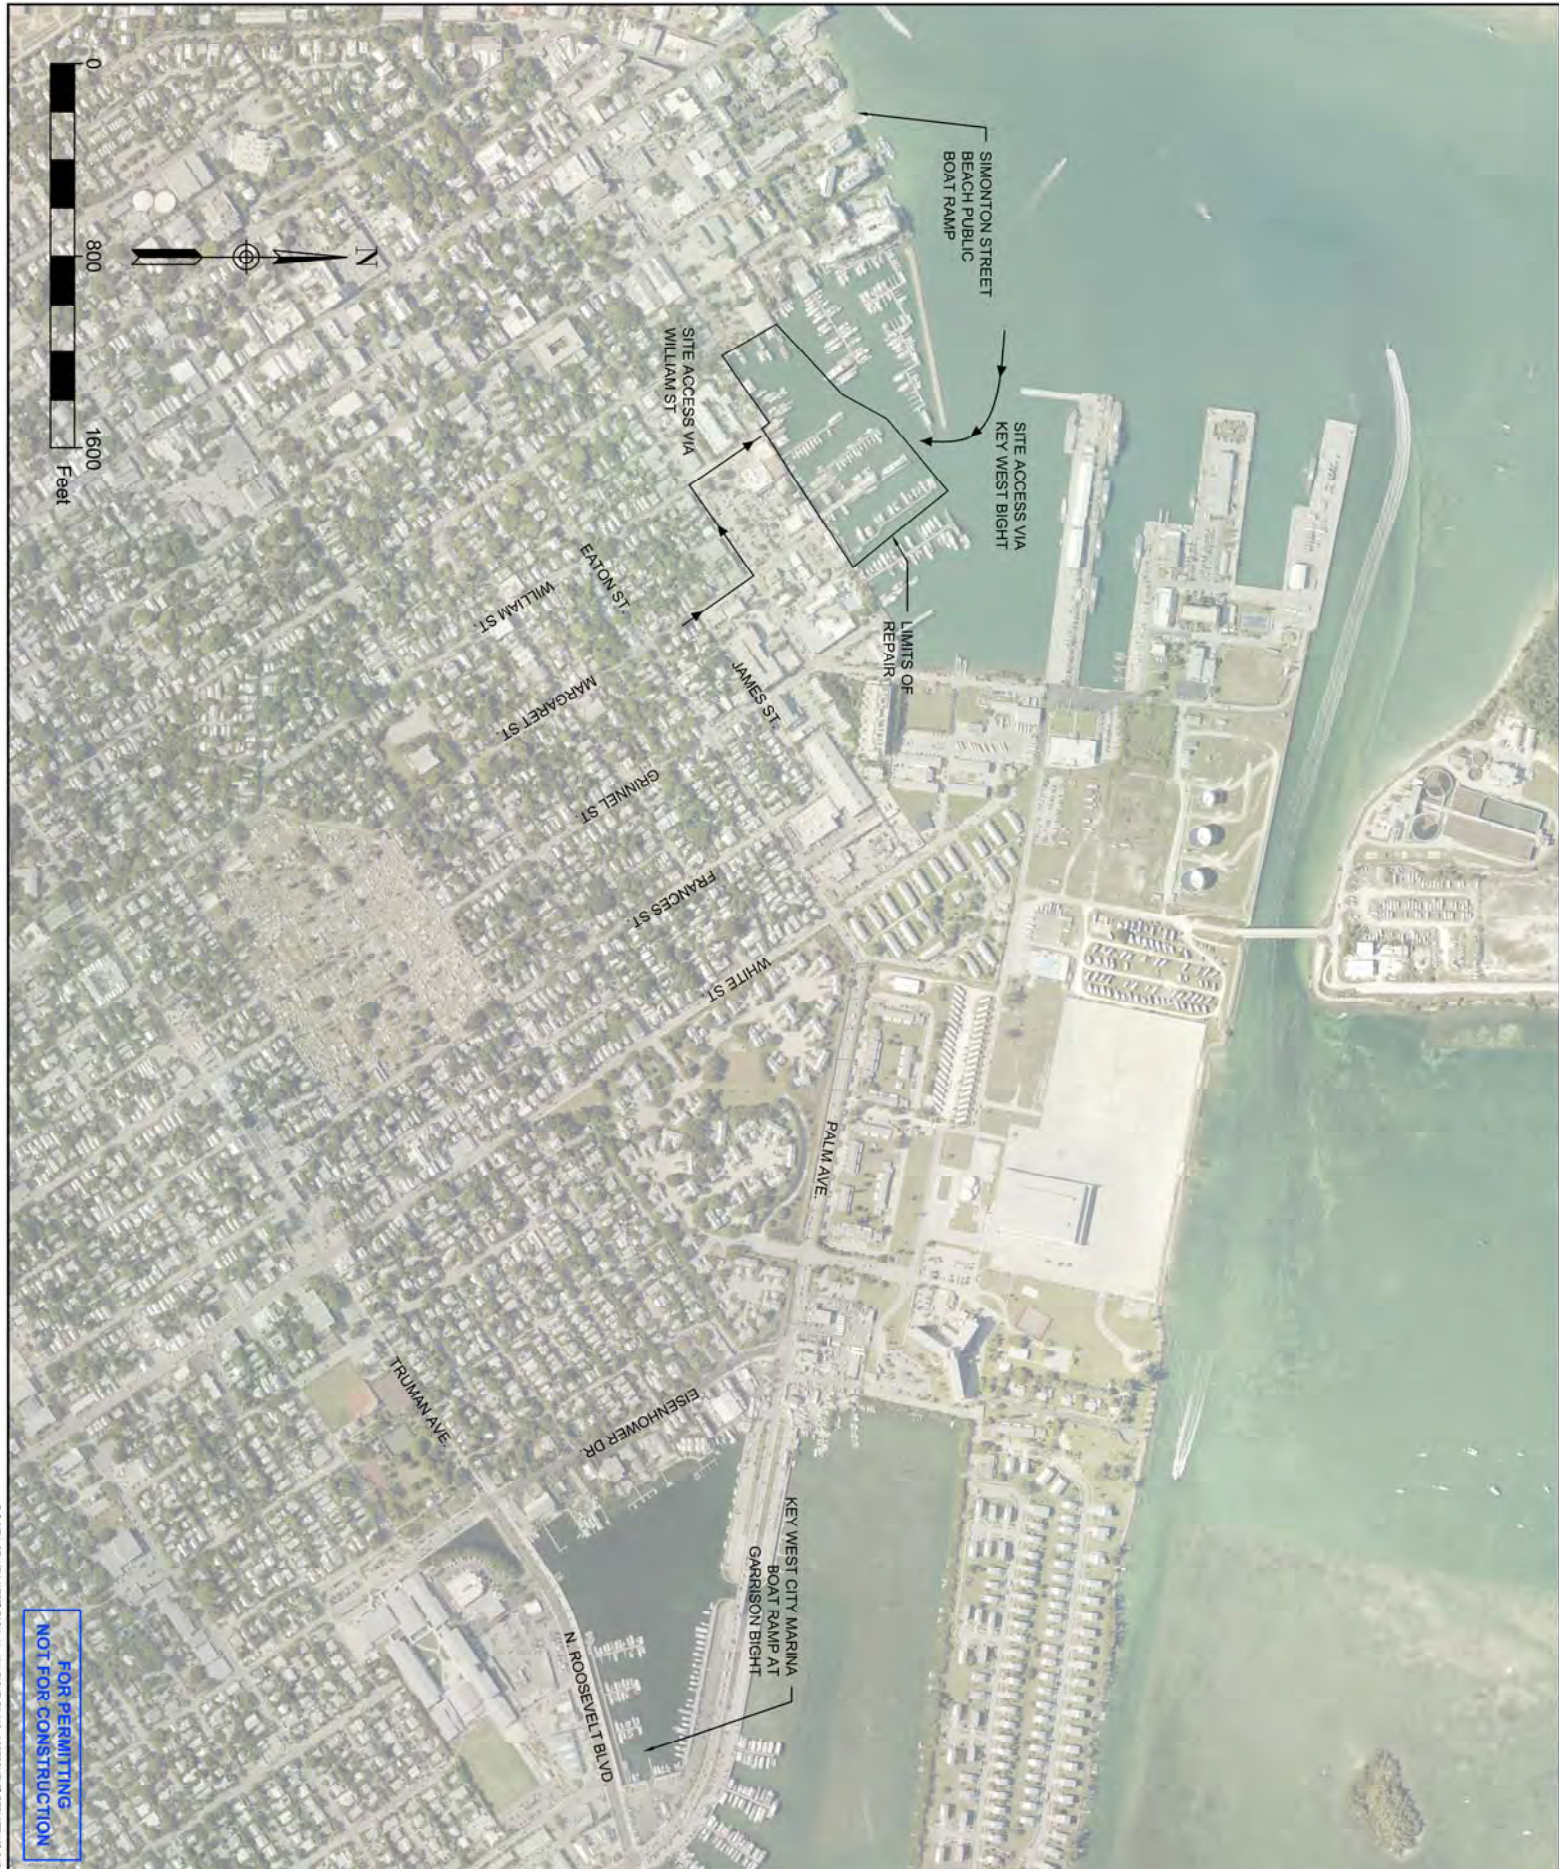

P:\0471 OF KEY WEST\JOB 11 - NW BOAT PILING ASSESSMENT\PERMITTING\CADD\KEY WEST_PILING_CONSTR_1.DWG

FOR PERMITTING
NOT FOR CONSTRUCTION

Sheet Reference:
G-002
Sheet 2 of 20


CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)
 KEY WEST BIGHT LOCATION AND ACCESS
 KEY WEST, MONROE COUNTY, FLORIDA

TT **TETRA TECH INC.**
 758 SOUTH FEDERAL HWY
 SUITE 314
 STUART, FL 34984-2936
 TEL (772) 781-3400
 FAX (772) 781-3411
 CERTIFICATE OF AUTHORIZATION
 NO. 2429

Designed by:				
Drawn By:	F. MARTINEZ			
Checked By:	S. MCGAHEE			
Date:	10/18/17			
Design file no:	NW_PILE_REPLACE_CONSTR_V1.DWG			
Scale:	AS SHOWN			
	Mark	Description	Date	Appr.


EXEMPT
 File Number:
 0137939-019-EE



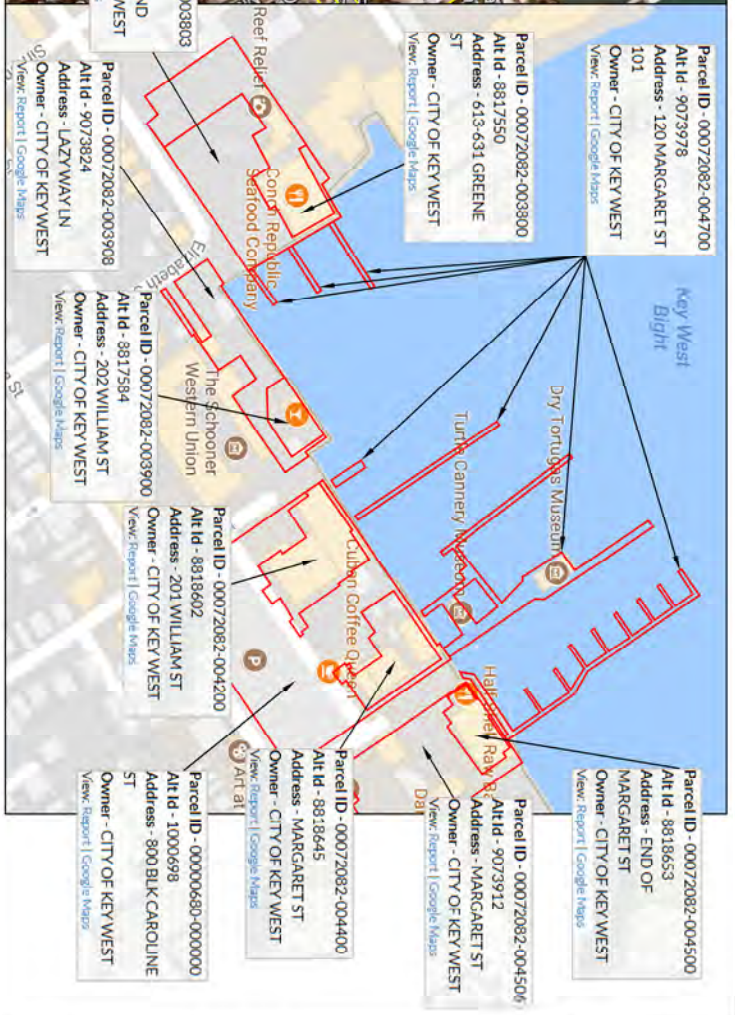

← from 1829 N Roosevelt Blvd, Key West, FL 33040
to Key West Bight Marina, 201 William St, Key West, FL 33040


5 min (1.3 miles)
via Palm Avenue Causeway and Eaton St
Fastest route, the usual traffic

1829 N Roosevelt Blvd
Key West, FL 33040

- ↑ Head northwest on 1st St
- ↑ Continue onto Palm Avenue Causeway
- ↑ Continue onto Palm Ave
- ↑ Continue onto Eaton St
- ↑ Turn right onto William St

Key West Bight Marina
201 William St, Key West, FL 33040

Received Electronically
 November 2, 2017
 South District

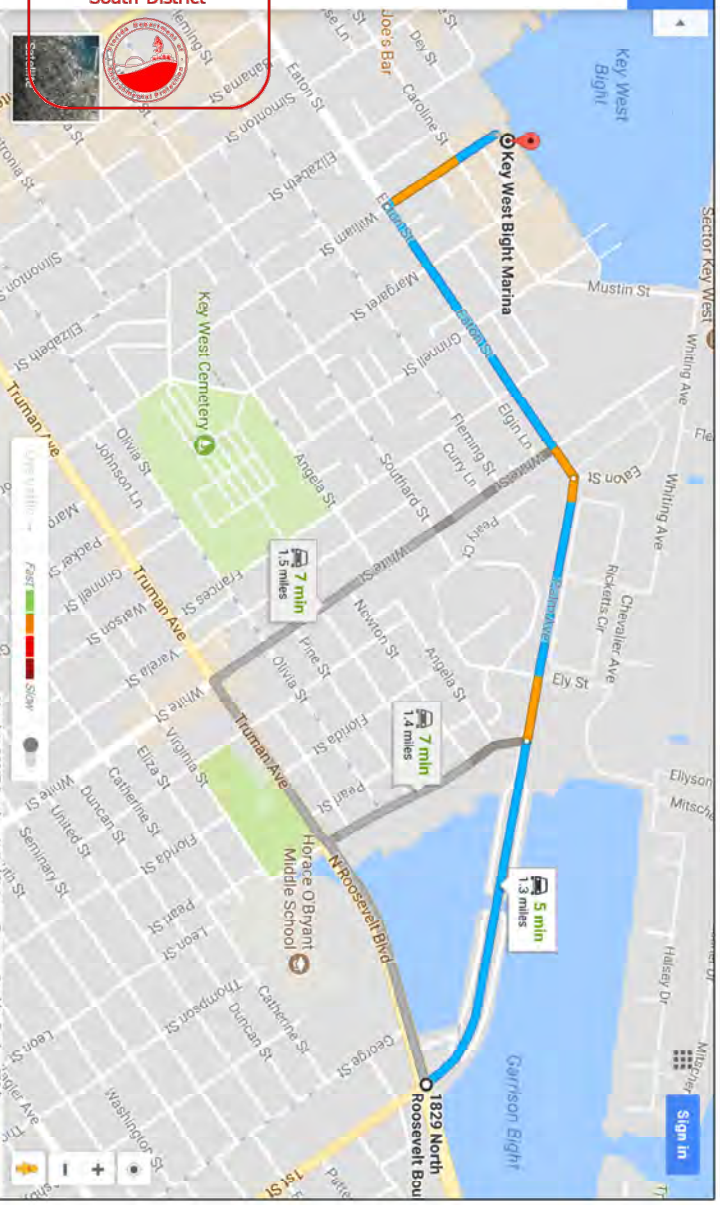

FOR PERMITTING NOT FOR CONSTRUCTION

P:\NOT FOR KEY WEST\11. KEY BIGHT MARINA MAINTENANCE\PERMITTING\CONTRACT\MAPS\FILE PERMIT COVER.PDF

CITY OF KEY WEST

KEY WEST BIGHT MARINA MAINTENANCE (PILING REPLACEMENT DOCK REPAIR)

VICINITY MAP AND DIRECTIONS TO SITE

KEY WEST, MONROE COUNTY, FLORIDA

TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 314
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411

CERTIFICATE OF AUTHORIZATION
NO. 2429


Designed by:	
Drawn by:	M. MARTINEZ
Checked by:	S. MCGAHEE
Date:	10/19/17
Design file no:	FILE PERMIT COVER.PDF
Scale:	AS SHOWN

EXEMPT

File Number:
0137939-019-EE



Custom Soil Resource Report
Soil Map

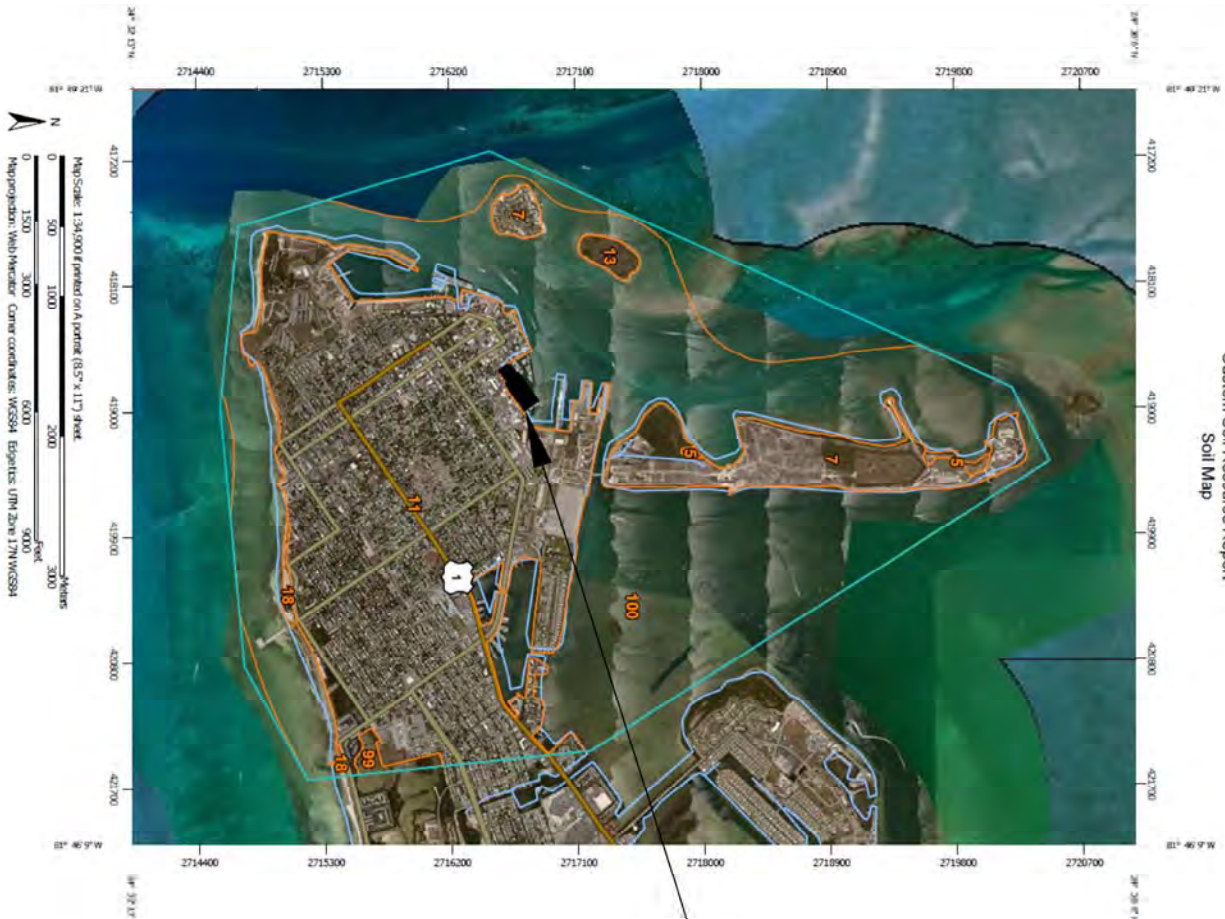

Map Scale: 1:34,900 (printed on A poster (8.5" x 11" sheet))
0 500 1000 2000 3000 4000 5000 Feet
0 1500 3000 4500 6000 Meters
Map Projection: Web Mercator Corner coordinates: WGS84 Edge: UTM Zone 17N WGS84

Map Unit Symbol	Map Unit Name	Acres in AOI	Percent of AOI
5	Islamorada muck, tidal	9.5	8.2%
7	Urban land	2,720	6.7%
11	Urban land	1,529.2	35.2%
13	Keywest very gravelly loam, extremely stony	21.5	0.5%
18	Beaches	10.5	0.2%
99	Water	18.2	0.4%
100	Waters of the Atlantic Ocean	2,181.5	50.2%
Subtotal for Soil Survey Area		4,042.3	93.9%
Total for Area of Interest		4,345.4	100.0%

PROJECT LOCATION -
RESEARCH SOIL
#11 & #100

11—Urban land

Map Unit Symbol: 11
Percent of AOI: 35.2%
Acres in AOI: 1,529.2
Area: 1,529.2 acres
Soil: Urban land
Soil Series: Urban land
Soil Order: Urban land
Soil Group: Urban land
Soil Family: Urban land
Soil Subgroup: Urban land
Soil Series: Urban land
Soil Order: Urban land
Soil Group: Urban land
Soil Family: Urban land
Soil Subgroup: Urban land
Soil Series: Urban land
Soil Order: Urban land
Soil Group: Urban land
Soil Family: Urban land
Soil Subgroup: Urban land

100—Waters of the Atlantic Ocean

Map Unit Symbol: 100
Percent of AOI: 50.2%
Acres in AOI: 2,181.5
Area: 2,181.5 acres
Soil: Waters of the Atlantic Ocean
Soil Series: Waters of the Atlantic Ocean
Soil Order: Waters of the Atlantic Ocean
Soil Group: Waters of the Atlantic Ocean
Soil Family: Waters of the Atlantic Ocean
Soil Subgroup: Waters of the Atlantic Ocean
Soil Series: Waters of the Atlantic Ocean
Soil Order: Waters of the Atlantic Ocean
Soil Group: Waters of the Atlantic Ocean
Soil Family: Waters of the Atlantic Ocean
Soil Subgroup: Waters of the Atlantic Ocean

Received
Electronically
November 2, 2017
South District



FOR PERMITTING
NOT FOR CONSTRUCTION

CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)
USDA/NRCS SOIL MAP
KEY WEST, MONROE COUNTY, FLORIDA

TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 314
STUART, FL 34994-2936
TEL: (772) 781-1818
FAX: (772) 781-3411
CERTIFICATE OF AUTHORIZATION
NO. 2429

Mark	Description	Date	Appr.

EXEMPT
File Number:
0137939-09-EE




Sheet Reference:
G-004
Sheet 4 of 20

K C

LEGEND

H1-1 DOCK NAME-PILE NUMBER

- TIMBER PILE
- CONCRETE PILE
- RED (BAD CONDITION - NEEDS REPLACEMENT)
- ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
- MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED /MONITORED)

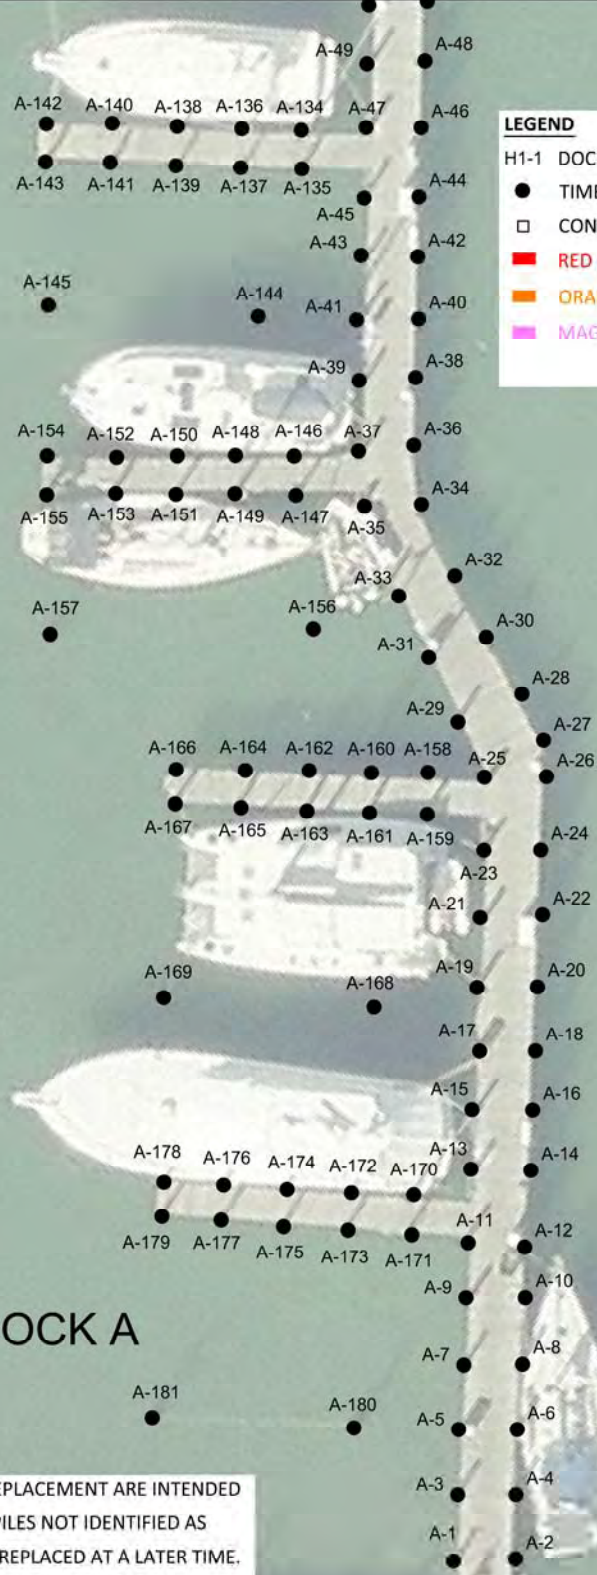

EXEMPT
 File Number:
 0137939-019-EE

Received Electronically
 November 2, 2017
 South District

DOCK A

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

HALF SHELL RAW BAR

**FOR PERMITTING
 NOT FOR CONSTRUCTION**



CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)

DOCK A PLAN VIEW

KEY WEST, MONROE COUNTY, FLORIDA

Tt TETRA TECH INC.
 759 SOUTH FEDERAL HWY
 SUITE 314
 STUART, FL 34994-2936
 TEL: (772) 781-3400
 FAX: (772) 781-3411

CERTIFICATE OF AUTHORIZATION
 NO. 2429

Designed by:
 Drawn By:
 F. MARTINEZ
 Checked By:
 S. MCGAHEE
 Date:
 10/20/17
 Design file no:
 KWB_PILE_PERMIT_SITE_V1.DWG
 Scale:
 AS SHOWN

Sheet Reference:
C-102
 Sheet 6 of 20

LEGEND

H1-1 DOCK NAME-PILE NUMBER

● TIMBER PILE

□ CONCRETE PILE


■ RED (BAD CONDITION - NEEDS REPLACEMENT)

■ ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)

■ MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

DOCK A

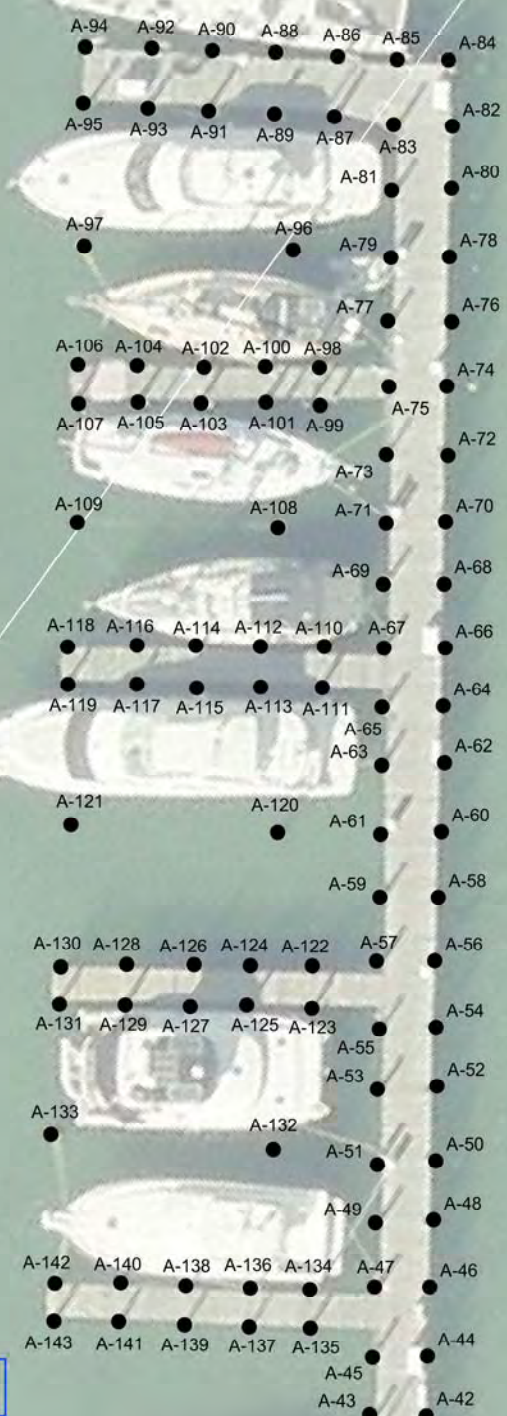


Received
Electronically
November 2, 2017
South District



DOCK A

EXEMPT
File Number:
0137939-019-EE

FOR PERMITTING
NOT FOR CONSTRUCTION



CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)

DOCK A PLAN VIEW

KEY WEST, MONROE COUNTY, FLORIDA



TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 314
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411
CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:	
Drawn By:	F. MARTINEZ
Checked By:	S. MCGAHEE
Date:	10/20/17
Design file no:	KWB_PILE_PERMIT_SITE_V1.DWG
Scale:	AS SHOWN

Sheet Reference:
C-103
Sheet 7 of 20

LEGEND

H1-1 DOCK NAME-PILE NUMBER

- TIMBER PILE
- CONCRETE PILE
- RED (BAD CONDITION - NEEDS REPLACEMENT)
- ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
- MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)


NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.



FUEL DOCK

DOCK C

DOCK C



FOR PERMITTING
NOT FOR CONSTRUCTION




CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)
 DOCK C AND FUEL DOCK PLAN VIEW
 KEY WEST, MONROE COUNTY, FLORIDA


TETRA TECH INC.
 759 SOUTH FEDERAL HWY
 SUITE 314
 STUART, FL 34994-2936
 TEL: (772) 781-3400
 FAX: (772) 781-3411
 CERTIFICATE OF AUTHORIZATION
 NO. 2429

Designed by:
 Drawn By:
 F. MARTINEZ
 Checked By:
 S. MCGAHEE
 Date:
 10/20/17
 Design file no:
 KWB_PILE_PERMIT_SITE_V1.DWG
 Scale:
 AS SHOWN

Sheet Reference:
C-104
 Sheet 8 of 20

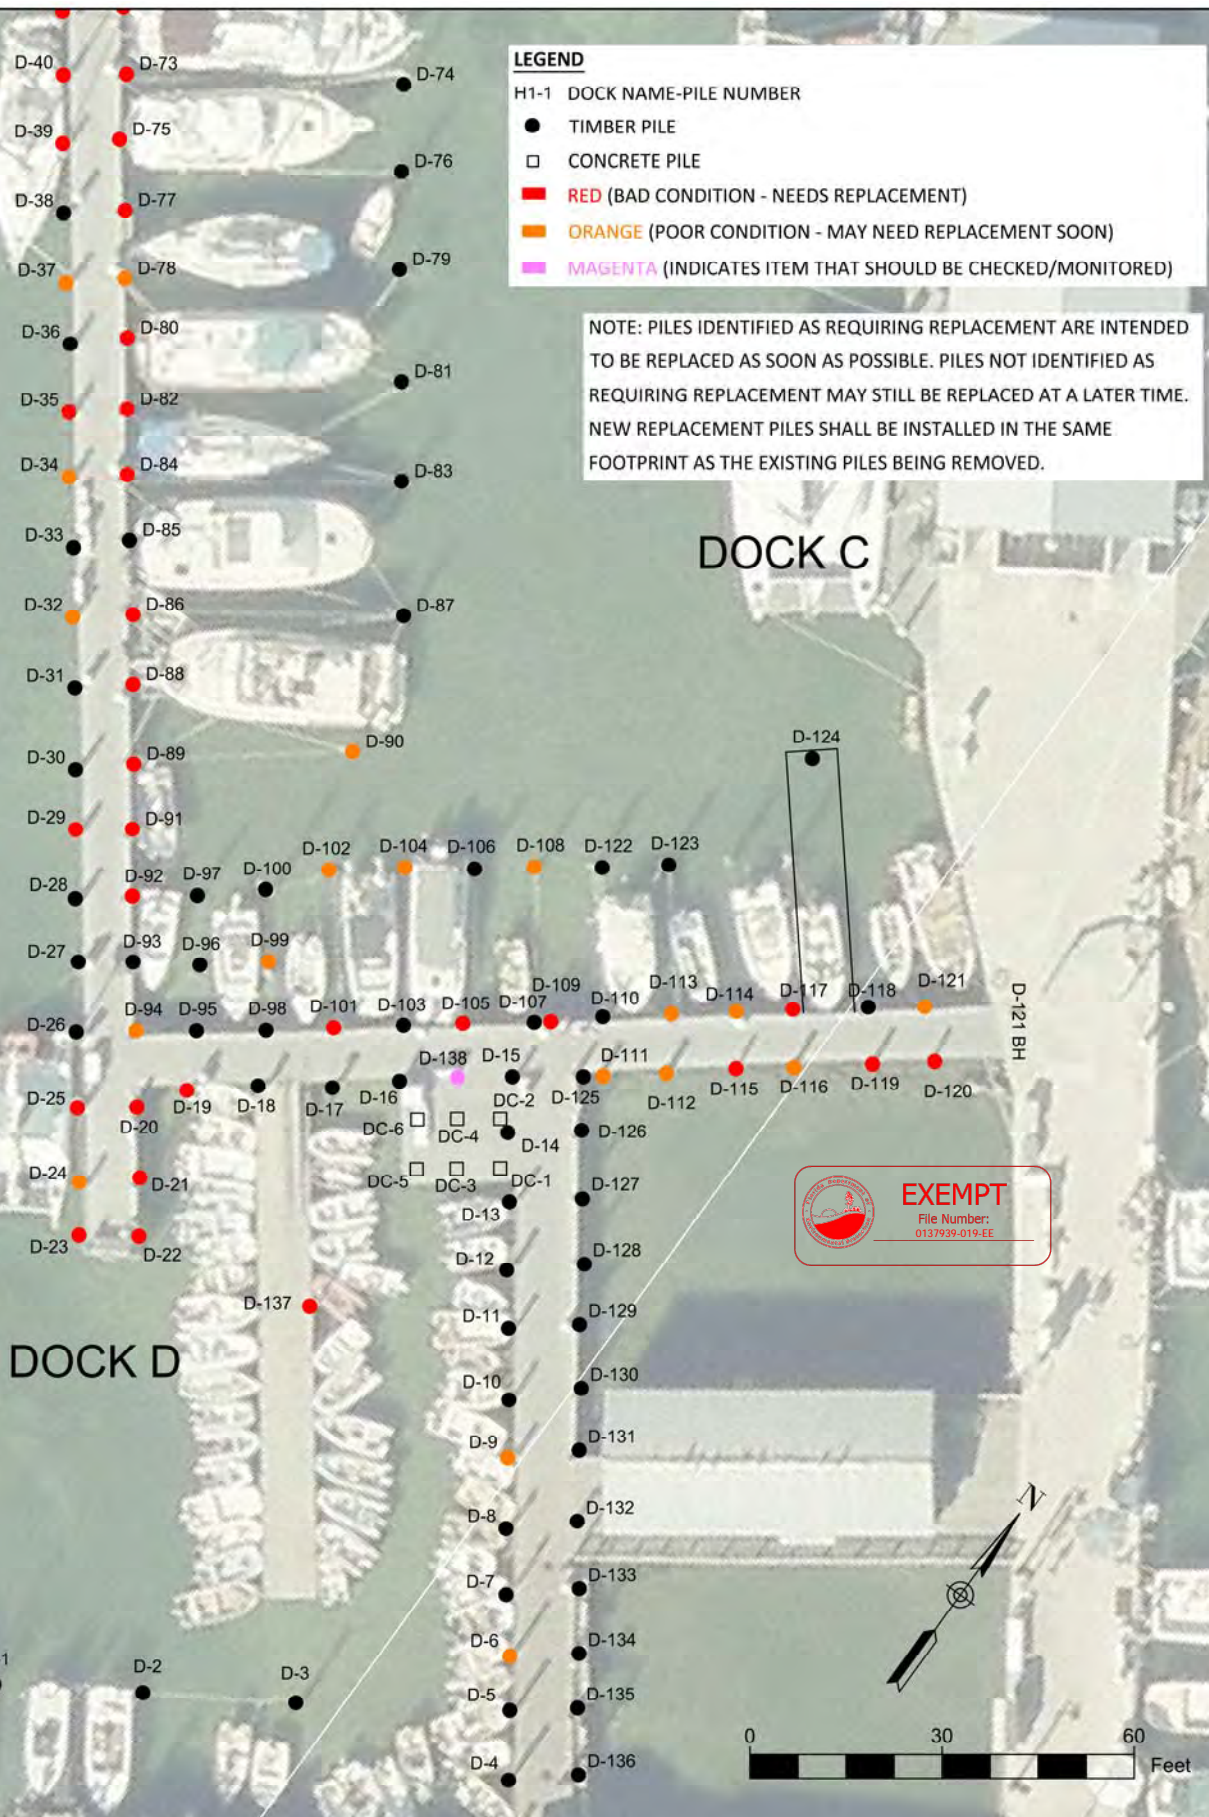

LEGEND

H1-1 DOCK NAME-PILE NUMBER

- TIMBER PILE
- CONCRETE PILE
- RED (BAD CONDITION - NEEDS REPLACEMENT)
- ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
- MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.



DOCK C

DOCK D

EXEMPT
 File Number: 0137939-019-EE

Received Electronically
 November 2, 2017
 South District

FOR PERMITTING
 NOT FOR CONSTRUCTION



CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)

DOCK D PLAN VIEW

KEY WEST, MONROE COUNTY, FLORIDA

Tt TETRA TECH INC.
 759 SOUTH FEDERAL HWY
 SUITE 314
 STUART, FL 34994-2936
 TEL: (772) 781-3400
 FAX: (772) 781-3411

CERTIFICATE OF AUTHORIZATION
 NO. 2429

Designed by:
 Drawn By: F. MARTINEZ
 Checked By: S. MCGAHEE
 Date: 10/20/17
 Design file no: KWB_PILE_PERMIT_SITE_V1.DWG
 Scale: AS SHOWN

Sheet Reference:
C-105
 Sheet 9 of 20

Received
Electronically
November 2, 2017
South District



LEGEND

H1-1 DOCK NAME-PILE NUMBER

- TIMBER PILE
- CONCRETE PILE
- RED (BAD CONDITION - NEEDS REPLACEMENT)
- ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
- MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.


DOCK D

FUEL DOCK



EXEMPT
File Number:
0137939-019-EE

FOR PERMITTING
NOT FOR CONSTRUCTION

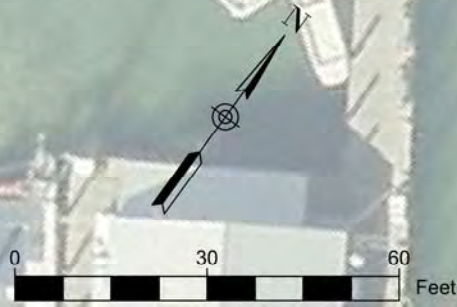

CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)

DOCK D PLAN VIEW


KEY WEST, MONROE COUNTY, FLORIDA

Tt TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 314
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411

CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:
Drawn By:
F. MARTINEZ
Checked By:
S. MCGAHEE
Date:
10/20/17
Design file no:
KWB_PILE_PERMIT_SITE_V1.DWG
Scale:
AS SHOWN

Sheet Reference:
C-106
Sheet 10 of 20

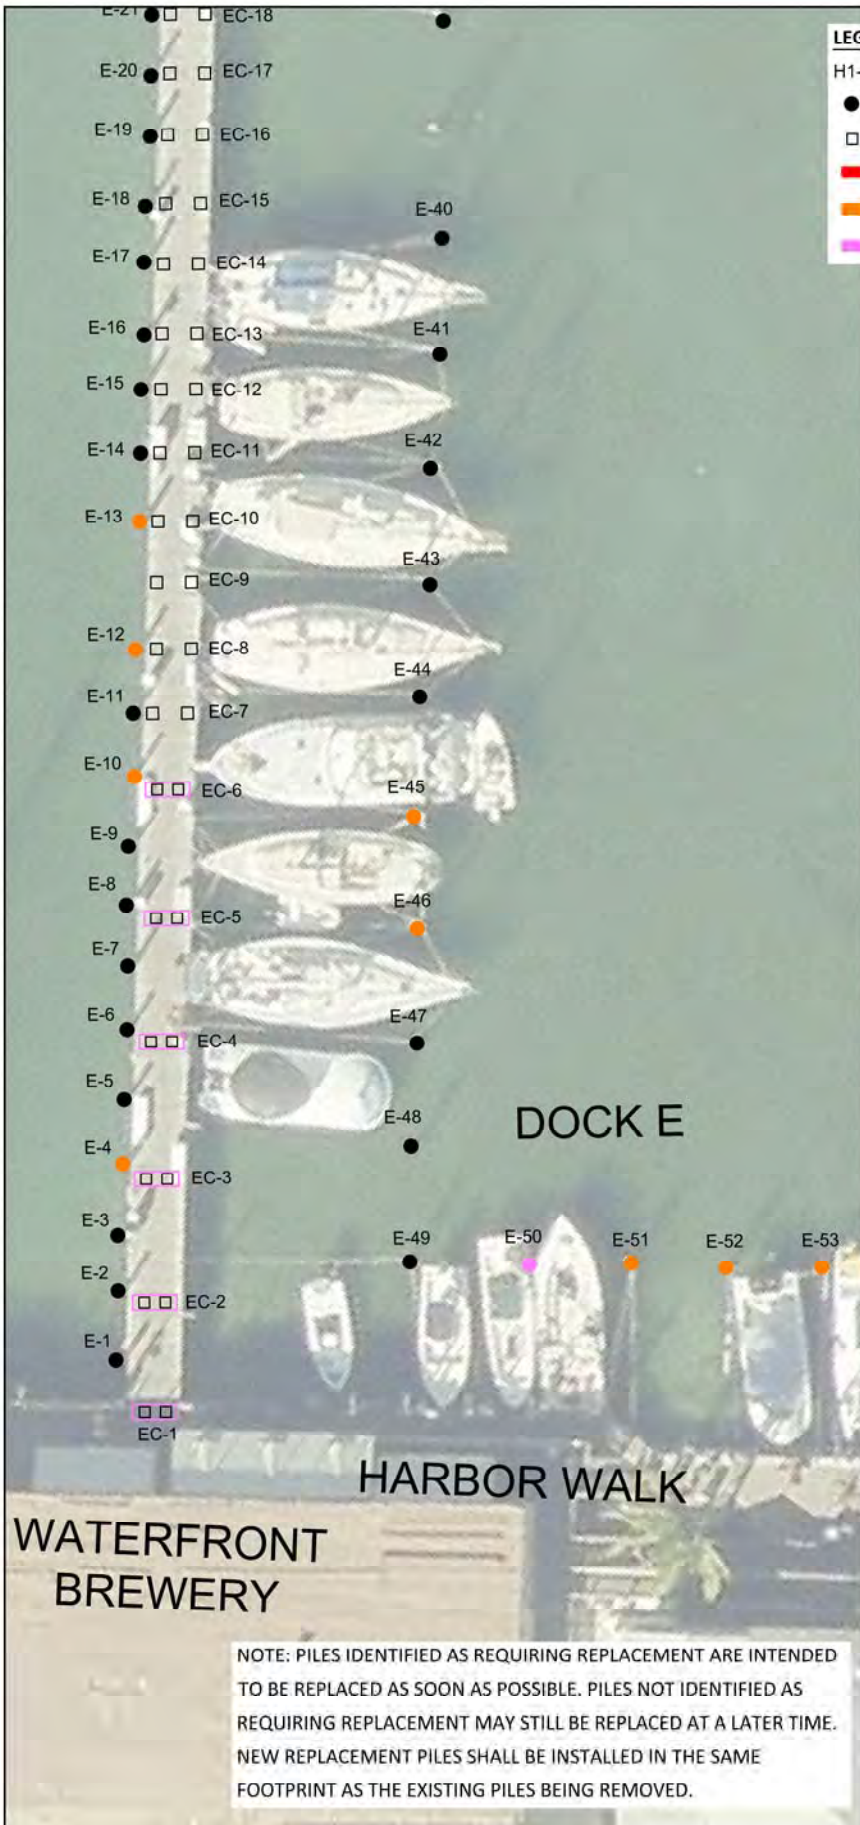

LEGEND

H1-1 DOCK NAME-PILE NUMBER

● TIMBER PILE

□ CONCRETE PILE

■ RED (BAD CONDITION - NEEDS REPLACEMENT)


■ ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)

■ MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

Received
Electronically
November 2, 2017
South District



DOCK E


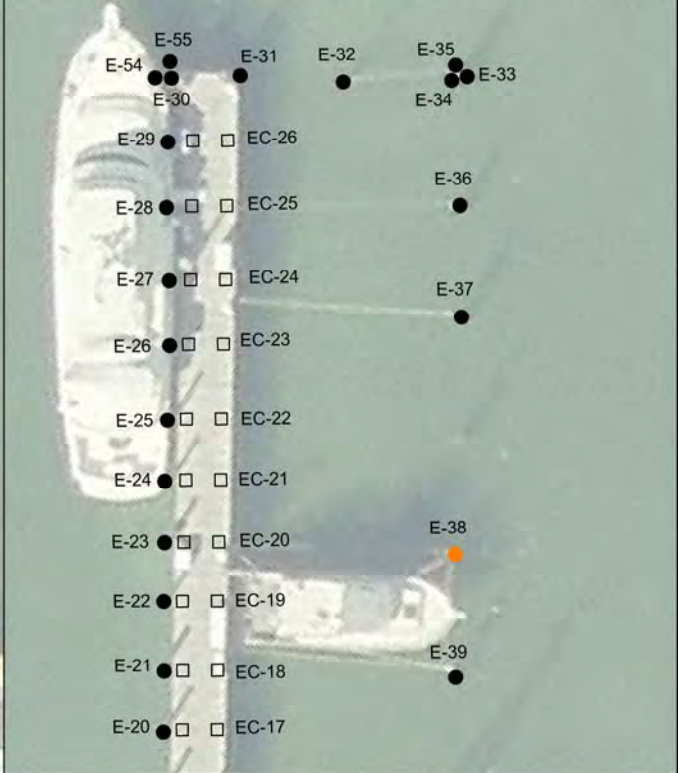


HARBOR WALK
WATERFRONT BREWERY

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

FOR PERMITTING
NOT FOR CONSTRUCTION

EXEMPT
File Number:
0137939-019-EE

CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)

DOCK E PLAN VIEW

KEY WEST, MONROE COUNTY, FLORIDA

Tt TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 314
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411

CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:
Drawn By:
F. MARTINEZ
Checked By:
S. MCGAHEE
Date:
10/20/17
Design file no:
KWB_PILE_PERMIT_SITE_V1.DWG
Scale:
AS SHOWN

Sheet Reference:
C-107
Sheet 11 of 20

LEGEND

H1-1 DOCK NAME-PILE NUMBER


- TIMBER PILE
- CONCRETE PILE
- RED (BAD CONDITION - NEEDS REPLACEMENT)
- ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
- MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

Received
Electronically
November 2, 2017
South District



DOCK F




SCHOONER WHARF

HARBOR WALK

WATERFRONT MARKET

WATERFRONT BREWERY

EXEMPT
File Number:
0137939-019-EE



FOR PERMITTING
NOT FOR CONSTRUCTION



CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)

DOCK F PLAN VIEW

KEY WEST, MONROE COUNTY, FLORIDA

Tt TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 314
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411

CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:
Drawn By:
F. MARTINEZ
Checked By:
S. MCGAHEE
Date:
10/20/17
Design file no:
KWB_PILE_PERMIT_SITE_V1.DWG
Scale:
AS SHOWN

Sheet Reference:
C-108
Sheet 12 of 20

LEGEND

H1-1 DOCK NAME-PILE NUMBER

● TIMBER PILE

□ CONCRETE PILE

■ RED (BAD CONDITION - NEEDS REPLACEMENT)

■ ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)

■ MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

Received Electronically

November 2, 2017

South District



DOCK G1
(FLOATING)

G-1

DOCK G2
(FLOATING)

G-4

G-3

G-2

DOCK G3
(FLOATING)

G-9

G-8

G-7

G-6

G-5

G-11

G-12

DOCK F

HARBOR WALK

SCHOONER WHARF



FOR PERMITTING
NOT FOR CONSTRUCTION



CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)
DOCK G PLAN VIEW
KEY WEST, MONROE COUNTY, FLORIDA



TETRA TECH INC.
750 SOUTH FEDERAL HWY
SUITE 111
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411
CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:

Drawn By:
F. MARTINEZ

Checked By:
S. MCGAHEE

Date:
10/20/17

Design File No:
WFL_PILING_S&P_V1.Dwg

Scale:
AS SHOWN

Sheet Reference:

C-109

Sheet 13 of 20



EXEMPT

File Number:
0137939-019-EE

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

LEGEND

H1-1 DOCK NAME-PILE NUMBER

● TIMBER PILE


□ CONCRETE PILE

■ RED (BAD CONDITION - NEEDS REPLACEMENT)

■ ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)

■ MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)


CONCH REPUBLIC RESTAURANT

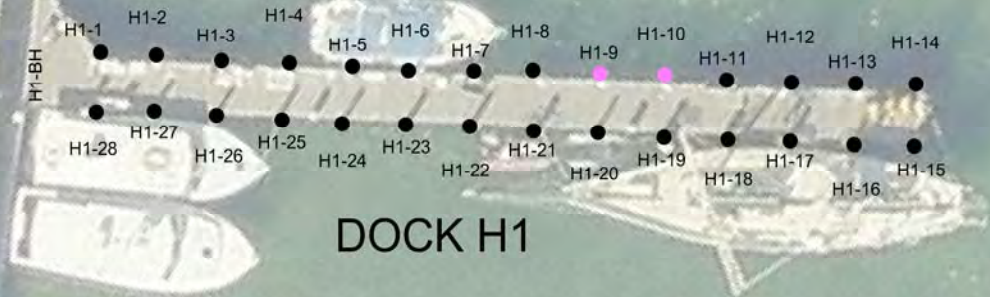


DOCK H1



DOCK H2



DOCK H3



FOR PERMITTING
NOT FOR CONSTRUCTION



CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)
DOCK H PLAN VIEW
KEY WEST, MONROE COUNTY, FLORIDA



TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 314
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411
CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:
Drawn By: F. MARTINEZ
Checked By: S. MCGAHEE
Date: 10/20/17
Design file no: KWB_PILE_PERMIT_SITE_V1.DWG
Scale: AS SHOWN

Sheet Reference:
C-110
Sheet 14 of 20

DOCK G1 (FLOATING)

HARBOR WALK

SCHOONER WHARF

HARBOR WALK

WATERFRONT MARKET

WATERFRONT BREWERY

DOCK F


NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.



LEGEND

H1-1 DOCK NAME-PILE NUMBER

- TIMBER PILE
- CONCRETE PILE
- RED (BAD CONDITION - NEEDS REPLACEMENT)
- ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
- MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)



CITY OF KEY WEST
 KEY WEST BIGHT MARINA MAINTENANCE
 (PILING REPLACEMENT DOCK REPAIR)
 HARBOR WALK PLAN VIEW
 KEY WEST, MONROE COUNTY, FLORIDA

TF TETRA TECH INC.
 759 SOUTH FEDERAL HWY
 SUITE 200 FL 34994-2936
 TEL: (772) 781-3400
 FAX: (772) 781-3411
 CERTIFICATE OF AUTHORIZATION
 NO. 2429

Received Electronically
 November 2, 2017
 South District




Designed by:
 Drawn By: F. MARTINEZ
 Checked By: S. MCGAHEE
 Date: 10/20/17
 Design File No: HAR_WALK_Plan_View
 Scale: AS SHOWN

FOR PERMITTING
 NOT FOR CONSTRUCTION

Sheet Reference:
C-111
 Sheet 15 of 20

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

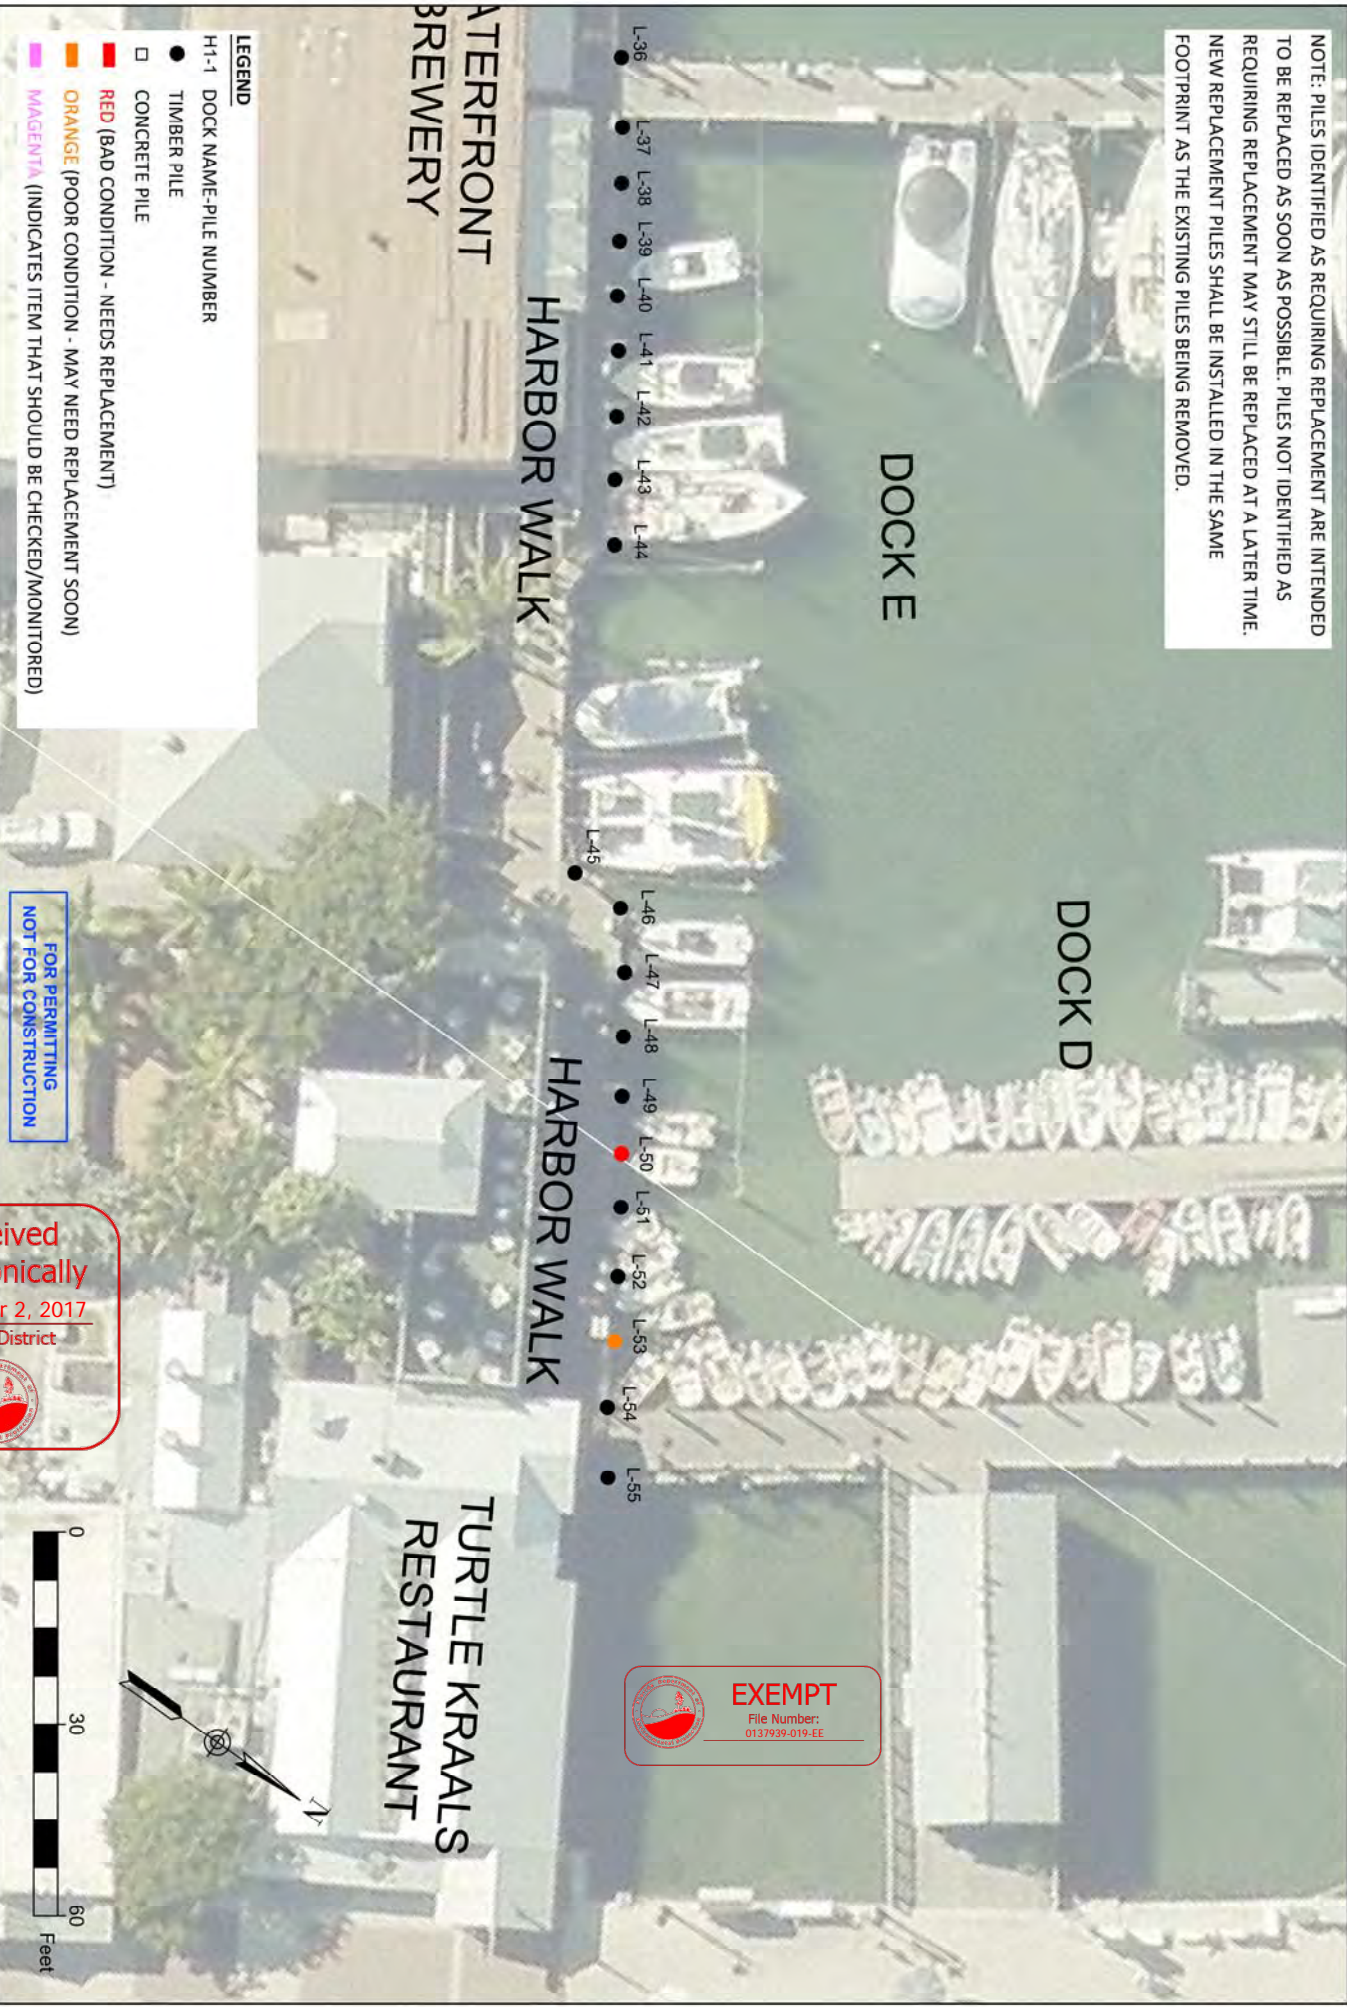

EXEMPT
File Number:
0137939-019-EE

- LEGEND**
- H1-1 DOCK NAME-PILE NUMBER
 - TIMBER PILE
 - CONCRETE PILE
 - RED (BAD CONDITION - NEEDS REPLACEMENT)
 - ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
 - MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

FOR PERMITTING
NOT FOR CONSTRUCTION



CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)
HARBOR WALK PLAN VIEW
KEY WEST, MONROE COUNTY, FLORIDA

TF TETRA TECH INC.
769 SOUTH FEDERAL HWY
SUITE 111 FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411
CERTIFICATE OF AUTHORIZATION
NO. 2429

Received
Electronically
November 2, 2017
South District



Designed by:
Drawn By:
Checked By:
Date:
Design File no:
Scale:
AS SHOWN


Sheet Reference:
C-112
Sheet 16 of 20

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

Received
Electronically
November 2, 2017
South District



EXEMPT
File Number:
0137939-019-EE

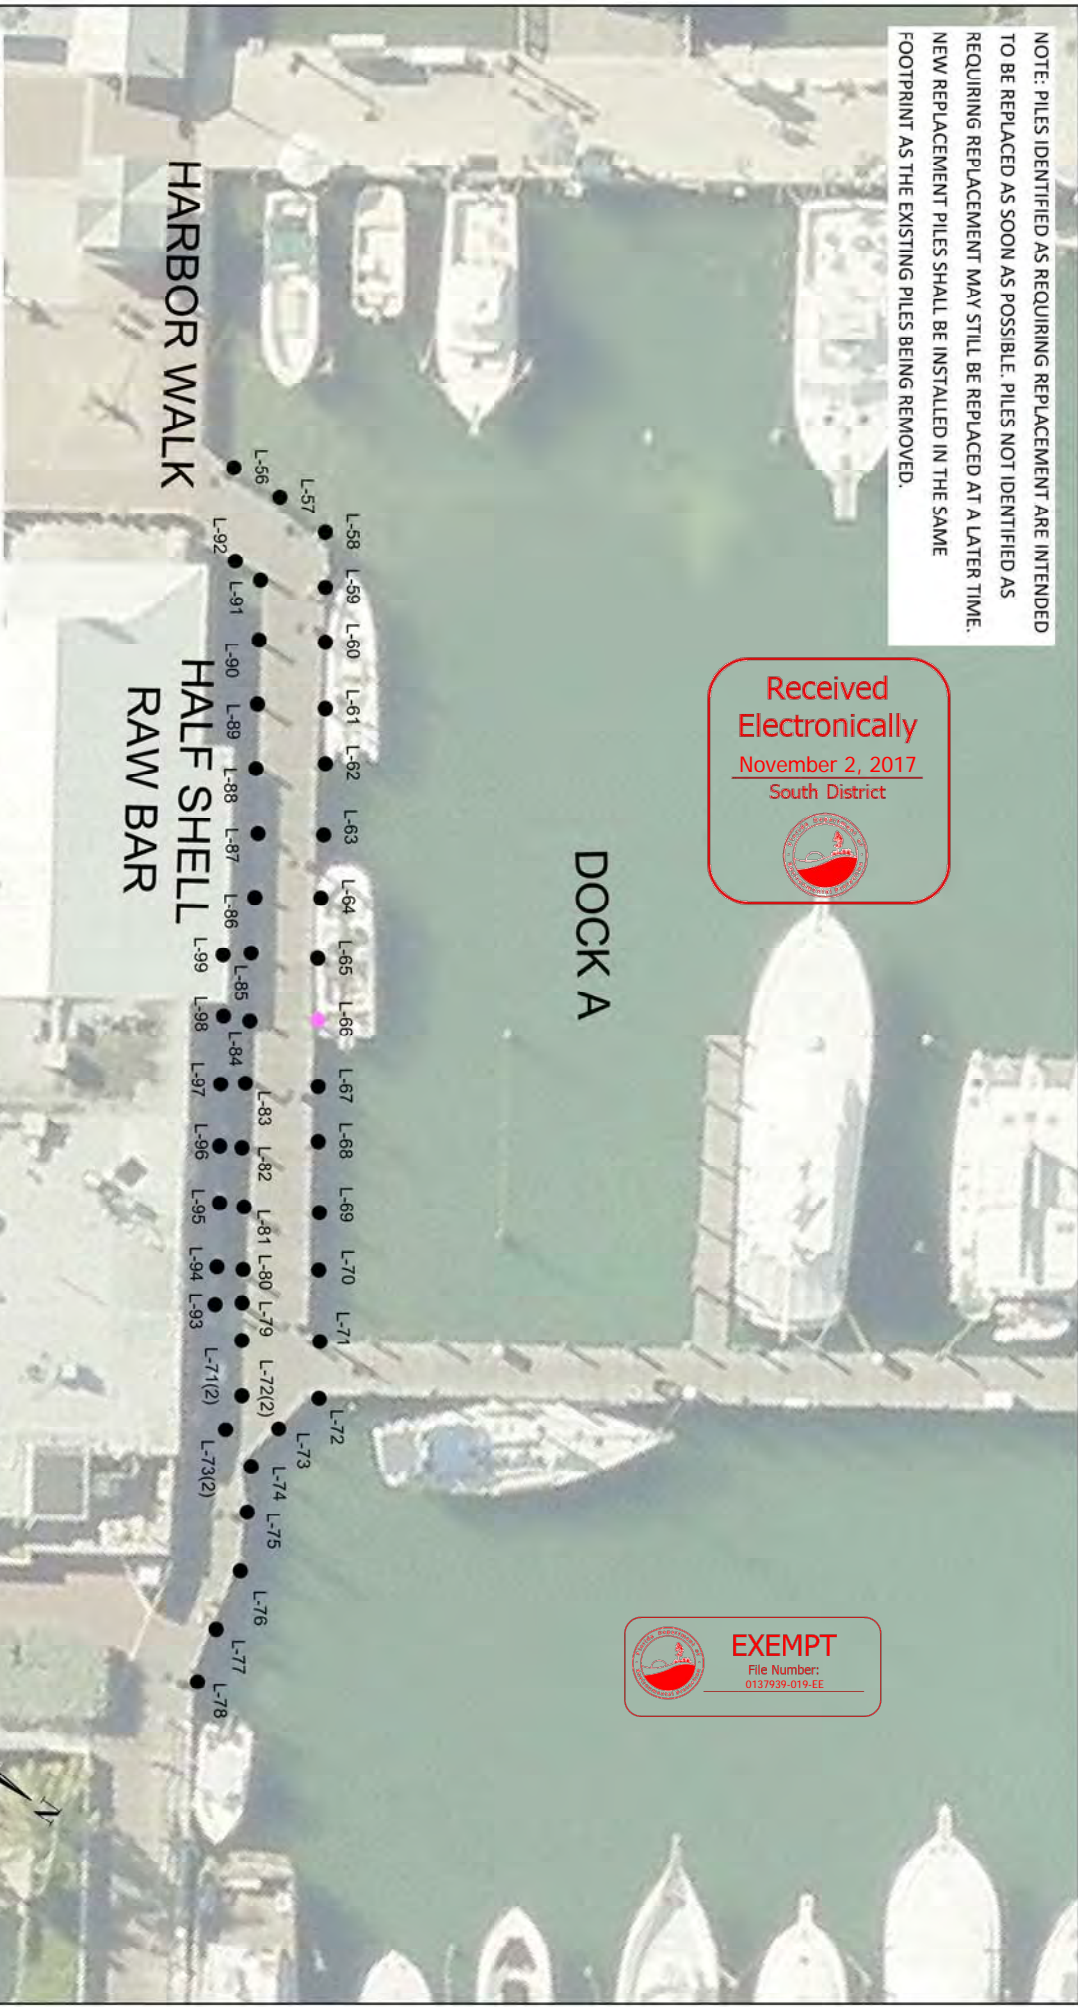LEGEND

H1-1 DOCK NAME-PILE NUMBER

- TIMBER PILE
- CONCRETE PILE
- RED (BAD CONDITION - NEEDS REPLACEMENT)
- ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
- MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

FOR PERMITTING
NOT FOR CONSTRUCTION




CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)
DOCK G PLAN VIEW
KEY WEST, MONROE COUNTY, FLORIDA

TF TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 111 STULZER FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411
CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:
Drawn By: F. MARTINEZ
Checked By: S. MCGAHEE
Date: 10/20/17
Design file no: WWP170117-019-EE
WWP170117-019-EE.dwg
Scale: AS SHOWN

Sheet Reference:
C-113
Sheet 17 of 20

Received
Electronically
November 2, 2017
South District

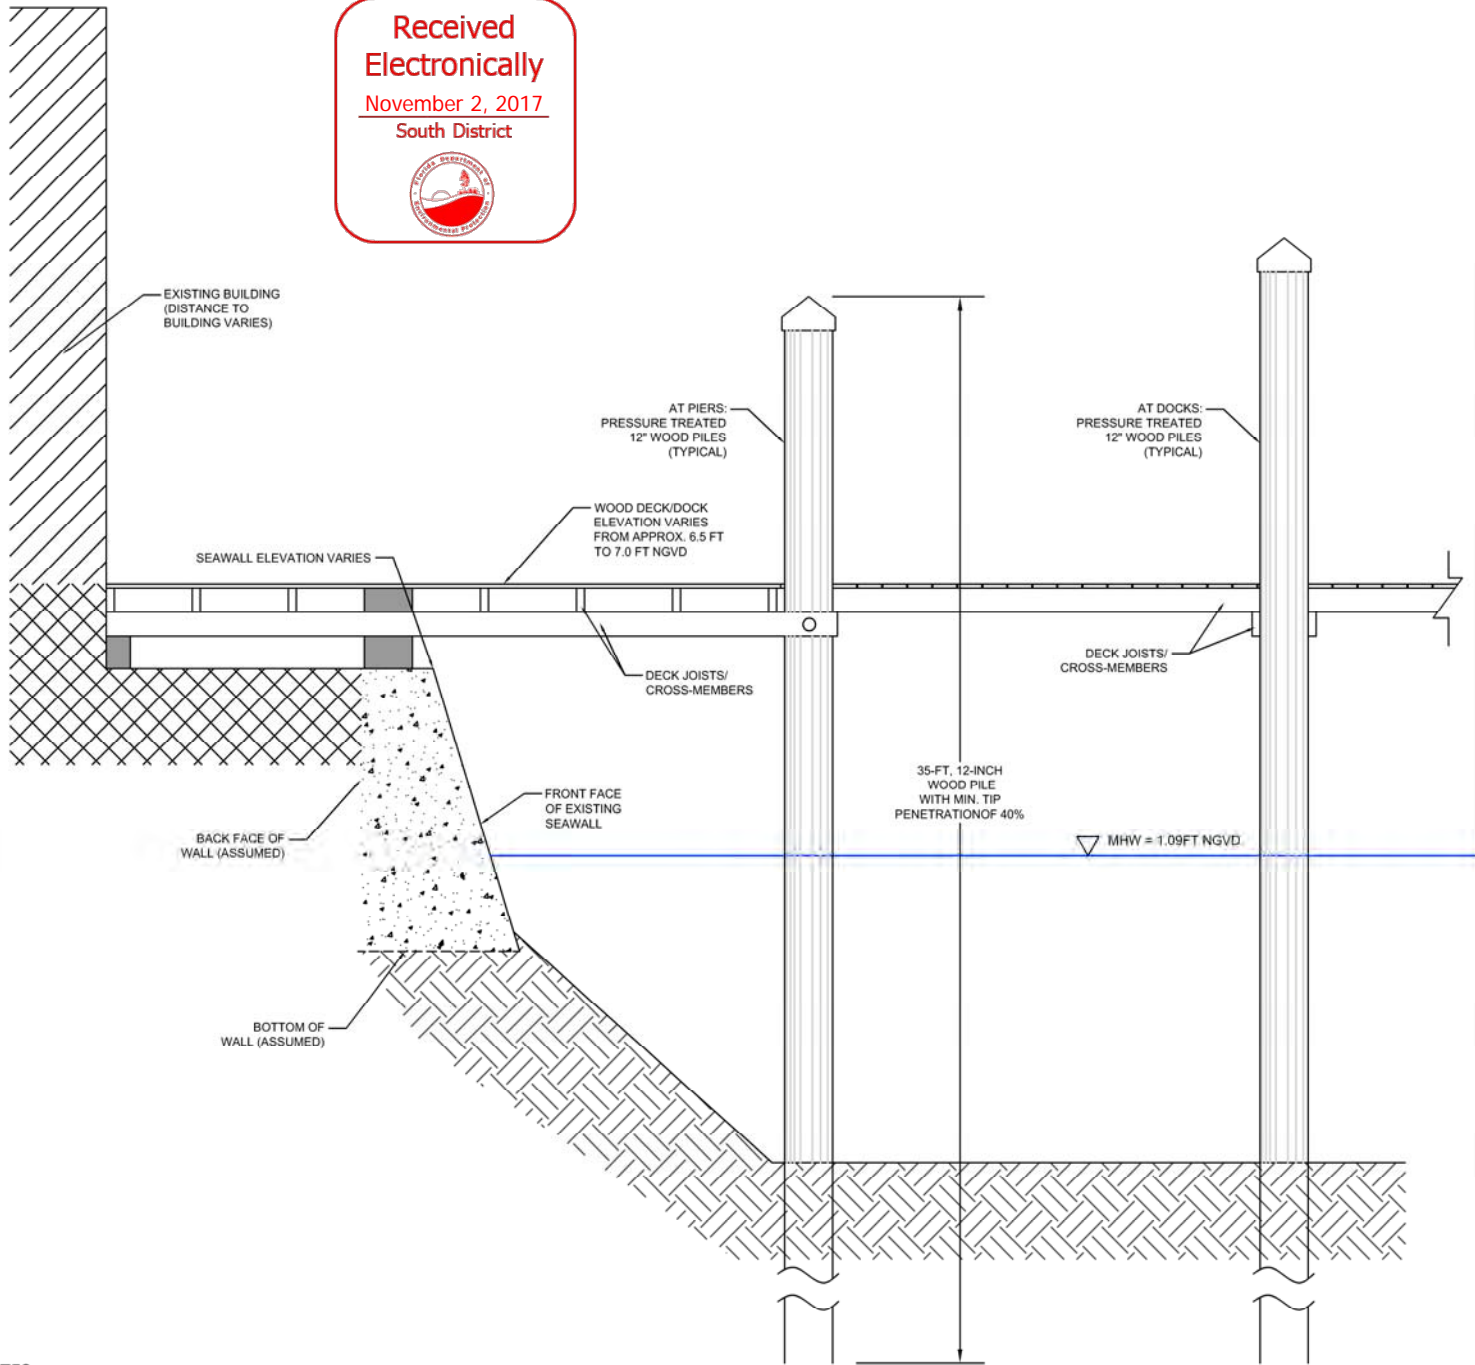

NOTES:

1. THIS CROSS-SECTION IS REPRESENTATIVE OF THE APPROXIMATE CONDITIONS/ELEVATIONS IN DOCK E, DOCK F, AND THE HARBOR WALK PIER IN FRONT OF THE WATERFRONT MARKET AND BREWERY.
2. WOOD PILES TO BE REPLACED INCLUDE STRUCTURAL AND FENDER PILES, 12" DIAMETER, APPROX. 35' MIN. LENGTH.
3. THE REPLACEMENT PILES ARE TO BE PLACED IN THE RESULTANT VOID CREATED BY REMOVAL OF THE EXISTING PILE.

DOCK AND DECK CROSS-SECTION
(DOCK E, DOCK F, AND HARBOR WALK PIER)
[NOT TO SCALE]



FOR PERMITTING
NOT FOR CONSTRUCTION



CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)
CROSS-SECTION DETAIL
KEY WEST, MONROE COUNTY, FLORIDA




TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 314
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411
CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:
Drawn By: F. MARTINEZ
Checked By: S. MCGAHEE
Date: 10/20/17
Design file no: KWB_PILE_PERMIT_SITE_V1.DWG
Scale: AS SHOWN

Sheet Reference:
C-114
Sheet 18 of 20

**Received
Electronically**
November 2, 2017
South District

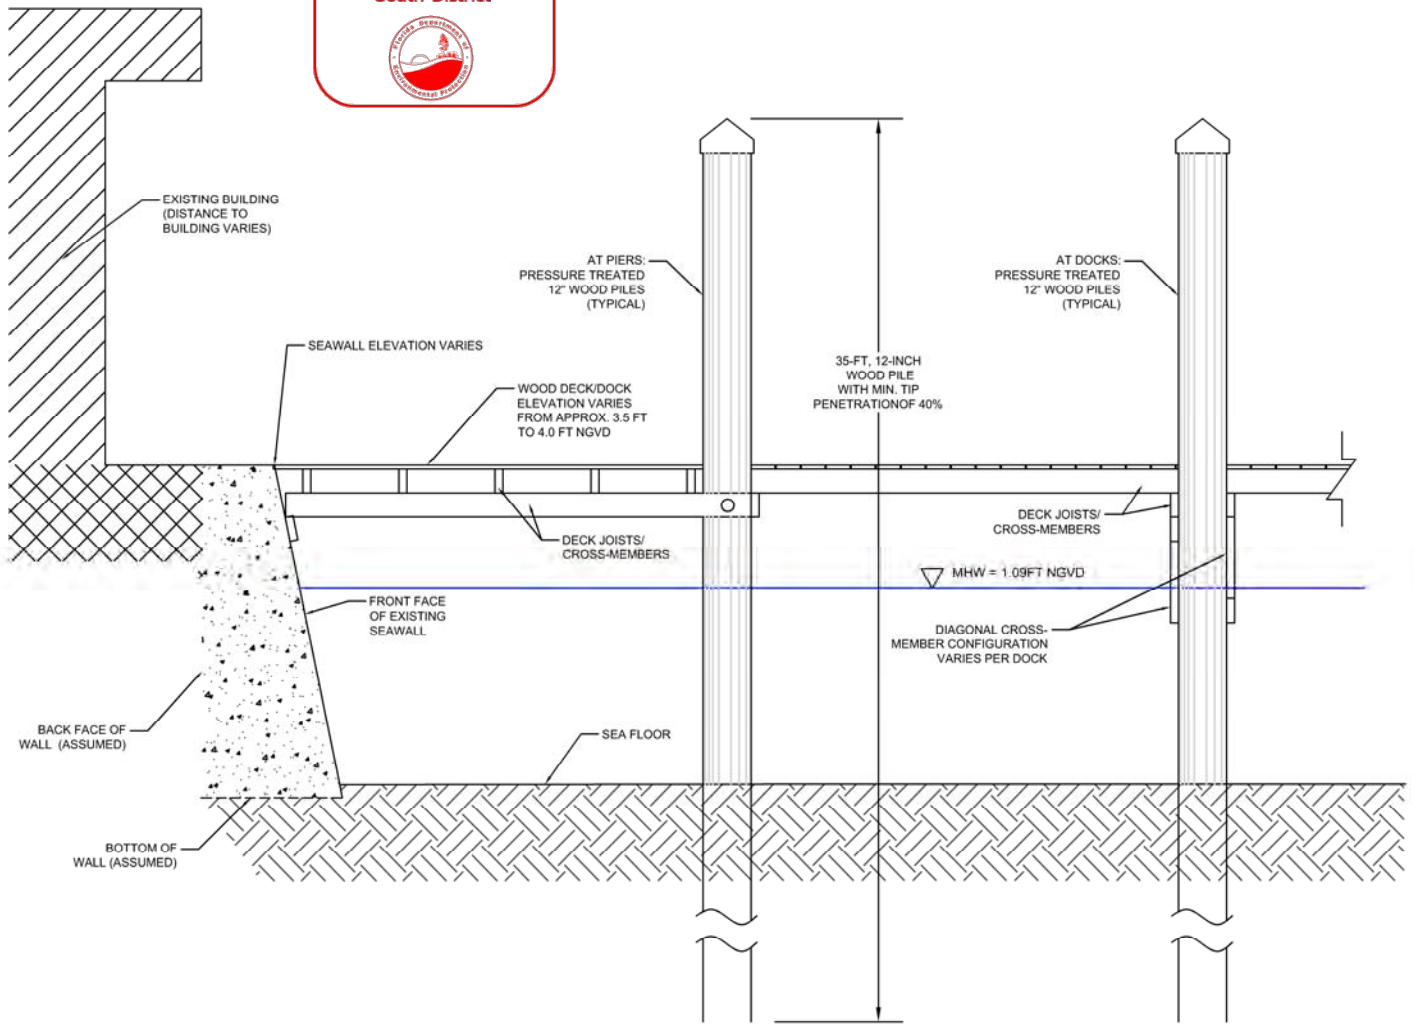DOCK AND DECK CROSS-SECTION
(DOCK A, DOCK C, DOCK D, DOCK H, AND HARBOR WALK PIER)
[NOT TO SCALE]

- NOTES:**
1. THIS CROSS-SECTION IS REPRESENTATIVE OF THE APPROXIMATE CONDITIONS/ELEVATIONS OF DOCK A, DOCK C, DOCK D, DOCK H, AND THE HARBOR WALK PIER OUTSIDE OF THE AREA IN FRONT OF THE WATERFRONT MARKET AND BREWERY. DOCK H IS CONNECTED DIRECTLY TO THE SEAWALL, WITHOUT A WOOD PIER WALKWAY.
 2. WOOD PILES TO BE REPLACED INCLUDE STRUCTURAL AND FENDER PILES, 12" DIAMETER, APPROX. 35' MIN. LENGTH.
 3. THE REPLACEMENT PILES ARE TO BE PLACED IN THE RESULTANT VOID CREATED BY REMOVAL OF THE EXISTING PILE.

 **EXEMPT**
File Number:
0137939-019-EE

**FOR PERMITTING
NOT FOR CONSTRUCTION**



CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)

CROSS-SECTION DETAIL

KEY WEST, MONROE COUNTY, FLORIDA


 **TETRA TECH INC.**
759 SOUTH FEDERAL HWY
SUITE 314
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411

CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:
Drawn By: F. MARTINEZ
Checked By: S. MCGAHEE
Date: 10/20/17
Design file no: KW_PILE_PERMIT_SITE_V1.DWG
Scale: AS SHOWN

Sheet Reference:
C-115
Sheet 19 of 20

**Received
Electronically**
November 2, 2017
South District

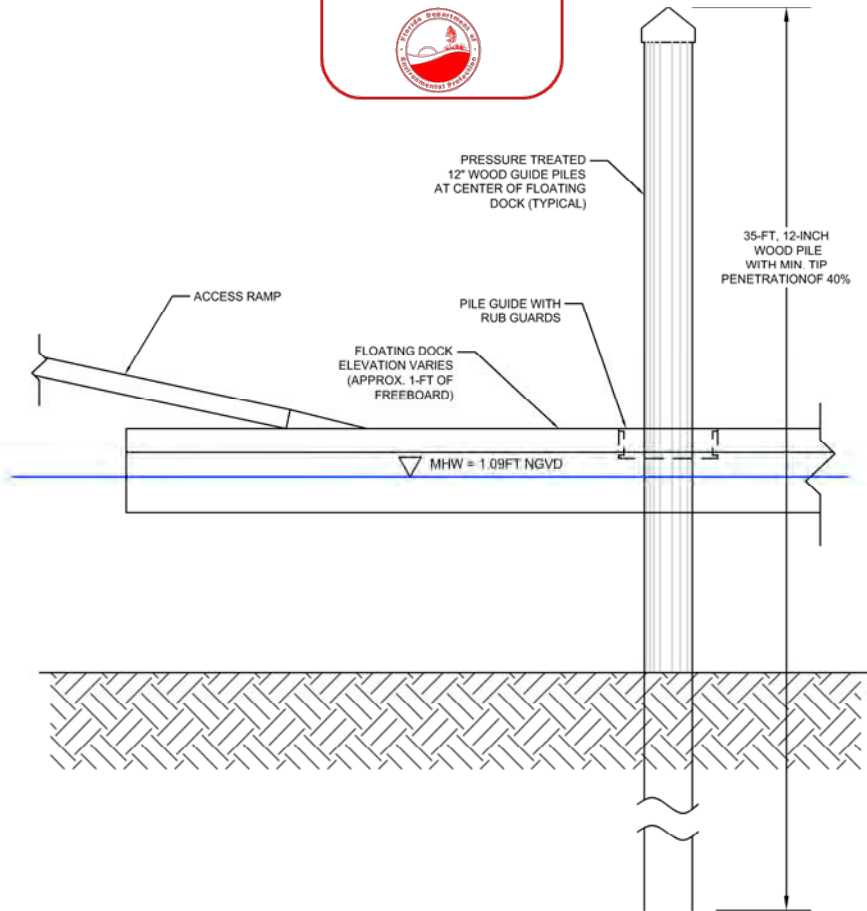**FLOATING DOCK CROSS-SECTION
(DOCK D AND DOCK G)
[NOT TO SCALE]**

NOTES:

1. THIS CROSS-SECTION IS REPRESENTATIVE OF THE APPROXIMATE CONDITIONS/ELEVATIONS OF THE FLOATING DOCK SECTIONS OF DOCK D, AND DOCK G.
2. WOOD PILES TO BE REPLACED INCLUDE STRUCTURAL PILES, 12" DIAMETER, APPROX. 35' MIN. LENGTH.
3. THE REPLACEMENT PILES ARE TO BE PLACED IN THE RESULTANT VOID CREATED BY REMOVAL OF THE EXISTING PILE.



**FOR PERMITTING
NOT FOR CONSTRUCTION**



**CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)**

CROSS-SECTION DETAIL

KEY WEST, MONROE COUNTY, FLORIDA



TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 314
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411

CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:
Drawn By: F. MARTINEZ
Checked By: S. MCGAHEE
Date: 10/20/17
Design file no: KWB_PILE_PERMIT_SITE_V1.DWG
Scale: AS SHOWN

Sheet Reference:
C-116
Sheet 20 of 20

373.406 Exemptions.—The following exemptions shall apply:

(6) Any district or the department may exempt from regulation under this part those activities that the district or department determines will have only minimal or insignificant individual or cumulative adverse impacts on the water resources of the district. The district and the department are authorized to determine, on a case-by-case basis, whether a specific activity comes within this exemption. Requests to qualify for this exemption shall be submitted in writing to the district or department, and such activities shall not be commenced without a written determination from the district or department confirming that the activity qualifies for the exemption.

History.—s. 2, part IV, ch. 72-299; s. 47, ch. 79-65; s. 5, ch. 80-259; s. 2, ch. 82-101; s. 12, ch. 89-279; s. 268, ch. 94-356; s. 2, ch. 95-215; s. 2, ch. 96-370; s. 15, ch. 98-203; s. 21, ch. 98-333; s. 2, ch. 2000-130; s. 2, ch. 2002-253; s. 6, ch. 2011-164; s. 1, ch. 2011-165; s. 14, ch. 2013-92.



DEPARTMENT OF THE ARMY
JACKSONVILLE DISTRICT CORPS OF ENGINEERS
MIAMI REGULATORY OFFICE
9900 SOUTHWEST 107th Ave, SUITE 203
MIAMI, FLORIDA 33176

REPLY TO
ATTENTION OF

July 10, 2018

Regulatory Division
South Permits Branch
Miami Section
SAJ-2017-01874-(NW-GGM)

City of Key West
c/o Doug Bradshaw, Director, Port of Marine Services
201 William Street
Key West, FL 33040

Dear Applicant:

Your application for a Department of the Army permit received on February 9, 2018, has been assigned number SAJ-2017-01874. A review of the information and drawings provided to the Corps shows the work is to repair and replace a maximum of 662 wood pilings in the same footprint, as depicted on the attached approved drawings (20 pages) date stamped 10 July 2018 by the Corps. Turbidity curtains will be deployed in/over waters of the United States and will remain in place until the work is completed and erodible materials have stabilized.

The project would affect waters of the United States associated with Key West Bight (aka Key West Harbor). The project site is located within a commercial marina basin, adjacent to 120 Margaret Street 101 within the Historic Waterfront of the Old Town District of Key West, in Section 31, Township 67 South, Range 25 East, Key West, Monroe County, Florida. (RE#s 00072082-004700, 00072082-003800, 00072082-003803, 00072082-003900, 00072082-003908, 00072082-004200) (MM± 1).

Central Geographic Position: **Latitude:** 24.5617340° North
Longitude: 81.8014300° West

Your project, as depicted on the enclosed drawings, is authorized by Nationwide Permit (NWP) Number 3. In addition, project specific conditions have been enclosed. This verification is valid until **March 18, 2022**. Furthermore, if you commence or are under contract to commence this activity before the date that the relevant nationwide permit is modified or revoked, you will have 12 months from the date of the modification or revocation of the NWP to complete the activity under the present terms and conditions of this nationwide permit. Please access the U.S. Army Corps of Engineers' (Corps) Jacksonville District's Regulatory Internet page to access Internet links to view the Final Nationwide Permits, Federal Register Vol. 82, dated January 6, 2017, specifically pages 1983 to 2008, and the table of Regional Conditions. The Internet page address is:

<http://www.saj.usace.army.mil/Missions/Regulatory.aspx>

Please be aware this Internet address is case sensitive and should be entered as it appears above. Once there you will need to click on "Source Book"; and, then click on "Nationwide Permits." These files contain the description of the Nationwide Permit authorization, the Nationwide Permit general conditions, and the regional conditions, which apply specifically to these verifications for NWP 3. Enclosed is a list of the six General Conditions, which apply to all Department of the Army authorizations. You must comply with all of the special and general conditions and any project specific condition of this authorization or you may be subject to enforcement action. In the event you have not completed construction of your project within the specified time limit, a separate application or re-verification may be required.

The following project-specific conditions are included with this authorization:

1. Reporting Address: The Permittee shall submit all reports, notifications, documentation and correspondence required by the general and special conditions of this permit to the following address:

a. For standard mail: U.S. Army Corps of Engineers, Regulatory Division, Special Projects and Enforcement Branch, 9900 Southwest 107th Avenue, Suite 203, Miami, Florida 33176.

b. For electronic mail CESAJ-ComplyDocs@usace.army.mil (not to exceed 10 MB).

The Permittee shall reference this permit number, SAJ-2017-01874 (NW-GGM), on all submittals.

2. Self-Certification: Within 60 days of completion of the work authorized by this permit, the Permittee shall complete the attached "Self-Certification Statement of Compliance" form (Attached) and submit it to the Corps. In the event that the completed work deviates in any manner from the authorized work, the Permittee shall describe the deviations between the work authorized by this permit and the work as constructed on the "Self-Certification Statement of Compliance" form. The description of any deviations on the "Self-Certification Statement of Compliance" form does not constitute approval of any deviations by the Corps.

3. Assurance of Navigation and Maintenance: The Permittee understands and agrees that, if future operations by the United States require the removal, relocation, or other alteration, of the structures or work herein authorized, or if in the opinion of the

Secretary of the Army or his authorized representative, said structure or work shall cause unreasonable obstruction to the free navigation of the navigable waters, the Permittee will be required, upon due notice from the Corps of Engineers, to remove, relocate, or alter the structural work or obstructions caused thereby, without expense to the United States. No claim shall be made against the United States on account of any such removal or alteration.

4. Manatee Conditions: The Permittee shall comply with the “Standard Manatee Conditions for In-Water Work – 2011” (Attached).

5. Sea Turtle and Smalltooth Sawfish Conditions: The Permittee shall comply with National Marine Fisheries Service's “Sea Turtle and Smalltooth Sawfish Construction Conditions” dated March 23, 2006 (Attached).

6. Posting of Permit: The Permittee shall ensure that all contractors, sub-contractors, and entities associated with the implementation of the project review, understand, and comply with the approved plans and special conditions made part of this permit. The Permittee shall inform all parties associated with the activity of the construction area boundaries, and the location of adjacent submerged aquatic resources (i.e. corals, seagrass) to be avoided. Complete copies of the permit and approved plans shall be available at the construction site at all times. Failure to comply with the approved plans and permit special conditions may subject the Permittee to enforcement action.

7. Agency Changes/Approvals: Should any other agency require and/or approve changes to the work authorized or obligated by this permit, the Permittee is advised a re-verification to this permit instrument is required prior to initiation of those changes. It is the Permittee's responsibility to request a re-verification of this permit from the **Miami** Permits Section. The Corps reserves the right to fully evaluate, amend, and approve or deny the request for re-verification of this permit.

8. Historic Properties:

a. No structure or work shall adversely affect impact or disturb properties listed in the National Register of Historic Places (NRHP) or those eligible for inclusion in the NRHP.

b. If during the ground disturbing activities and construction work within the permit area, there are archaeological/cultural materials encountered which were not the subject of a previous cultural resources assessment survey (and which shall include, but not be limited to: pottery, modified shell, flora, fauna, human remains, ceramics, stone tools or metal implements, dugout canoes, evidence of structures or any other physical remains that could be associated with Native American cultures or early colonial or American settlement), the Permittee shall immediately stop all work and

ground-disturbing activities within a 100-meter diameter of the discovery and notify the Corps within the same business day (8 hours). The Corps shall then notify the Florida State Historic Preservation Officer (SHPO) and the appropriate Tribal Historic Preservation Officer(s) (THPO(s)) to assess the significance of the discovery and devise appropriate actions.

c. Additional cultural resources assessments may be required of the permit area in the case of unanticipated discoveries as referenced in accordance with the above Special Condition ; and if deemed necessary by the SHPO, THPO(s), or Corps, in accordance with 36 CFR 800 or 33 CFR 325, Appendix C (5). Based, on the circumstances of the discovery, equity to all parties, and considerations of the public interest, the Corps may modify, suspend or revoke the permit in accordance with 33 CFR Part 325.7. Such activity shall not resume on non-federal lands without written authorization from the SHPO for finds under his or her jurisdiction, and from the Corps.

d. In the unlikely event that unmarked human remains are identified on non-federal lands, they will be treated in accordance with Section 872.05 Florida Statutes. All work and ground disturbing activities within a 100-meter diameter of the unmarked human remains shall immediately cease and the Permittee shall immediately notify the medical examiner, Corps, and State Archeologist within the same business day (8-hours). The Corps shall then notify the appropriate SHPO and THPO(s). Based, on the circumstances of the discovery, equity to all parties, and considerations of the public interest, the Corps may modify, suspend or revoke the permit in accordance with 33 CFR Part 325.7. Such activity shall not resume without written authorization from the State Archeologist and from the Corps.

9. Florida Keys National Marine Sanctuary: This Corps permit does not authorize you to damage, diminish, degrade, impair, destroy, or otherwise harm any Florida Keys National Marine Sanctuary (FKNMS) trust resource. In order to legally conduct your work, you are provided with a copy of the FKNMS letter of authorization (FKNMS-2017-138) dated February 13, 2018. You must understand and agree to comply with the provisions of this document. The FKNMS letter contains mandatory terms and conditions. Your authorization under this Corps permit is conditional upon your compliance with all of the mandatory terms and conditions associated with the FKNMS requirements, which terms and conditions are incorporated by reference in this permit. Failure to comply with the terms and conditions would constitute noncompliance with your Corps permit. The FKNMS is the appropriate authority to determine compliance with the terms and conditions of its requirements and with the Marine Protection, Research, and Sanctuaries Act of 1972 (16 U.S.C. 1432).

10. Project Design Criteria (PDCs) For In-Water Activities: The Permittee shall comply with National Marine Fisheries Service's "PDCs for In-Water Activities" dated November 20, 2017 (Attached).

11. TURBIDITY CONTROLS:

- a. Shall be used throughout construction to control erosion and siltation and ensure that turbidity levels within the project area do not exceed background conditions.
- b. Shall be made of material in which listed species cannot become entangled (i.e., reinforced impermeable polycarbonate vinyl fabric [PVC]), and shall be monitored to ensure listed species are not entangled or trapped in the project area.
- c. Shall be removed promptly when the work is complete and the water quality in the project area has returned to background conditions.
- d. Shall not block entry to or exit from designated critical habitat.

12. DAYLIGHT HOURS: All activities must be completed during daylight hours.

13. CONSTRUCTION LOCATION: All work is to be performed from land. No in-water work is authorized under this letter of authorization.

14. NOISE EFFECTS BMPS: All projects shall comply with the requirements of the attached "Noise Best Management Practices (BMPs) for Piling Installation" (Attached).

15. PROJECT DRAWINGS: The project must be completed in accordance with the enclosed construction drawings (20 pages), date-stamped by the U.S. Army Corps of Engineers (Corps) on July 10, 2018 and the general and special conditions which are incorporated in, and made a part of, the permit.

This authorization does not include conditions that would prevent the 'take' of a state-listed fish or wildlife species. These species are protected under sec. 379.411, Florida Statutes, and listed under Rule 68A-27, Florida Administrative Code. With regard to fish and wildlife species designated as species of special concern or threatened by the State of Florida, you are responsible for coordinating directly with the Florida Fish and Wildlife Conservation Commission (FWC). Permittees can visit the FWC license and permitting webpage (<http://www.myfwc.com/license/wildlife/>) for more information, including a list of those fish and wildlife species designated as species of special concern or threatened. The Florida Natural Areas Inventory (<http://www.fnai.org/>) also maintains updates lists, by county, of documented occurrences of those species.

This letter of authorization does not give absolute Federal authority to perform the work as specified on your application. The proposed work may be subject to local building restrictions mandated by the National Flood Insurance Program. You should contact your local office that issues building permits to determine if your site is located

in a flood-prone area, and if you must comply with the local building requirements mandated by the National Flood Insurance Program.

If you are unable to access the internet or require a hardcopy of any of the conditions, limitations, or expiration date for the above referenced GP, please contact Gletys Guardia-Montoya by telephone at 305-526-2515 or by email at Gletys.Guardia-Montoya@usace.army.mil.

Thank you for your cooperation with our permit program. The Corps Jacksonville District Regulatory Division is committed to improving service to our customers. We strive to perform our duty in a friendly and timely manner while working to preserve our environment. We invite you to take a few minutes to visit <http://per2.nwp.usace.army.mil/survey.html> and complete our automated Customer Service Survey. Your input is appreciated – favorable or otherwise. Again, please be aware this web address is case sensitive and should be entered as it appears above.

Sincerely,

Gletys Guardia-Montoya
Project Manager

Enclosures:

General Conditions
Self-Certification Statement of Compliance
Permit Transfer Request
Site sketches & images (20 pages) dated by the Corps July 10, 2018
FWS Standard Manatee Conditions for In-Water Work (2011)
NMFS Sea Turtle and Smalltooth Sawfish Construction Conditions (2006)
NMFS' "PDCs for In-Water Activities" dated November 20, 2017.
Noise Best Management Practices (BMPs) for Piling Installation
NOAA-FKNMS Letter of Authorization dated February 13, 2018.

Copies Furnished via e-mail:

Applicant: City of Key West
Doug Bradshaw
dbradshaw@cityofkeywest-fl.gov

Agent: Tetra Tech, Inc.
MartinezRivera, Francisco
Francisco.MartinezRivera@tetrattech.com

Frodsham, Dave
Dave.Frodsham@tetrattech.com

CESAJ-RD-PE

GENERAL CONDITIONS

33 CFR PART 320-330

PUBLISHED FEDERAL REGISTER DATED 13 NOVEMBER 1986

1. The time limit for completing the work authorized ends on **date identified in the letter**. If you find that you need more time to complete the authorized activity, submit your request for a time extension to this office for consideration at least one month before the above date is reached.
2. You must maintain the activity authorized by this permit in good condition and in conformance with the terms and conditions of this permit. You are not relieved of this requirement if you abandon the permitted activity, although you may make a good faith transfer to a third party in compliance with General Condition 4 below. Should you wish to cease to maintain the authorized activity or should you desire to abandon it without a good faith transfer, you must obtain a modification of this permit from this office, which may require restoration of the area.
3. If you discover any previously unknown historic or archeological remains while accomplishing the activity authorized by this permit, you must immediately notify this office of what you have found. We will initiate the Federal and state coordination required to determine if the remains warrant a recovery effort or if the site is eligible for listing in the National Register of Historic Places.
4. If you sell the property associated with this permit you must obtain the signature of the new owner in the space provided and forward a copy of the permit to this office to validate the transfer of this authorization.
5. If a conditioned water quality certification has been issued for your project, you must comply with the conditions specified in the certification as special conditions to this permit. For your convenience, a copy of the certification is attached if it contains such conditions.
6. You must allow a representatives from this office to inspect the authorized activity at any time deemed necessary to ensure that it is being or has been accomplished in accordance with the terms and conditions of your permit.

SELF-CERTIFICATION STATEMENT OF COMPLIANCE

Permit Number: NWS-GGM
Application Number: SAJ-2017-01874

Permittee's Name & Address (please print or type): _____

Telephone Number: _____

Location of the Work: _____

Date Work Started: _____ Date Work Completed: _____

PROPERTY IS INACCESSIBLE WITHOUT PRIOR NOTIFICATION: YES ___ NO ___
PLEASE CONTACT _____ AT _____
TO SCHEDULE AN INSPECTION

Description of the Work (e.g. bank stabilization, residential or commercial filling, docks, dredging, etc.):

Acreage or Square Feet of Impacts to Waters of the United States: _____

Describe Mitigation completed (if applicable): _____

Describe any Deviations from Permit (attach drawing(s) depicting the deviations):

I certify that all work, and mitigation (if applicable) was done in accordance with the limitations and conditions as described in the permit. Any deviations as described above are depicted on the attached drawing(s).

Signature of Permittee

Date

DEPARTMENT OF THE ARMY PERMIT TRANSFER REQUEST

PERMIT NUMBER: SAJ-2017-01874-(NW-GGM)

When the structures or work authorized by this permit are still in existence at the time the property is transferred, the terms and conditions of this permit will continue to be binding on the new owner(s) of the property. Although the construction period for works authorized by Department of the Army permits is finite, the permit itself, with its limitations, does not expire.

To validate the transfer of this permit and the associated responsibilities associated with compliance with its terms and conditions, have the transferee sign and date below and mail to the U.S. Army Corps of Engineers, Enforcement Branch, Post Office Box 4970, Jacksonville, FL 32232-0019.

(TRANSFEREE-SIGNATURE)

(SUBDIVISION)

(DATE)

(LOT)

(BLOCK)

(NAME-PRINTED)

(STREET ADDRESS)

(MAILING ADDRESS)

(CITY, STATE, ZIP CODE)



UNITED STATES DEPARTMENT OF COMMERCE
National Oceanic and Atmospheric Administration
NATIONAL MARINE FISHERIES SERVICE
Southeast Regional Office
263 13th Avenue South
St. Petersburg, FL 33701

SEA TURTLE AND SMALLTOOTH SAWFISH CONSTRUCTION CONDITIONS

The permittee shall comply with the following protected species construction conditions:

- a. The permittee shall instruct all personnel associated with the project of the potential presence of these species and the need to avoid collisions with sea turtles and smalltooth sawfish. All construction personnel are responsible for observing water-related activities for the presence of these species.
- b. The permittee shall advise all construction personnel that there are civil and criminal penalties for harming, harassing, or killing sea turtles or smalltooth sawfish, which are protected under the Endangered Species Act of 1973.
- c. Siltation barriers shall be made of material in which a sea turtle or smalltooth sawfish cannot become entangled, be properly secured, and be regularly monitored to avoid protected species entrapment. Barriers may not block sea turtle or smalltooth sawfish entry to or exit from designated critical habitat without prior agreement from the National Marine Fisheries Service's Protected Resources Division, St. Petersburg, Florida.
- d. All vessels associated with the construction project shall operate at "no wake/idle" speeds at all times while in the construction area and while in water depths where the draft of the vessel provides less than a four-foot clearance from the bottom. All vessels will preferentially follow deep-water routes (e.g., marked channels) whenever possible.
- e. If a sea turtle or smalltooth sawfish is seen within 100 yards of the active daily construction/dredging operation or vessel movement, all appropriate precautions shall be implemented to ensure its protection. These precautions shall include cessation of operation of any moving equipment closer than 50 feet of a sea turtle or smalltooth sawfish. Operation of any mechanical construction equipment shall cease immediately if a sea turtle or smalltooth sawfish is seen within a 50-ft radius of the equipment. Activities may not resume until the protected species has departed the project area of its own volition.
- f. Any collision with and/or injury to a sea turtle or smalltooth sawfish shall be reported immediately to the National Marine Fisheries Service's Protected Resources Division (727-824-5312) and the local authorized sea turtle stranding/rescue organization.
- g. Any special construction conditions, required of your specific project, outside these general conditions, if applicable, will be addressed in the primary consultation.

Revised: March 23, 2006

O:\forms\Sea Turtle and Smalltooth Sawfish Construction Conditions.doc



STANDARD MANATEE CONDITIONS FOR IN-WATER WORK

2011

The permittee shall comply with the following conditions intended to protect manatees from direct project effects:

- a. All personnel associated with the project shall be instructed about the presence of manatees and manatee speed zones, and the need to avoid collisions with and injury to manatees. The permittee shall advise all construction personnel that there are civil and criminal penalties for harming, harassing, or killing manatees which are protected under the Marine Mammal Protection Act, the Endangered Species Act, and the Florida Manatee Sanctuary Act.
- b. All vessels associated with the construction project shall operate at "Idle Speed/No Wake" at all times while in the immediate area and while in water where the draft of the vessel provides less than a four-foot clearance from the bottom. All vessels will follow routes of deep water whenever possible.
- c. Siltation or turbidity barriers shall be made of material in which manatees cannot become entangled, shall be properly secured, and shall be regularly monitored to avoid manatee entanglement or entrapment. Barriers must not impede manatee movement.
- d. All on-site project personnel are responsible for observing water-related activities for the presence of manatee(s). All in-water operations, including vessels, must be shutdown if a manatee(s) comes within 50 feet of the operation. Activities will not resume until the manatee(s) has moved beyond the 50-foot radius of the project operation, or until 30 minutes elapses if the manatee(s) has not reappeared within 50 feet of the operation. Animals must not be herded away or harassed into leaving.
- e. Any collision with or injury to a manatee shall be reported immediately to the Florida Fish and Wildlife Conservation Commission (FWC) Hotline at 1-888-404-3922. Collision and/or injury should also be reported to the U.S. Fish and Wildlife Service in Jacksonville (1-904-731-3336) for north Florida or Vero Beach (1-772-562-3909) for south Florida, and to FWC at ImperiledSpecies@myFWC.com
- f. Temporary signs concerning manatees shall be posted prior to and during all in-water project activities. All signs are to be removed by the permittee upon completion of the project. Temporary signs that have already been approved for this use by the FWC must be used. One sign which reads *Caution: Boaters* must be posted. A second sign measuring at least 8 ½" by 11" explaining the requirements for "Idle Speed/No Wake" and the shut down of in-water operations must be posted in a location prominently visible to all personnel engaged in water-related activities. These signs can be viewed at MyFWC.com/manatee. Questions concerning these signs can be sent to the email address listed above.

CAUTION: MANATEE HABITAT

All project vessels

IDLE SPEED / NO WAKE

When a manatee is within 50 feet of work
all in-water activities must

SHUT DOWN

Report any collision with or injury to a manatee:



Wildlife Alert:

1-888-404-FWCC(3922)

cell *FWC or #FWC

Noise Best Management Practices (BMPs) for Piling Installation

The following best management practices are designed to reduce the exposure to sea turtles, smalltooth sawfish, and sturgeon to potential harmful daily noise exposure levels associated with pile driving during dock and seawall construction activities.

Noise BMP Plan A (For all projects): Sea Turtle, Smalltooth Sawfish, and Sturgeon Construction Conditions

The permittee shall comply with the following protected species construction conditions:

- a. All construction personnel are responsible for observing water-related activities to detect the presence of these species.
- b. The permittee shall advise all construction personnel that there are civil and criminal penalties for harming, harassing, or killing species protected under the Endangered Species Act of 1973.
- c. Siltation barriers shall be made of material in which protected species cannot become entangled, be properly secured, and be regularly monitored to avoid protected species' entrapment. Barriers may not block protected species entry to or exit from designated critical habitat without prior agreement from the National Marine Fisheries Service's Protected Resources Division, St. Petersburg, Florida.
- d. If a protected species is seen within 100 yd of the active daily construction/dredging operation or vessel movement, all appropriate precautions shall be implemented to ensure its protection. These precautions shall include cessation of operation of any moving equipment closer than 50 ft of a protected species. Operation of any mechanical construction equipment shall cease immediately if a protected species is seen within a 50-ft radius of the equipment. Activities may not resume until the protected species has departed the project area of its own volition.
- e. Any injury to a protected species shall be reported immediately to the National Marine Fisheries Service's Protected Resources Division (727-824-5312) and the local authorized sea turtle stranding/rescue organization.
- f. All work must occur during daylight hours.

Noise BMP Plan B (for Impact Pile-Driving Installation of 6 or More Concrete Piles per Day)

The permittee shall follow all conditions defined in the Noise BMP Plan A above plus the conditions provided below:

1. It must be determined if the project occurs in open water or a confined space. This differentiation is important because if a project occurs in a confined space, an animal may not move through or past a noise source to escape it. A *confined space* is defined as any area that has a solid object (e.g., shoreline, seawall, jetty) or structure within 150 feet (ft) of the pile installation site that would effectively serve as a barrier or otherwise prevent animals from moving past it to exit the area. This does not include objects such as docks or other pile-supported structures that would not stop animal movement or significantly reflect noise.
2. If the project is located in open water, up to 10 concrete piles measuring up to 24-in diameter may be installed per day.
3. If the project is located in a confined space, up to 5 concrete piles measuring up to 24-in diameter may be installed per day.
4. If more than 5 piles will be installed per day in a confined space, noise abatement measures (below) are required for all of the concrete piles installed that day with a maximum of 10 piles installed per day.

Noise Abatement Measures: Approved noise abatement measures include noise attenuation piles (TNAP) and/or bubble curtains.

TNAP design must be constructed of a double-walled tubular casing (a casing within a larger casing), with at least a 5-in-wide hollow space completely filled with closed-cell foam or other noise dampening material between the walls. The TNAP must be long enough to be seated firmly on the sea bottom, fit over the pile being driven, and extend at least 3 ft above the surface of the water.

Bubble curtain design must adhere to the guidelines for unconfined and confined bubble curtains defined below, and be followed as detailed in the USACE permit application. The use of *any* other alternative noise control method must receive prior approval by NMFS and the USACE.

If the required noise abatement measure discussed above cannot be used, then the pile must be installed by a different method using the appropriate noise BMPs defined in this document. (e.g., concrete piles may be installed by vibratory hammer instead, following BMP Plan A).

Bubble Curtain Specifications for Pile Driving

When using an impact hammer to drive or proof concrete piles, use one of the following sound attenuation methods:

1. If water velocity is equal to or less than 1.6 ft per second (1.1 miles per hour) for the entire installation period, surround the pile being driven by a confined or

unconfined bubble curtain that will distribute small air bubbles around 100% of the pile perimeter for the full depth of the water column.

- a. General - An unconfined bubble curtain is composed of an air compressor(s), supply lines to deliver the air, distribution manifolds or headers, perforated aeration pipe, and a frame. The frame facilitates transport and placement of the system, keeps the aeration pipes stable, and provides ballast to counteract the buoyancy of the aeration pipes in operation.
- b. The aeration pipe system shall consist of multiple layers of perforated pipe rings, stacked vertically in accordance with the following:

Water Depth (m)	No. of Layers
0 to less than 5	2
5 to less than 10	4
10 to less than 15	7
15 to less than 20	10
20 to less than 25	13

- c. The pipes in all layers shall be arranged in a geometric pattern which shall allow for the pile being driven to be completely enclosed by bubbles for the full depth of the water column and with a radial dimension such that the rings are no more than 0.5 m from the outside surface of the pile.
 - i. The lowest layer of perforated aeration pipe shall be designed to ensure contact with the substrate without burial and shall accommodate sloped conditions.
 - ii. Air holes shall be 1.6 millimeter (mm) (1/16-in) in diameter and shall be spaced approximately 20 mm (3/4 in) apart. Air holes with this size and spacing shall be placed in 4 adjacent rows along the pipe to provide uniform bubble flux.
 - iii. The system shall provide a bubble flux 3.0 m³ per minute per linear meter of pipe in each layer (32.91 ft³ per minute per lin ft of pipe in each layer). The total volume of air per layer is the product of the bubble flux and the circumference of the ring:

$$V_t = 3.0 \text{ m}^3/\text{min}/\text{m} * \text{Circumference of the aeration ring in m}$$
 or

$$V_t = 32.91 \text{ ft}^3/\text{min}/\text{ft} * \text{Circumference of the aeration ring in ft}$$
 - iv. Meters shall be provided as follows:

- Pressure meters shall be installed at all inlets to aeration pipelines and at points of lowest pressure in each branch of the aeration pipeline.

- Flow meters shall be installed in the main line at each compressor and at each branch of the aeration pipelines at each inlet. In applications where the feed line from the compressor is continuous from the compressor to the aeration pipe inlet, the flow meter at the compressor can be eliminated.

Flow meters shall be installed according to the manufacturer's recommendation based on either laminar flow or non-laminar flow.

2. If water velocity is greater than 1.6 ft per second (1.1 miles per hour) at any point during installation or if constructing a seawall, surround the pile or area being driven by a confined bubble curtain (e.g., a bubble ring surrounded by a fabric or non-metallic sleeve). The confined bubble curtain will distribute air bubbles around 100% of the pile perimeter for the full depth of the water column, according to specifications below.
 - a. General - A confined bubble curtain is composed of an air compressor(s), supply lines to deliver the air, distribution manifolds or headers, perforated aeration pipe(s), and a means of confining the bubbles.
 - b. The confinement shall extend from the substrate to a sufficient elevation above the maximum water level expected during pile installation such that when the air delivery system is adjusted properly, the bubble curtain does not act as a water pump (i.e., little or no water should be pumped out of the top of the confinement system).
 - c. The confinement shall contain resilient pile guides that prevent the pile and the confinement from coming into contact with each other and do not transmit vibrations to the confinement sleeve and into the water column (e.g., rubber spacers, air-filled cushions).
 - d. In-water less than 15 m deep, the system shall have a single aeration ring at the substrate level. In-waters greater than 15 m deep, the system shall have at least 2 rings: 1 at the substrate level and the other at mid-depth.
 - e. The lowest layer of perforated aeration pipe shall be designed to ensure contact with the substrate without sinking into the substrate and shall accommodate for sloped conditions.

- f. Air holes shall be 1.6 mm (1/16-in) in diameter and shall be spaced approximately 20 mm (3/4 in) apart. Air holes with this size and spacing shall be placed in 4 adjacent rows along the pipe to provide uniform bubble flux.
- g. The system shall provide a bubble flux of 2.0 m³ per minute per linear meter of pipe in each layer (21.53 ft³ per minute per lin ft of pipe in each layer). The total volume of air per layer is the product of the bubble flux and the circumference of the ring:

$$V_t = 2.0 \text{ m}^3/\text{min}/\text{m} * \text{Circumference of the aeration ring in m}$$

or

$$V_t = 21.53 \text{ ft}^3/\text{min}/\text{ft} * \text{Circumference of the aeration ring in ft}$$

- h. Flow meters shall be provided as follows:
Pressure meters shall be installed at all inlets to aeration pipelines and at points of lowest pressure in each branch of the aeration pipeline.
 - ii. Flow meters shall be installed in the main line at each compressor and at each branch of the aeration pipelines at each inlet. In applications where the feed line from the compressor is continuous from the compressor to the aeration pipe inlet, the flow meter at the compressor can be eliminated.
 - iii. Flow meters shall be installed according to the manufacturer's recommendation based on either laminar flow or non-laminar flow.

U.S. Army Corps of Engineers Jacksonville District's Programmatic Biological Opinion (JaxBO) Project Design Criteria (PDCs) for In-Water Activities

November 20, 2017

- 1) **(AP.7.) Education and Observation:** The permittee must ensure that all personnel associated with the project are instructed about the potential presence of species protected under the ESA and the Marine Mammal Protection Act (MMPA). All on-site project personnel are responsible for observing water-related activities for the presence of protected species. All personnel shall be advised that there are civil and criminal penalties for harming, harassing, or killing ESA-listed species or marine mammals. To determine which species may be found in the project area, please review the relevant Protected Species List at:
http://sero.nmfs.noaa.gov/protected_resources/section_7/threatened_endangered/index.html
- 2) **(AP.8.) Reporting** of interactions with protected species:
 - a) Any collision(s) with and/or injury to any sea turtle, sawfish, whale, or sturgeon occurring during the construction of a project, shall be reported immediately to NMFS's Protected Resources Division (PRD) at (1-727-824-5312) or by email to takereport.nmfs@noaa.gov and SAJ-RD-Enforcement@usace.army.mil.
 - b) Smalltooth sawfish: Report sightings to 1-844-SAWFISH or email Sawfish@MyFWC.com
 - c) Sturgeon: Report dead sturgeon to 1-844-STURG 911 (1-844-788-7491) or email nmfs.ser.sturgeonnetwork@noaa.gov
 - d) Sea turtles and marine mammals: Report stranded, injured, or dead animals to 1-877-WHALE HELP (1-877-942-5343).
 - e) North Atlantic right whale: Report injured, dead, or entangled right whales to the USCG via VHF Channel 16.
- 3) **(AP.9.) Vessel Traffic and Construction Equipment:** All vessel operators must watch for and avoid collision with species protected under the ESA and MMPA. Vessel operators must avoid potential interactions with protected species and operate in accordance with the following protective measures:
 - a) *Construction Equipment:*
 - i) All vessels associated with the construction project shall operate at "Idle Speed/No Wake" at all times while operating in water depths where the draft of the vessel provides less than a 4-foot (ft) clearance from the bottom, and in all depths after a protected species has been observed in and has departed the area.
 - ii) All vessels will follow marked channels and/or routes using the maximum water depth whenever possible.
 - iii) Operation of any mechanical construction equipment, including vessels, shall cease immediately if a listed species is observed within a 50-ft radius of

construction equipment and shall not resume until the species has departed the area of its own volition.

- iv) If the detection of species is not possible during certain weather conditions (e.g., fog, rain, wind), then in-water operations will cease until weather conditions improve and detection is again feasible.

b) *All Vessels:*

- i) Sea turtles: Maintain a minimum distance of 150 ft.
- ii) North Atlantic right whale: Maintain a minimum 1,500-ft distance (500 yards).
- iii) Vessels 65 ft in length or longer must comply with the Right Whale Ship Strike Reduction Rule (50 CFR 224.105) which includes reducing speeds to 10 knots or less in Seasonal Management Areas (<http://www.fisheries.noaa.gov/pr/shipstrike/>).
- iv) Mariners shall check various communication media for general information regarding avoiding ship strikes and specific information regarding right whale sightings in the area. These include NOAA weather radio, USCG NAVTEX broadcasts, and Notices to Mariners.
- v) Marine mammals (i.e., dolphins, whales [other than North Atlantic right whales], and porpoises): Maintain a minimum distance of 300 ft.
- vi) When these animals are sighted while the vessel is underway (e.g., bow-riding), attempt to remain parallel to the animal's course. Avoid excessive speed or abrupt changes in direction until they have left the area.
- vii) Reduce speed to 10 knots or less when mother/calf pairs or groups of marine mammals are observed, when safety permits.

- 4) **(AP.10.) Turbidity Control Measures during Construction:** Turbidity must be monitored and controlled. Prior to initiating any of the work covered under this Opinion, the Permittee shall install turbidity curtains as described below. In some instances, the use of turbidity curtains may be waived by the USACE project manager if the project is deemed too minimal to generate turbidity (e.g., certain ATON installation, scientific survey device placement, marine debris removal) or if the current is too strong for the curtains to stay in place. Turbidity curtains specifications:

- a) Install floating turbidity barriers with weighted skirts that extend to within 1 ft of the bottom around all work areas that are in, or adjacent to, surface waters.
- b) Use these turbidity barriers throughout construction to control erosion and siltation and ensure that turbidity levels within the project area do not exceed background conditions.
- c) Position turbidity barriers in a way that does not block species' entry to or exit from designated critical habitat.
- d) Monitor and maintain turbidity barriers in place until the authorized work has been completed and the water quality in the project area has returned to background conditions.
- e) In the range of ESA-listed corals (St. Lucie Inlet, Martin County south to the Dry Tortugas and the U.S. Caribbean) and Johnson's seagrass (Turkey Creek/Palm

Bay south to central Biscayne Bay in the lagoon systems on the east coast of Florida):

- i) Projects that include upland earth moving (e.g., grading to install a building or parking lot associated with a dock and seawall project), must install sediment control barriers to prevent any upland sediments from reaching estuarine or marine waters.
 - ii) The turbidity curtain requirement cannot be waived for any project that moves or removes sediment (e.g., dredging, auger to create a pile, trenching to install a cableline). If turbidity curtains are not feasible in an area based on site conditions such as water current, high wave action, or stormy conditions, the project must undergo individual Section 7 consultation and is not covered under this Programmatic Opinion.
- 5) **(AP.11.) Entanglement:** All turbidity curtains and other in-water equipment must be properly secured with materials that reduce the risk of entanglement of marine species (described below). Turbidity curtains likewise must be made of materials that reduce the risk of entanglement of marine species.
- a) In-water lines (rope, chain, and cable, including the lines to secure turbidity curtains) must be stiff, taut, and non-looping. Examples of such lines are heavy metal chains or heavy cables that do not readily loop and tangle. Flexible in-water lines, such as nylon rope or any lines that could loop or tangle, must be enclosed in a plastic or rubber sleeve/tube to add rigidity and prevent the line from looping and tangling. In all instances, no excess line is allowed in the water.
 - b) Turbidity curtains and other in-water equipment must be placed in a manner that does not entrap species within the construction area or block access for them to navigate around the construction area.



UNITED STATES DEPARTMENT OF COMMERCE
National Oceanic and Atmospheric Administration
NATIONAL OCEAN SERVICE

Florida Keys National Marine Sanctuary

33 East Quay Road
Key West, FL 33040

February 13, 2018

Ms. Gletys Guardia-Montoya
Department of the Army Jacksonville District Corps of Engineers
Miami Regulatory Office
9900 Southwest 107th Avenue, Suite 203
Miami, FL 33176

Dear Ms. Guardia-Montoya:

NOAA Florida Keys National Marine Sanctuary (FKNMS or sanctuary) has reviewed a Department of the Army Corps of Engineers (DA Corps) application no. 2017-01874 (NW-GGM). The applicant, City of Key West, c/o Doug Bradshaw, is requesting a permit to replace approximately 79 pilings at the Key West Bight Marina, located at 120 Margaret Street, Key West, Monroe County, FL. The proposed activity is prohibited by FKNMS regulations at 15 CFR § 922.163(a)(3).

NOAA has reviewed the project described in the DA Corps application and has determined that the proposed project will have a negligible impact on sanctuary resources. Therefore, pursuant to 15 CFR § 922.49, NOAA does not object to the issuance of a DA Corps permit for the project as proposed, and a separate FKNMS permit will not be required.


This determination is only applicable to DA Corps application no. 2017-01874 (NW-GGM). If any changes are made to the project description in this application, DA Corps shall notify NOAA and this letter of authorization will be rescinded. Upon such notification, NOAA shall re-review the project and provide a supplementary determination. Further information on Sanctuary permit review and authorization is set forth at 15 CFR § 922.49.

This project has been assigned authorization #FKNMS-2017-138. Please contact FKNMS Permit Coordinator Joanne Delaney at Joanne.Delaney@noaa.gov if you have questions about the sanctuary's determination on this project. Thank you for your continued cooperation with the Florida Keys National Marine Sanctuary.

Sincerely,

Sarah Fangman
Superintendent

cc: Francisco Martinez, Tetra Tech, Inc.







CITY OF KEY WEST

KEY WEST BIGHT MARINA MAINTENANCE (PILING REPLACEMENT DOCK REPAIR)

PILE REPLACEMENT PERMITTING

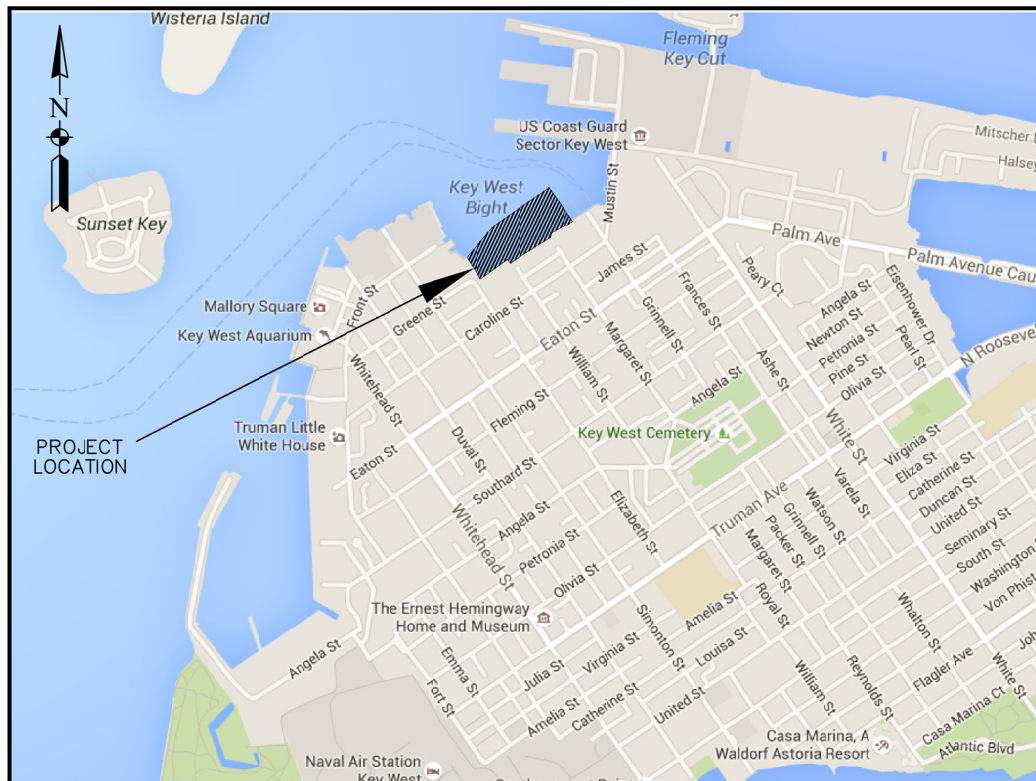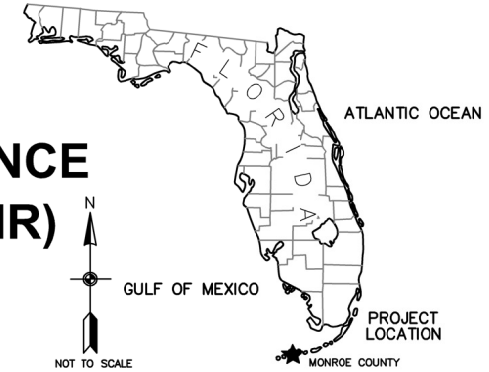

VICINITY MAP

KEY WEST BIGHT MARINA, KEY WEST, FLORIDA

INDEX OF SHEETS

SHEET #	TITLE	LATEST UPDATE	REV.
G-001	COVER SHEET AND VICINITY MAP	10/18/2017	0
G-002	KEY WEST BIGHT LOCATION AND ACCESS	10/18/2017	0
G-003	VICINITY MAP AND DIRECTIONS TO SITE	10/18/2017	0
G-004	USDA/NRCS SOIL MAP	10/18/2017	0
C-101	KEY WEST BIGHT MARINA PLAN VIEW	10/18/2017	0
C-102	DOCK A PLAN VIEW	10/18/2017	0
C-103	DOCK A PLAN VIEW	10/18/2017	0
C-104	DOCK C AND FUEL DOCK PLAN VIEW	10/18/2017	0
C-105	DOCK D PLAN VIEW	10/18/2017	0
C-106	DOCK D PLAN VIEW	10/18/2017	0
C-107	DOCK E PLAN VIEW	10/18/2017	0
C-108	DOCK F PLAN VIEW	10/18/2017	0
C-109	DOCK G PLAN VIEW	10/18/2017	0
C-110	DOCK H PLAN VIEW	10/18/2017	0
C-111	HARBOR WALK PLAN VIEW	10/18/2017	0
C-112	HARBOR WALK PLAN VIEW	10/18/2017	0
C-113	HARBOR WALK PLAN VIEW	10/18/2017	0
C-114	CROSS-SECTION DETAIL	10/18/2017	0
C-115	CROSS-SECTION DETAIL	10/18/2017	0
C-116	CROSS-SECTION DETAIL	10/18/2017	0



Description	Date	Appr.

Designed By: P. W. MARKREZ
 Checked By: S. MCSAHEE
 Date: 7/17/17
 Drawn File: P. W. MARKREZ
 Scale: AS SHOWN

TETRA TECH INC.
 701 W. FEDERAL HWY
 SUITE 314
 STUART, FL 34994-2936
 TEL: (772) 781-3400
 FAX: (772) 781-3411
 PROJECT FILE NO.: 17-2420
 PERMIT AUTHORITY OF AUTHORIZATION NO. 2420



CITY OF KEY WEST
 KEY WEST BIGHT MARINA MAINTENANCE
 (PILING REPLACEMENT DOCK REPAIR)
 COVER SHEET AND VICINITY MAP
 KEY WEST, MONROE COUNTY, FLORIDA



Mark	Description	Date	Appr.

Designed by:
 Drawn By: F. MARTINEZ
 Checked By: S. MCCABEE
 Date: 10/18/17
 Design file no: www.keywest.com/james
 Scale: AS SHOWN

TETRA TECH INC
 756 SOUTH FEDERAL HWY
 SUITE 314
 STUART, FL 34984-2936
 TEL: (772) 781-3411
 FAX: (772) 781-3411
 CERTIFICATE OF AUTHORIZATION
 NO. 2429



CITY OF KEY WEST
 KEY WEST BIGHT MARINA MAINTENANCE
 (PILING REPLACEMENT DOCK REPAIR)
 KEY WEST BIGHT LOCATION AND ACCESS
 KEY WEST, MONROE COUNTY, FLORIDA

FOR PERMITTING
 NOT FOR CONSTRUCTION

Sheet Reference:
 G-002
 Sheet 2 of 20



Parcel ID - 00072082-004700
 Alt Id - 9073978
 Address - 120 MARGARET ST 101
 Owner - CITY OF KEY WEST
[View Report](#) | [Google Maps](#)

Parcel ID - 00072082-003800
 Alt Id - 8817550
 Address - 613-631 GREENE ST
 Owner - CITY OF KEY WEST
[View Report](#) | [Google Maps](#)

Parcel ID - 00072082-004500
 Alt Id - 8818653
 Address - END OF MARGARET ST
 Owner - CITY OF KEY WEST
[View Report](#) | [Google Maps](#)

Parcel ID - 00072082-004506
 Alt Id - 9073912
 Address - MARGARET ST
 Owner - CITY OF KEY WEST
[View Report](#) | [Google Maps](#)

Parcel ID - 00072082-004400
 Alt Id - 8818645
 Address - MARGARET ST
 Owner - CITY OF KEY WEST
[View Report](#) | [Google Maps](#)

Parcel ID - 00006680-000000
 Alt Id - 1000698
 Address - 800 BLK CAROLINE ST
 Owner - CITY OF KEY WEST
[View Report](#) | [Google Maps](#)

Parcel ID - 00072082-004200
 Alt Id - 8818602
 Address - 201 WILLIAM ST
 Owner - CITY OF KEY WEST
[View Report](#) | [Google Maps](#)

Parcel ID - 00072082-003900
 Alt Id - 8817584
 Address - 202 WILLIAM ST
 Owner - CITY OF KEY WEST
[View Report](#) | [Google Maps](#)

Parcel ID - 00072082-003908
 Alt Id - 9073824
 Address - LAZY WAY LN
 Owner - CITY OF KEY WEST
[View Report](#) | [Google Maps](#)

Parcel ID - 00072082-003803
 Alt Id - 9073725
 Address - VACANT LAND
 Owner - CITY OF KEY WEST
[View Report](#) | [Google Maps](#)




from 1829 N Roosevelt Blvd, Key West, FL 33040
 to Key West Bight Marina, 201 William St, Key West, F...

5 min (1.3 miles)
 via Palm Avenue Causeway and Eaton St
 Fastest route, the usual traffic

1829 N Roosevelt Blvd
 Key West, FL 33040

- ↑ Head northwest on 1st St
10 ft
- ↑ Continue onto Palm Avenue Causeway
0.4 mi
- ↑ Continue onto Palm Ave
0.3 mi
- ↑ Continue onto Eaton St
0.4 mi
- ➡ Turn right onto William St
0.2 mi

Key West Bight Marina
 201 William St, Key West, FL 33040

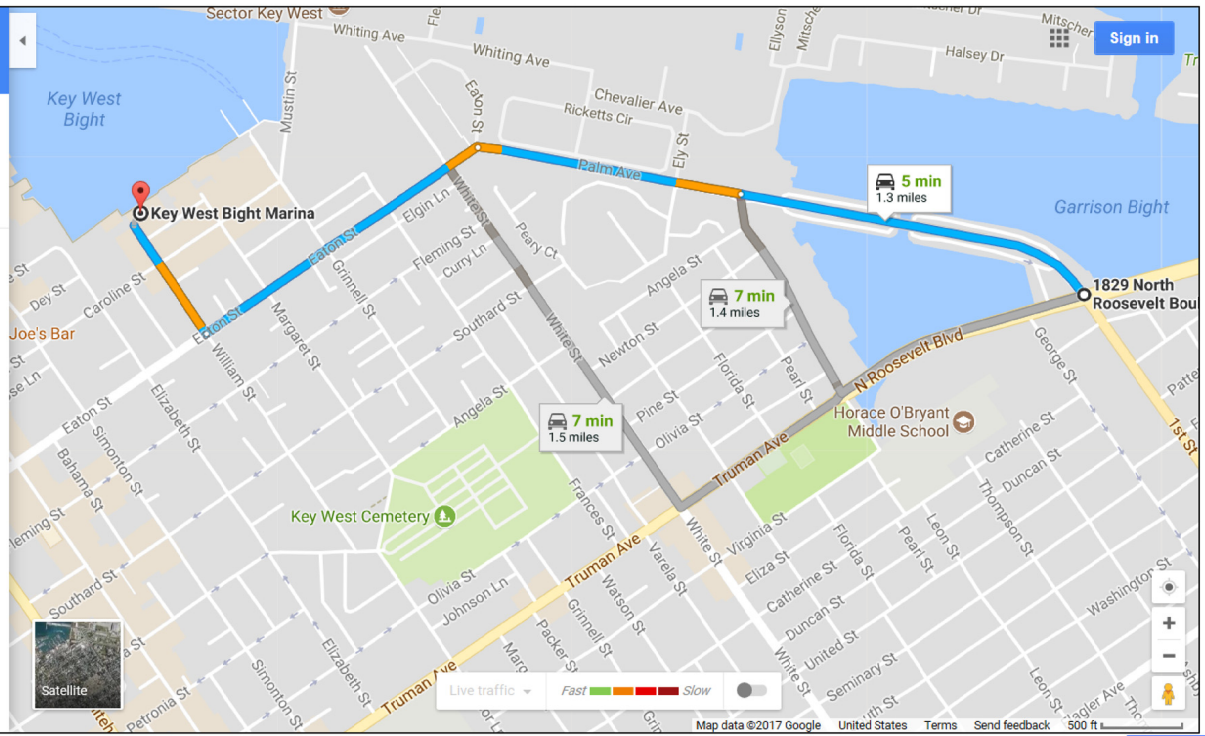

Designed by:
 P. W. MARTINEZ
 Checked by:
 S. MCGAHEE
 Date:
 06/29/17
 Description:
 VICINITY MAP OF AUTHORIZATION
 NO. 21628

TETRA TECH INC.
 3915 W. FEDERAL HWY
 SUITE 300
 STUART, FL 34994-2936
 TEL: (772) 781-3400
 FAX: (772) 781-3411
 PERMITS@TETRA-TECH.COM

CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)
 VICINITY MAP AND DIRECTIONS TO SITE
KEY WEST, MONROE COUNTY, FLORIDA

**FOR PERMITTING
 NOT FOR CONSTRUCTION**

Sheet Reference:
G-003
 Sheet 3 of 20

P:\CITY OF KEY WEST\TASK 11. KW BIGHT PILING ASSESSMENT\PERMITTING\CADD\WMB_PILE PERMIT_COVER_V1.DWG



Custom Soil Resource Report
Soil Map



Monroe County, Keys Area, Florida (FL687)			
Map Unit Symbol	Map Unit Name	Acres in AOI	Percent of AOI
5	Islamorada muck, tidal	9.5	0.2%
7	Udorthents-Urban land complex	272.0	6.3%
11	Urban land	1,529.2	35.2%
13	Keyvaca very gravelly loam, extremely stony	21.5	0.5%
18	Beaches	10.5	0.2%
99	Water	18.2	0.4%
100	Waters of the Atlantic Ocean	2,181.5	50.2%
Subtotals for Soil Survey Area		4,042.3	93.8%
Totals for Area of Interest		4,345.4	100.0%

PROJECT LOCATION -
RELEVANT SOIL
CLASSIFICATIONS:
#11 & #100

11—Urban land

Map Unit Setting
National map unit symbol: vryh
Elevation: 0 to 10 feet
Mean annual precipitation: 30 to 51 inches
Mean annual air temperature: 72 to 82 degrees F
Frost-free period: 358 to 365 days
Farmland classification: Not prime farmland

Map Unit Composition
Urban land: 95 percent
Minor components: 5 percent
Estimates are based on observations, descriptions, and transects of the mapunit.

Description of Urban Land
Setting
Landform: Islands
Landform position (three-dimensional): Interfluvial
Down-slope shape: Linear
Across-slope shape: Linear
Parent material: No parent material

Properties and qualities
Slope: 0 to 1 percent
Frequency of flooding: Rare

Interpretive groups
Land capability classification (irrigated): None specified
Other vegetative classification: Forage suitability group not assigned (G15AC999FL)

Minor Components
Udorthents
Percent of map unit: 3 percent
Landform: Islands
Landform position (three-dimensional): Interfluvial
Down-slope shape: Convex
Across-slope shape: Linear
Other vegetative classification: Forage suitability group not assigned (G15AC999FL)

Beaches, tidal
Percent of map unit: 2 percent
Landform: Beaches on islands
Landform position (three-dimensional): Rise
Down-slope shape: Convex
Across-slope shape: Linear
Other vegetative classification: Forage suitability group not assigned (G15AC999FL)

100—Waters of the Atlantic Ocean

Map Unit Composition
Waters of the Atlantic ocean: 100 percent
Estimates are based on observations, descriptions, and transects of the mapunit.

Description of Waters Of The Atlantic Ocean
Interpretive groups
Land capability classification (irrigated): None specified
Other vegetative classification: Forage suitability group not assigned (G15AC999FL)

Designated by:	Drawn by:	Checked by:	Design file no.:	Scale:	Appr.:
	F. MARTINEZ	S. MCGARRETT	10/18/17	AS SHOWN	

TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 314
STUART, FL 34984-2936
TEL: (772) 781-3411
FAX: (772) 781-3411
CERTIFICATE OF AUTHORIZATION
NO. 2428



CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)
USDA/NRCS SOIL MAP
KEY WEST, MONROE COUNTY, FLORIDA

FOR PERMITTING
NOT FOR CONSTRUCTION



Sheet Reference:
G-004
Sheet 4 of 20

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ON SHEETS C-102 TO C-113 ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE.

PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME, WITHIN THE REQUESTED TIMELINE.

NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

AREA OF DOCKS FOR THE KEY WEST BIGHT MARINA IS APPROXIMATELY: 24,710 SF

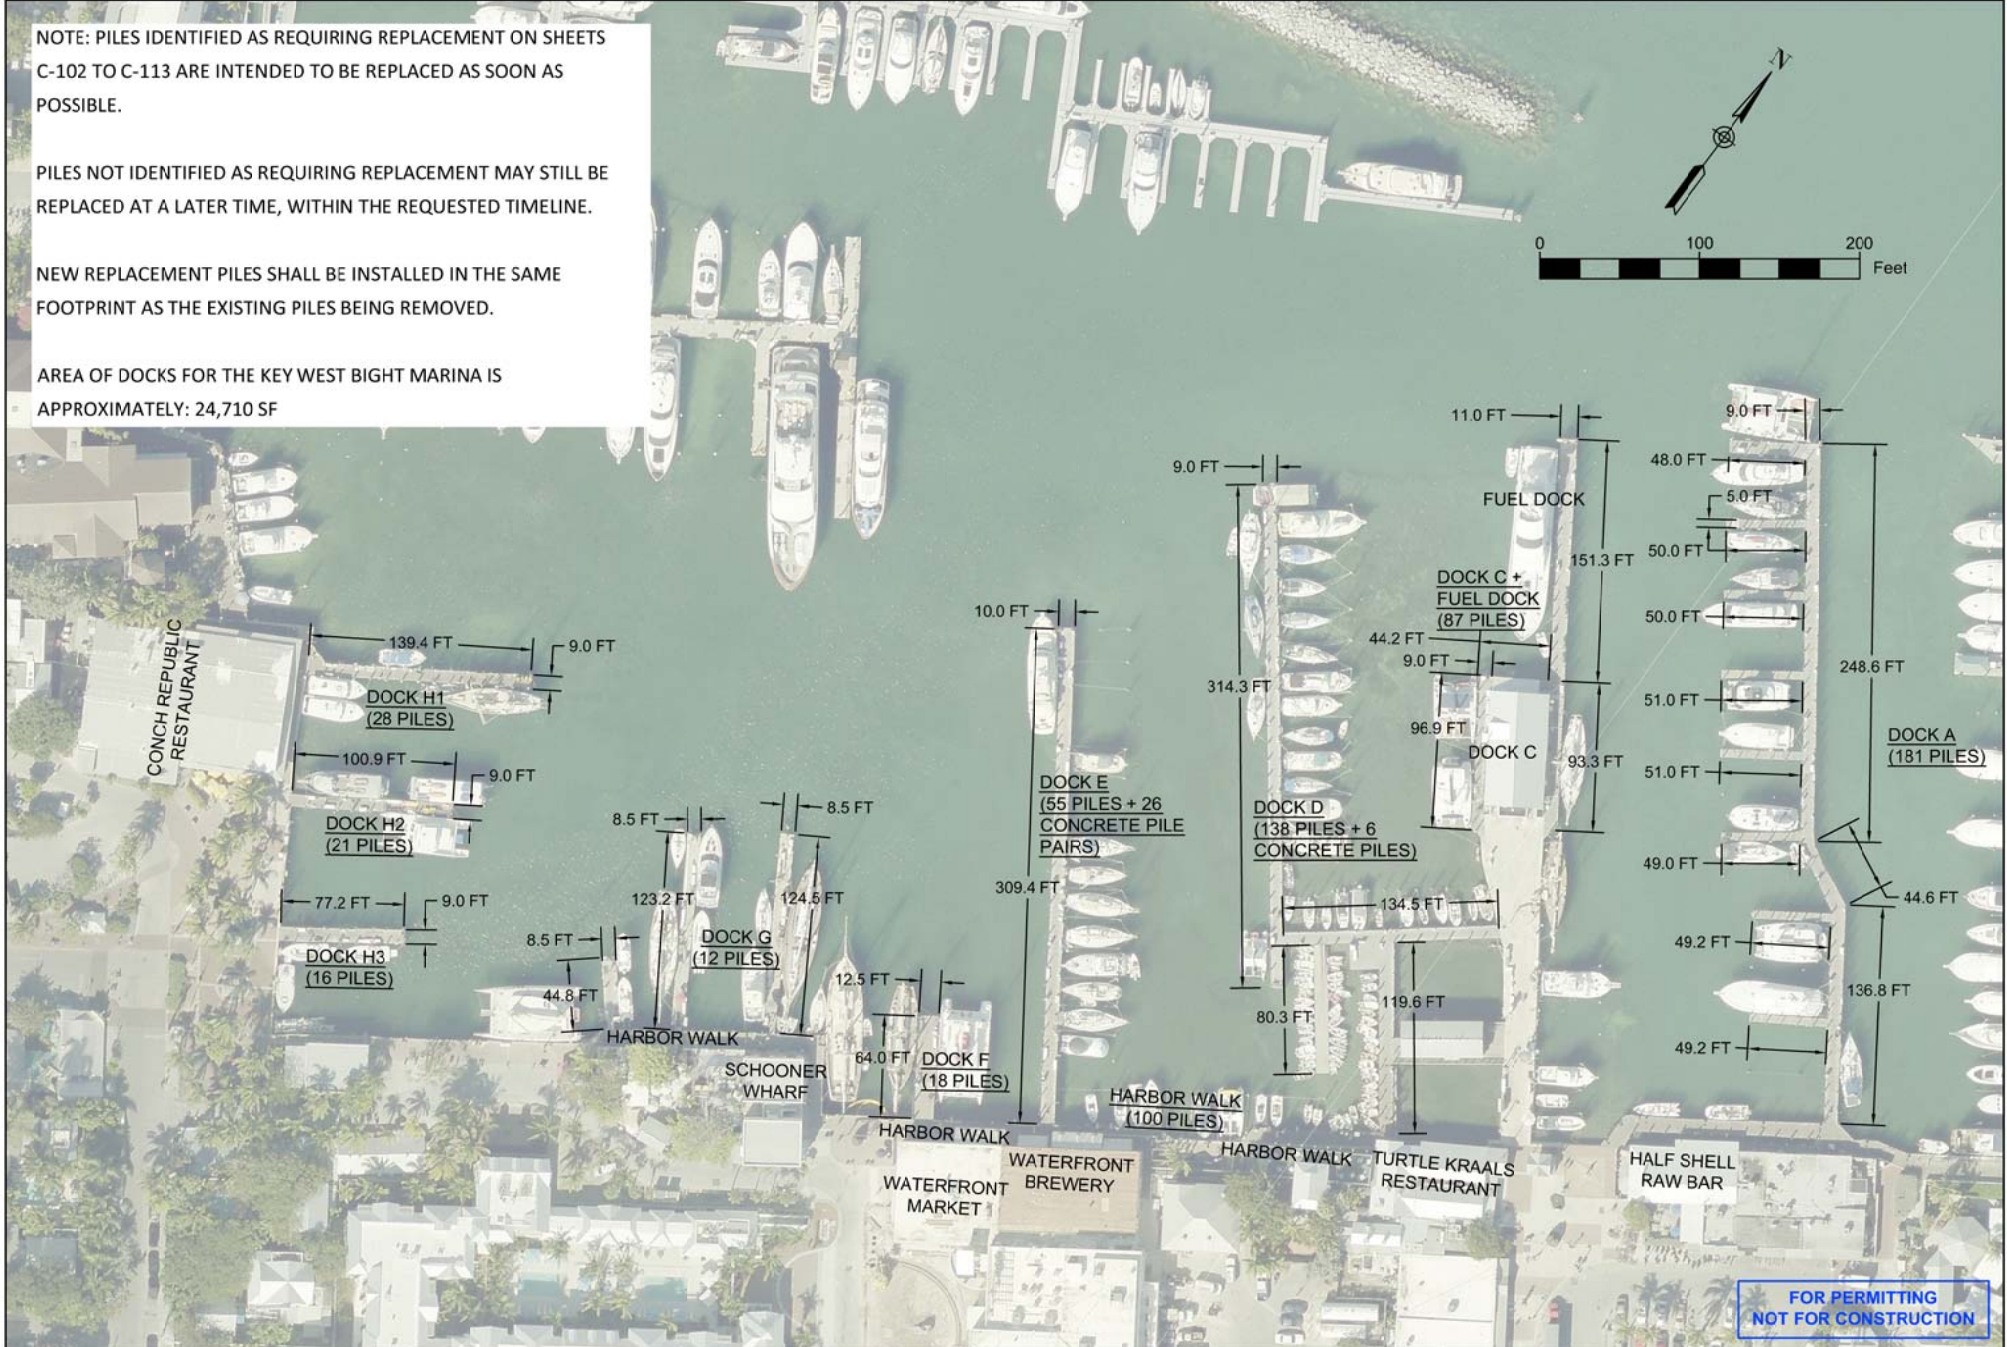

FOR PERMITTING
NOT FOR CONSTRUCTION




CITY OF KEY WEST
**KEY WEST BIGHT MARINA MAINTENANCE
 (PILING REPLACEMENT DOCK REPAIR)**
 KEY WEST BIGHT MARINA PLAN VIEW
 KEY WEST, MONROE COUNTY, FLORIDA

TT TETRA TECH INC.
 759 SOUTH FEDERAL HWY
 SUITE 314
 STUART, FL 34994-2936
 TEL: (772) 781-3400
 FAX: (772) 781-3411
 CERTIFICATE OF AUTHORIZATION
 No. 12-29

USACE SAJ-2017-01874-(NW-GGM)
Page 5 of 20. July 10th, 2018.

Designed by:
 Drawn By:
 F. MARTINEZ
 Checked By:
 S. MCGAHEE
 Date:
 10/20/17
 Design file no:
 KWB_PILE_PERMIT_SITE_V1.DWG
 Scale:
 AS SHOWN

Sheet Reference:
C-101
 Sheet 5 of 20

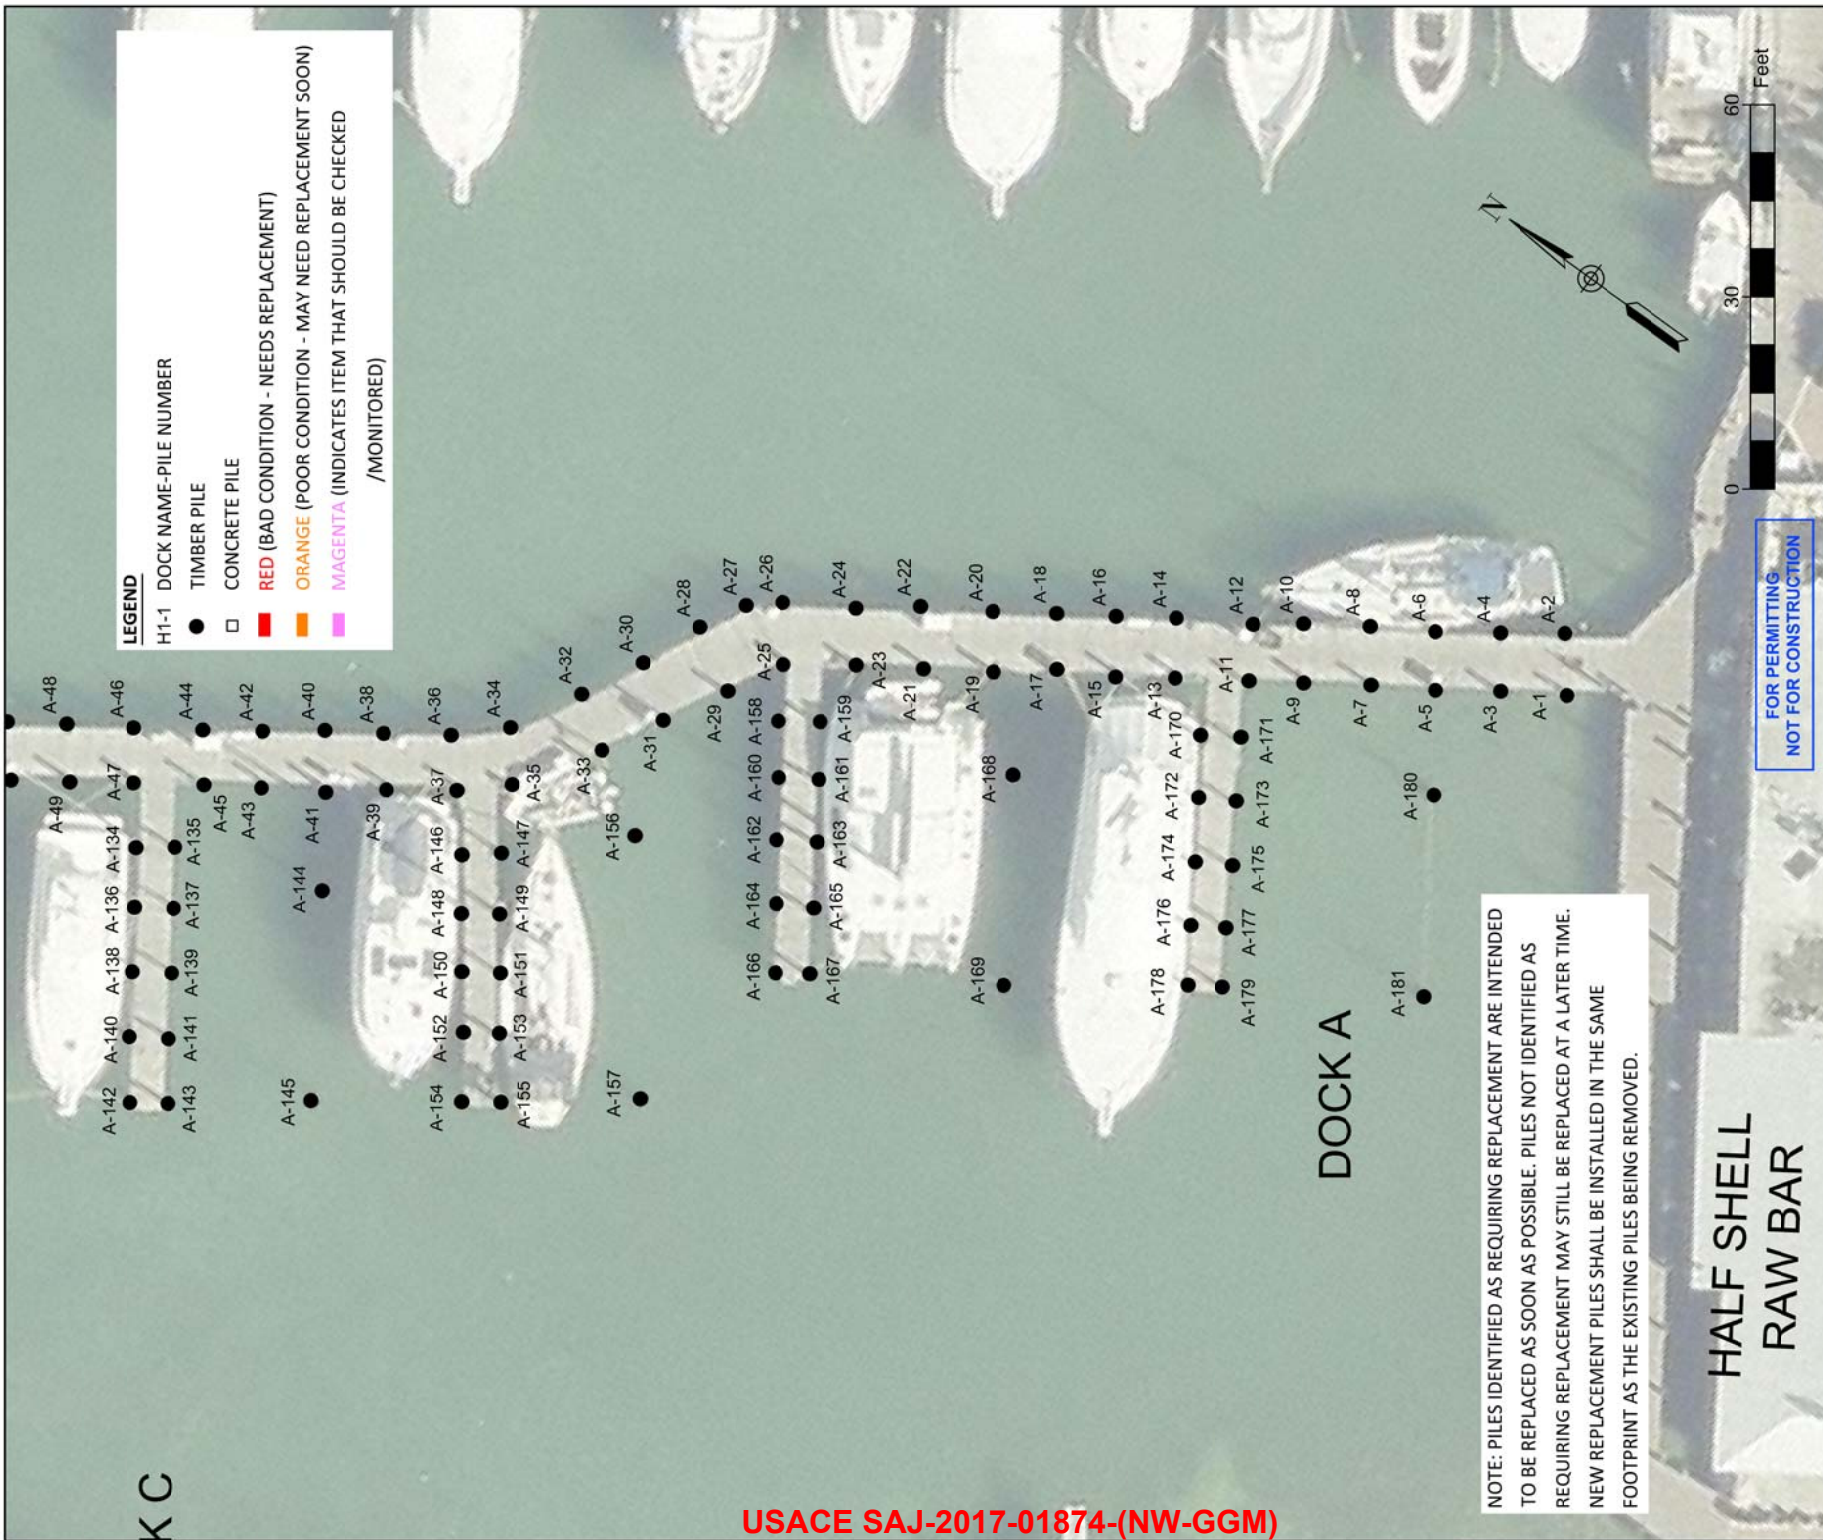

LEGEND

H1-1 DOCK NAME-PILE NUMBER

● TIMBER PILE

□ CONCRETE PILE


■ RED (BAD CONDITION - NEEDS REPLACEMENT)

■ ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)

■ MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED /MONITORED)

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

**HALF SHELL
RAW BAR**



CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)

DOCK A PLAN VIEW

KEY WEST, MONROE COUNTY, FLORIDA



TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 300
MIAMI, FL 33130
TEL: (772) 781-3400
FAX: (772) 781-3411

CERTIFICATE OF AUTHORIZATION
NO. 2429

**FOR PERMITTING
NOT FOR CONSTRUCTION**

Designed by:
Drawn By: F. MARTINEZ
Checked By: S. MCGAHEE
Date: 10/20/17
Design file no: NW_PILE_PERMITS_V1.DWG
Scale: AS SHOWN

Sheet Reference:
C-102
Sheet 6 of 20


LEGEND

H1-1 DOCK NAME-PILE NUMBER

- TIMBER PILE
- CONCRETE PILE

- RED (BAD CONDITION - NEEDS REPLACEMENT)
- ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
- MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)


NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

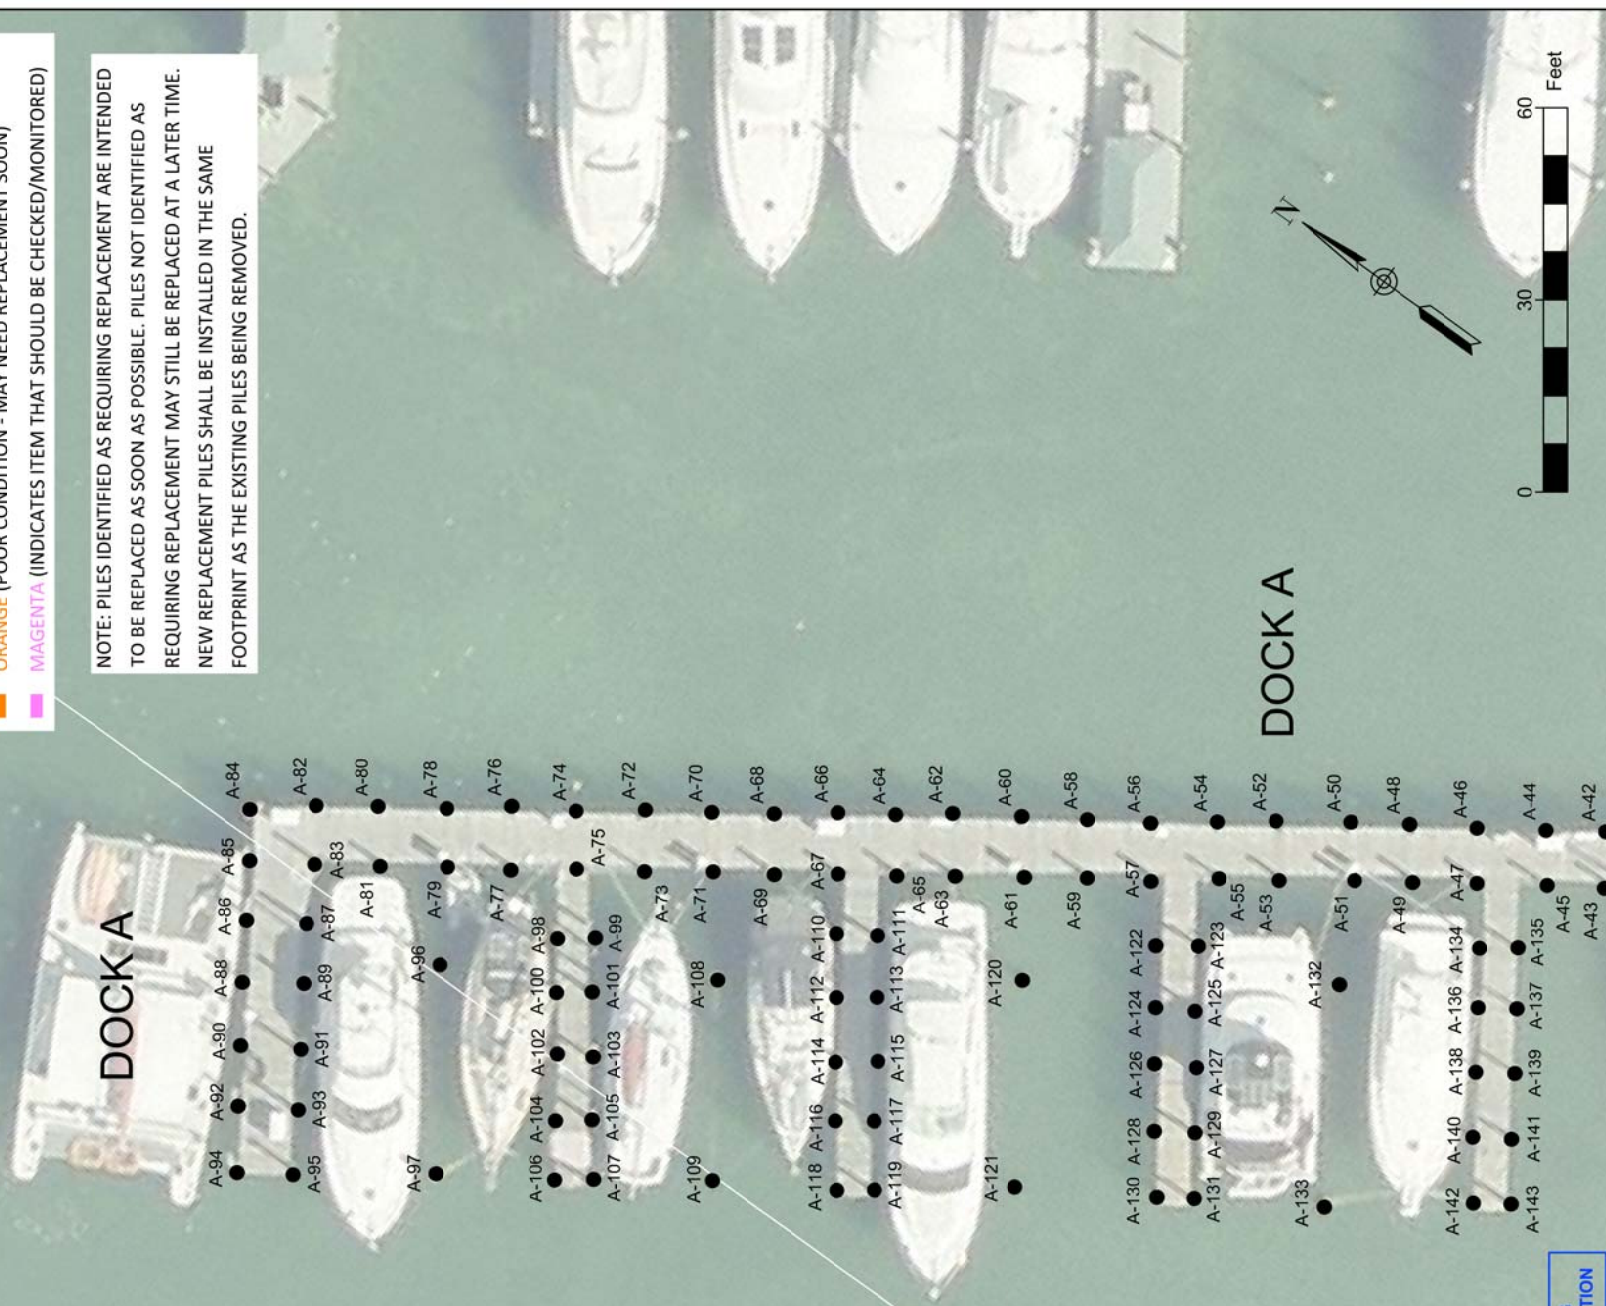

DOCK A



FOR PERMITTING
NOT FOR CONSTRUCTION



CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)
DOCK A PLAN VIEW
KEY WEST, MONROE COUNTY, FLORIDA



TETRA TECH INC.
759 SOUTH FEDERAL HWY
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411
CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:
Drawn By: F. MARTINEZ
Checked By: S. MCGAHEE
Date: 10/20/17
Design File No: NW_PILE_REPLACE_SHE_V1.DWG
Scale: AS SHOWN

Sheet Reference:
C-103
Sheet 7 of 20



LEGEND

H1-1 DOCK NAME-PILE NUMBER

- TIMBER PILE
- CONCRETE PILE
- RED (BAD CONDITION - NEEDS REPLACEMENT SOON)
- ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
- MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

USACE SAJ-2017-01874-(NW-GGM)

Page 8 of 20. July 10th, 2018.

FOR PERMITTING
NOT FOR CONSTRUCTION



CITY OF KEY WEST
**KEY WEST BIGHT MARINA MAINTENANCE
 (PILING REPLACEMENT DOCK REPAIR)**
 DOCK C AND FUEL DOCK PLAN VIEW
 KEY WEST, MONROE COUNTY, FLORIDA



TETRA TECH INC.
 759 SOUTH FEDERAL HWY
 STUART, FL 34994-2936
 TEL: (772) 781-3400
 FAX: (772) 781-3411
 CERTIFICATE OF AUTHORIZATION
 NO. 2429

Designed by:
 Drawn By: F. MARTINEZ
 Checked By: S. MCCAGHEE
 Date: 10/20/17
 Design file no: NW_PILE_PERMITS_VI.LING
 Scale: AS SHOWN

Sheet Reference:
C-104
 Sheet 8 of 20



LEGEND

H1-1 DOCK NAME-PILE NUMBER

● TIMBER PILE

□ CONCRETE PILE

● RED (BAD CONDITION - NEEDS REPLACEMENT)

● ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)

● MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

DOCK C

DOCK D

FOR PERMITTING
NOT FOR CONSTRUCTION



CITY OF KEY WEST
**KEY WEST BIGHT MARINA MAINTENANCE
 (PILING REPLACEMENT DOCK REPAIR)**
 DOCK D PLAN VIEW
 KEY WEST, MONROE COUNTY, FLORIDA



TETRA TECH INC.
 759 SOUTH FEDERAL HWY
 SUITE 300
 MIAMI, FL 33130
 TEL: (772) 781-3400
 FAX: (772) 781-3411

CERTIFICATE OF AUTHORIZATION
 NO. 2429

Designed by:
 Drawn By: F. MARTINEZ
 Checked By: S. MCCAGHEE
 Date: 10/20/17
 Design file no: NW_PILE_PERM_SHE_V1.DWG
 Scale: AS SHOWN

Sheet Reference:
C-105
 Sheet 9 of 20

E

LEGEND

H1-1 DOCK NAME-PILE NUMBER

● TIMBER PILE


□ CONCRETE PILE

■ RED (BAD CONDITION - NEEDS REPLACEMENT)

■ ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)

■ MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

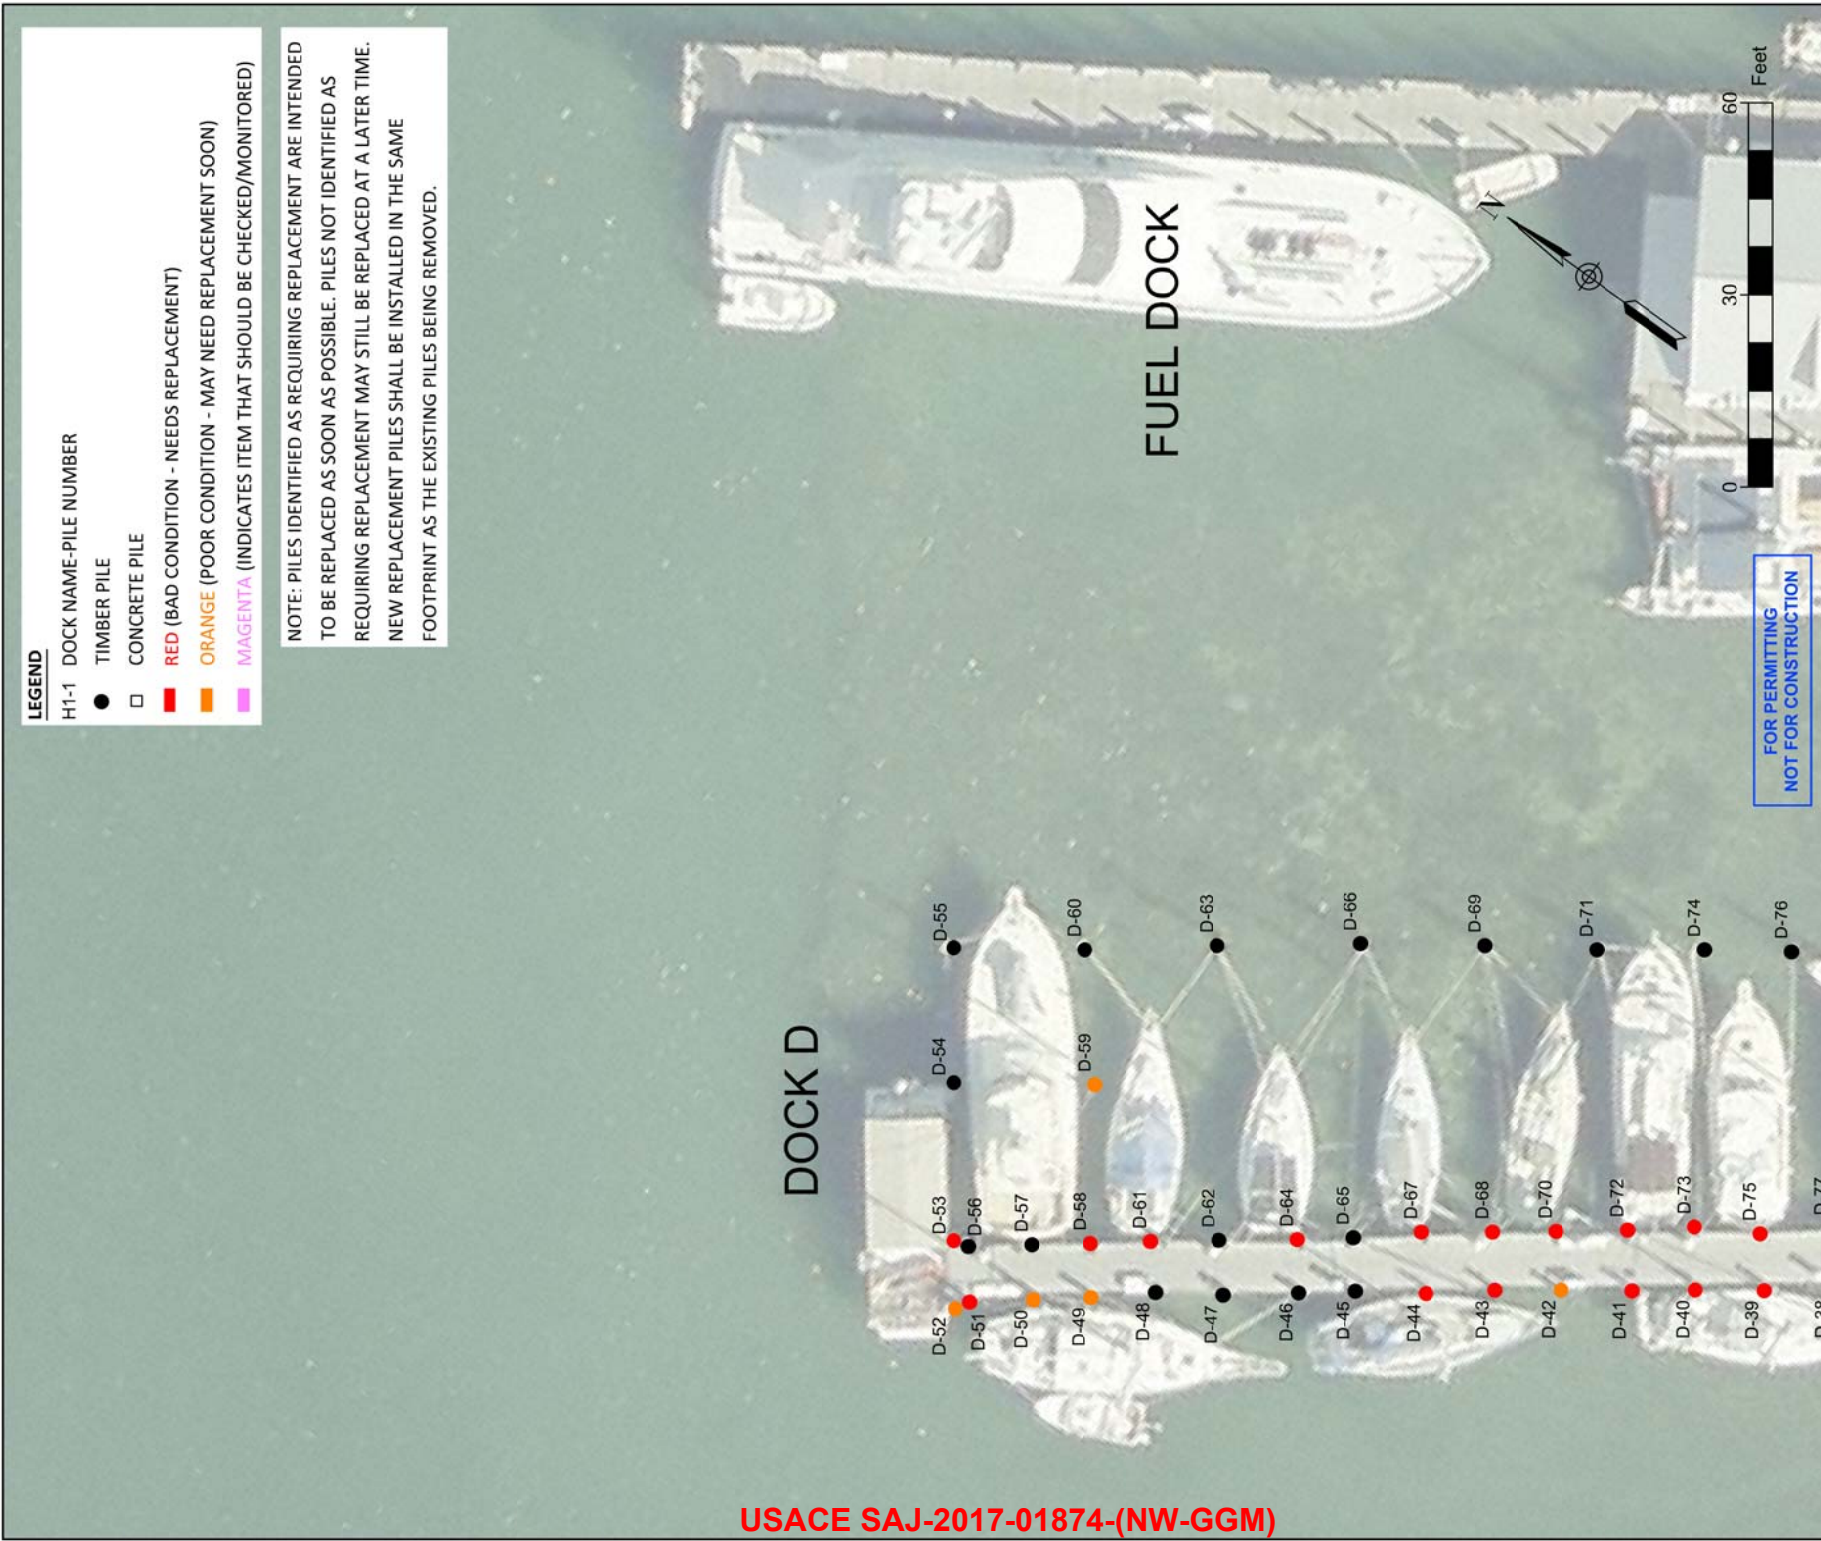


CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)
DOCK D PLAN VIEW
KEY WEST, MONROE COUNTY, FLORIDA




TETRA TECH INC.
799 SOUTH FEDERAL HWY
SUITE 300
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411
CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:
Drawn By: F. MARTINEZ
Checked By: S. MCGAHEE
Date: 10/20/17
Design file no: NW_PILE_REPLACE_SHE_V1.DWG
Scale: AS SHOWN

Sheet Reference:
C-106
Sheet 10 of 20

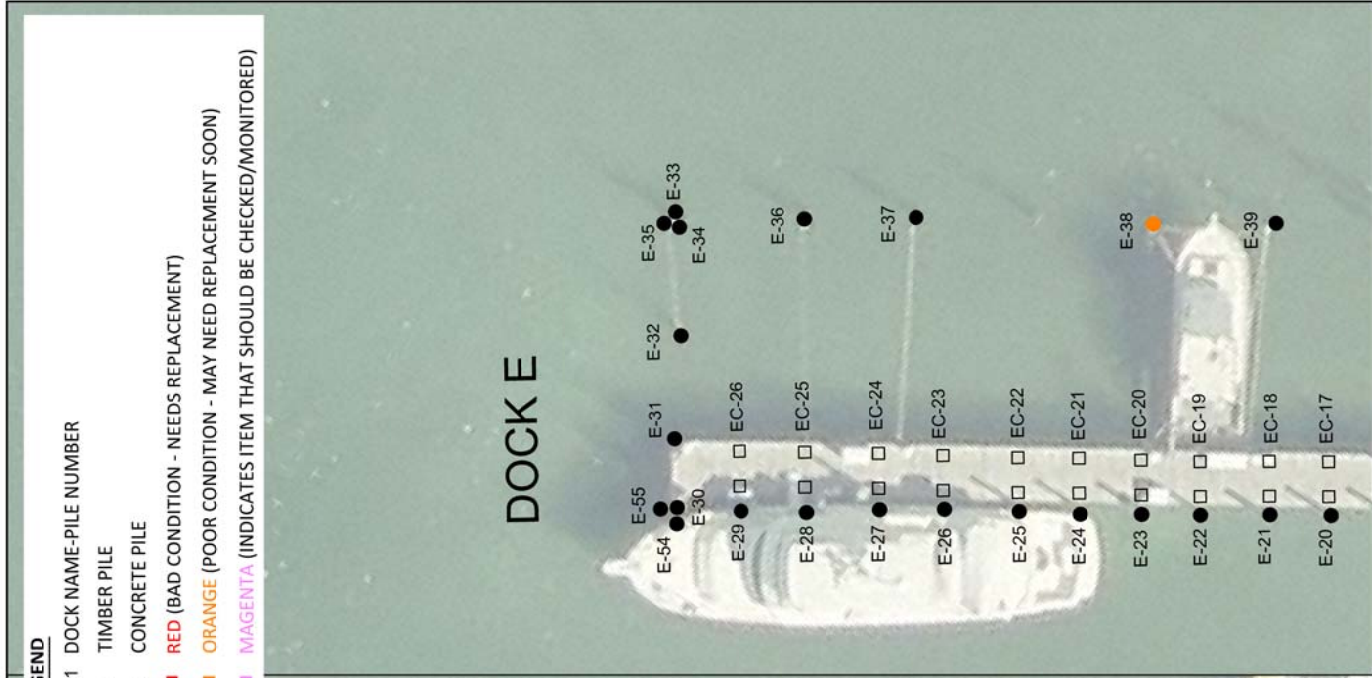

- LEGEND**
- H1-1 DOCK NAME-PILE NUMBER
 - TIMBER PILE
 - CONCRETE PILE
 - RED (BAD CONDITION - NEEDS REPLACEMENT)
 - ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
 - MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

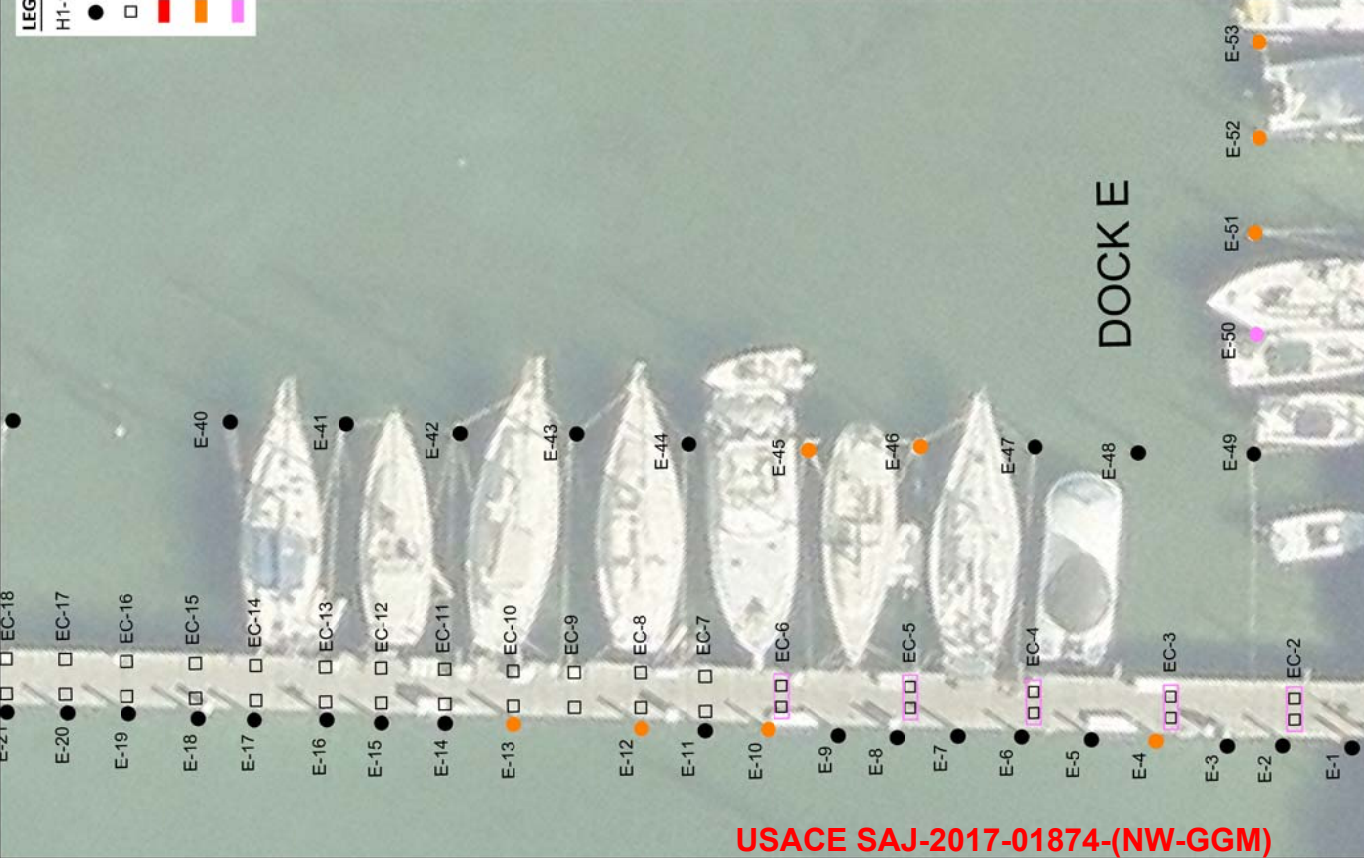

**FOR PERMITTING
NOT FOR CONSTRUCTION**

0 30 60
Feet

Designed by:	AS SHOWN
Drawn By:	F. MARTINEZ
Checked By:	S. MCGAHEE
Date:	10/20/17
Design file no:	NW_PILE_PERMITS_V1.DWG
Scale:	AS SHOWN

Sheet Reference:
C-107
Sheet 11 of 20


TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 300
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411

CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)

DOCK E PLAN VIEW

KEY WEST, MONROE COUNTY, FLORIDA

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.



P:\CITY OF KEY WEST\TASK 11 - KEY BIGHT PILING ASSESSMENT\PERMITTING\DOCK\DOCK E_PILE_PERMITS_V1.DWG


LEGEND

H1-1 DOCK NAME-PILE NUMBER

- TIMBER PILE
- CONCRETE PILE

- RED (BAD CONDITION - NEEDS REPLACEMENT)
- ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
- MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

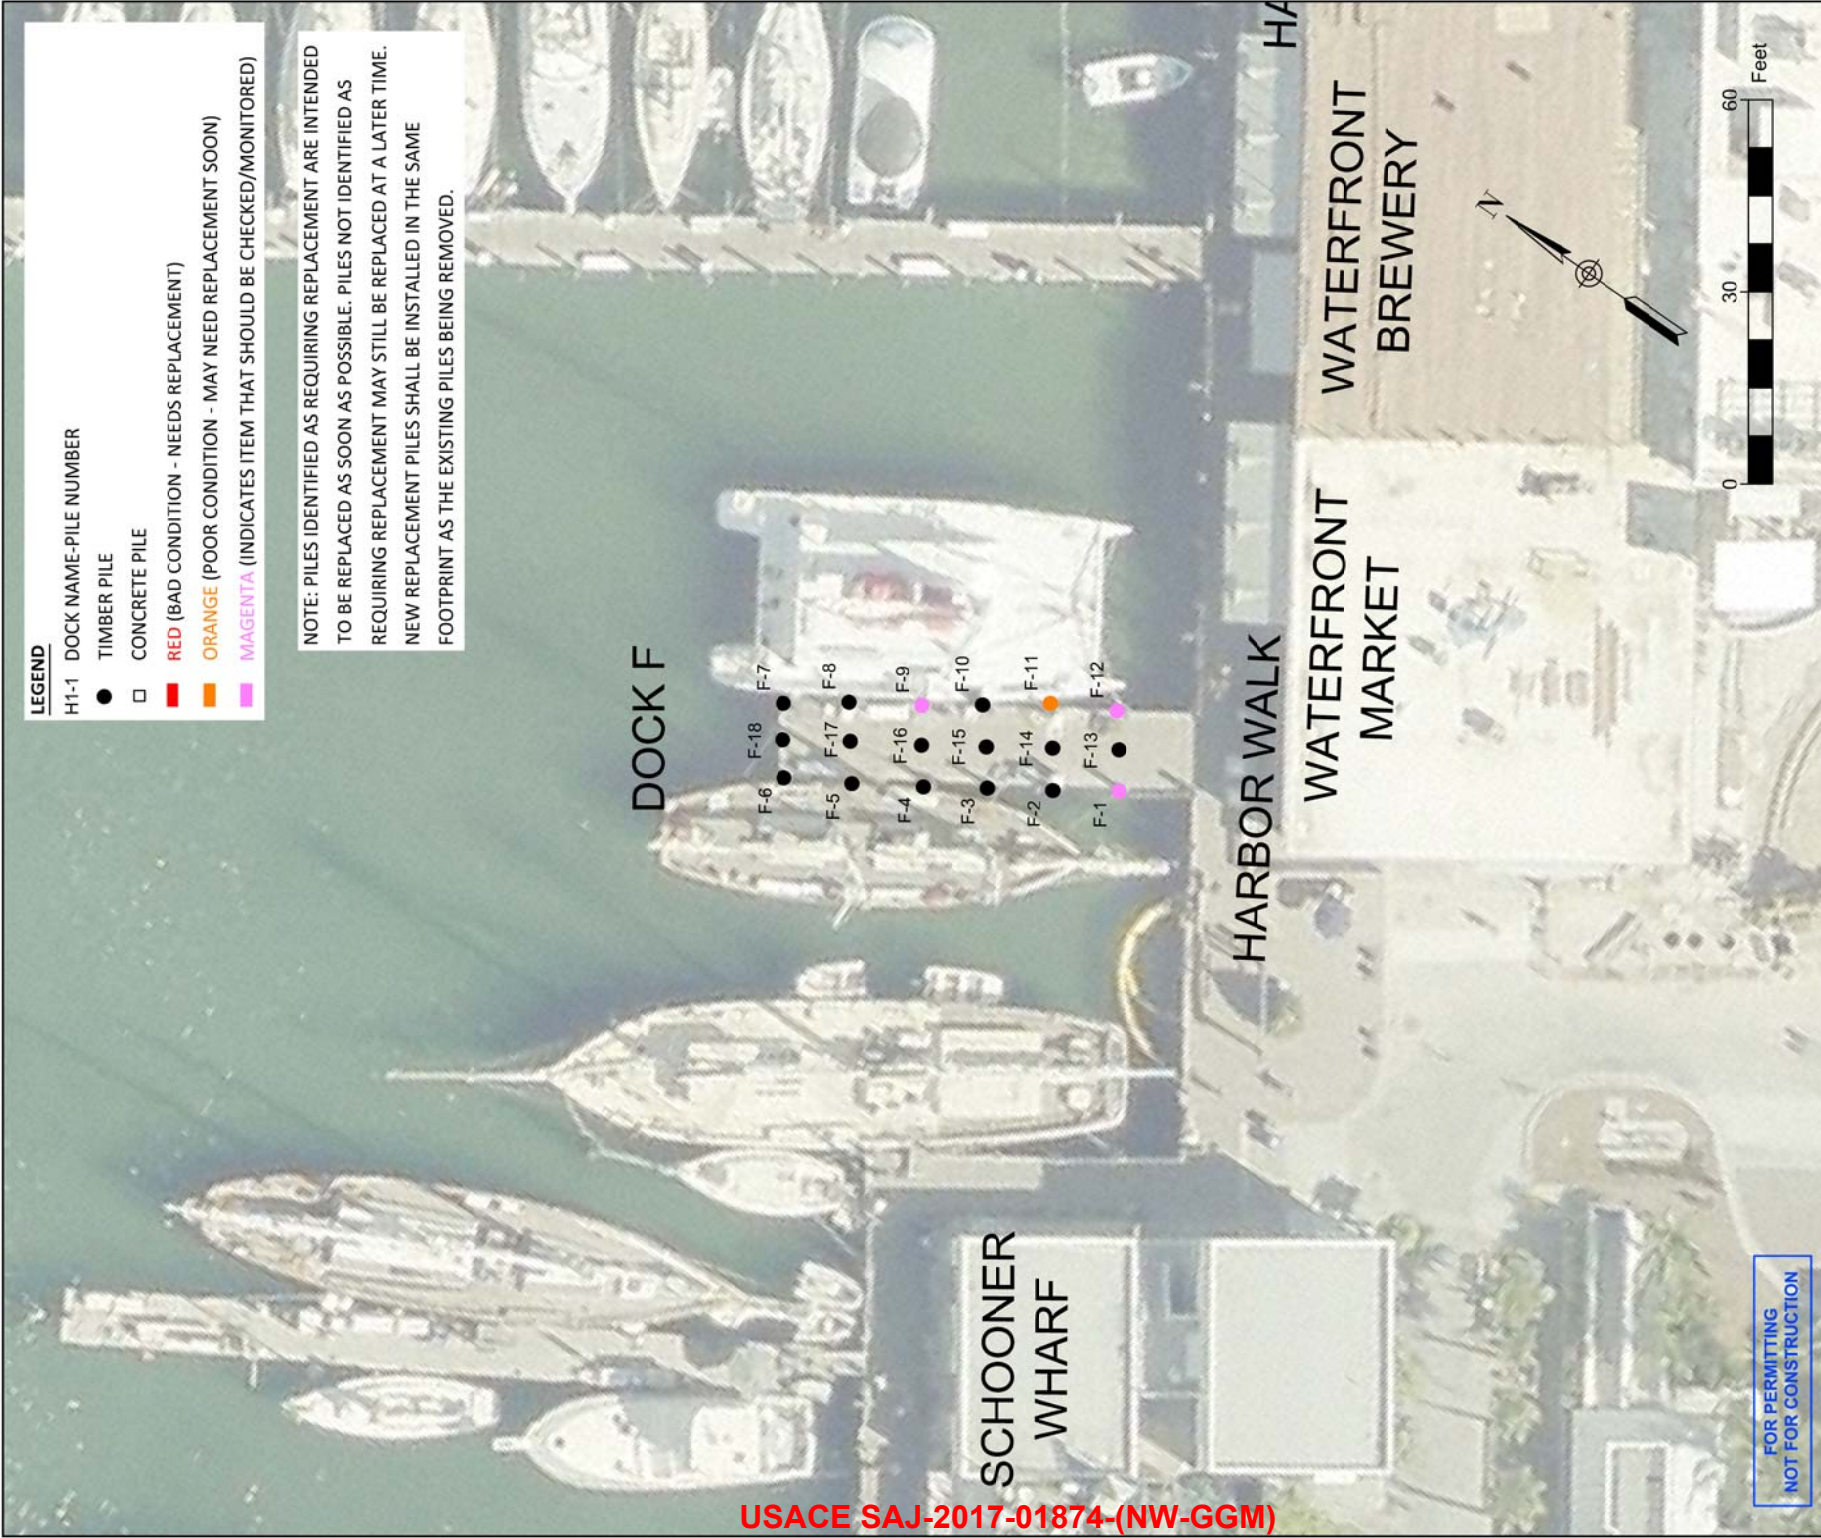

FOR PERMITTING
NOT FOR CONSTRUCTION



CITY OF KEY WEST
**KEY WEST BIGHT MARINA MAINTENANCE
 (PILING REPLACEMENT DOCK REPAIR)**
 DOCK F PLAN VIEW
 KEY WEST, MONROE COUNTY, FLORIDA



TETRA TECH INC.
 799 SOUTH FEDERAL HWY
 SUITE 300
 STUART, FL 34994-2936
 TEL: (772) 781-3400
 FAX: (772) 781-3411

CERTIFICATE OF AUTHORIZATION
 NO. 2429

Designed by:
 Drawn By: F. MARTINEZ
 Checked By: S. MCGAHEE
 Date: 10/20/17
 Design file no: NW_PILE_PERMITS_VI.DWG
 Scale: AS SHOWN

Sheet Reference:
C-108
 Sheet 12 of 20




LEGEND

H1-1 DOCK NAME-PILE NUMBER

- TIMBER PILE
- CONCRETE PILE
- RED (BAD CONDITION - NEEDS REPLACEMENT)
- ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
- MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

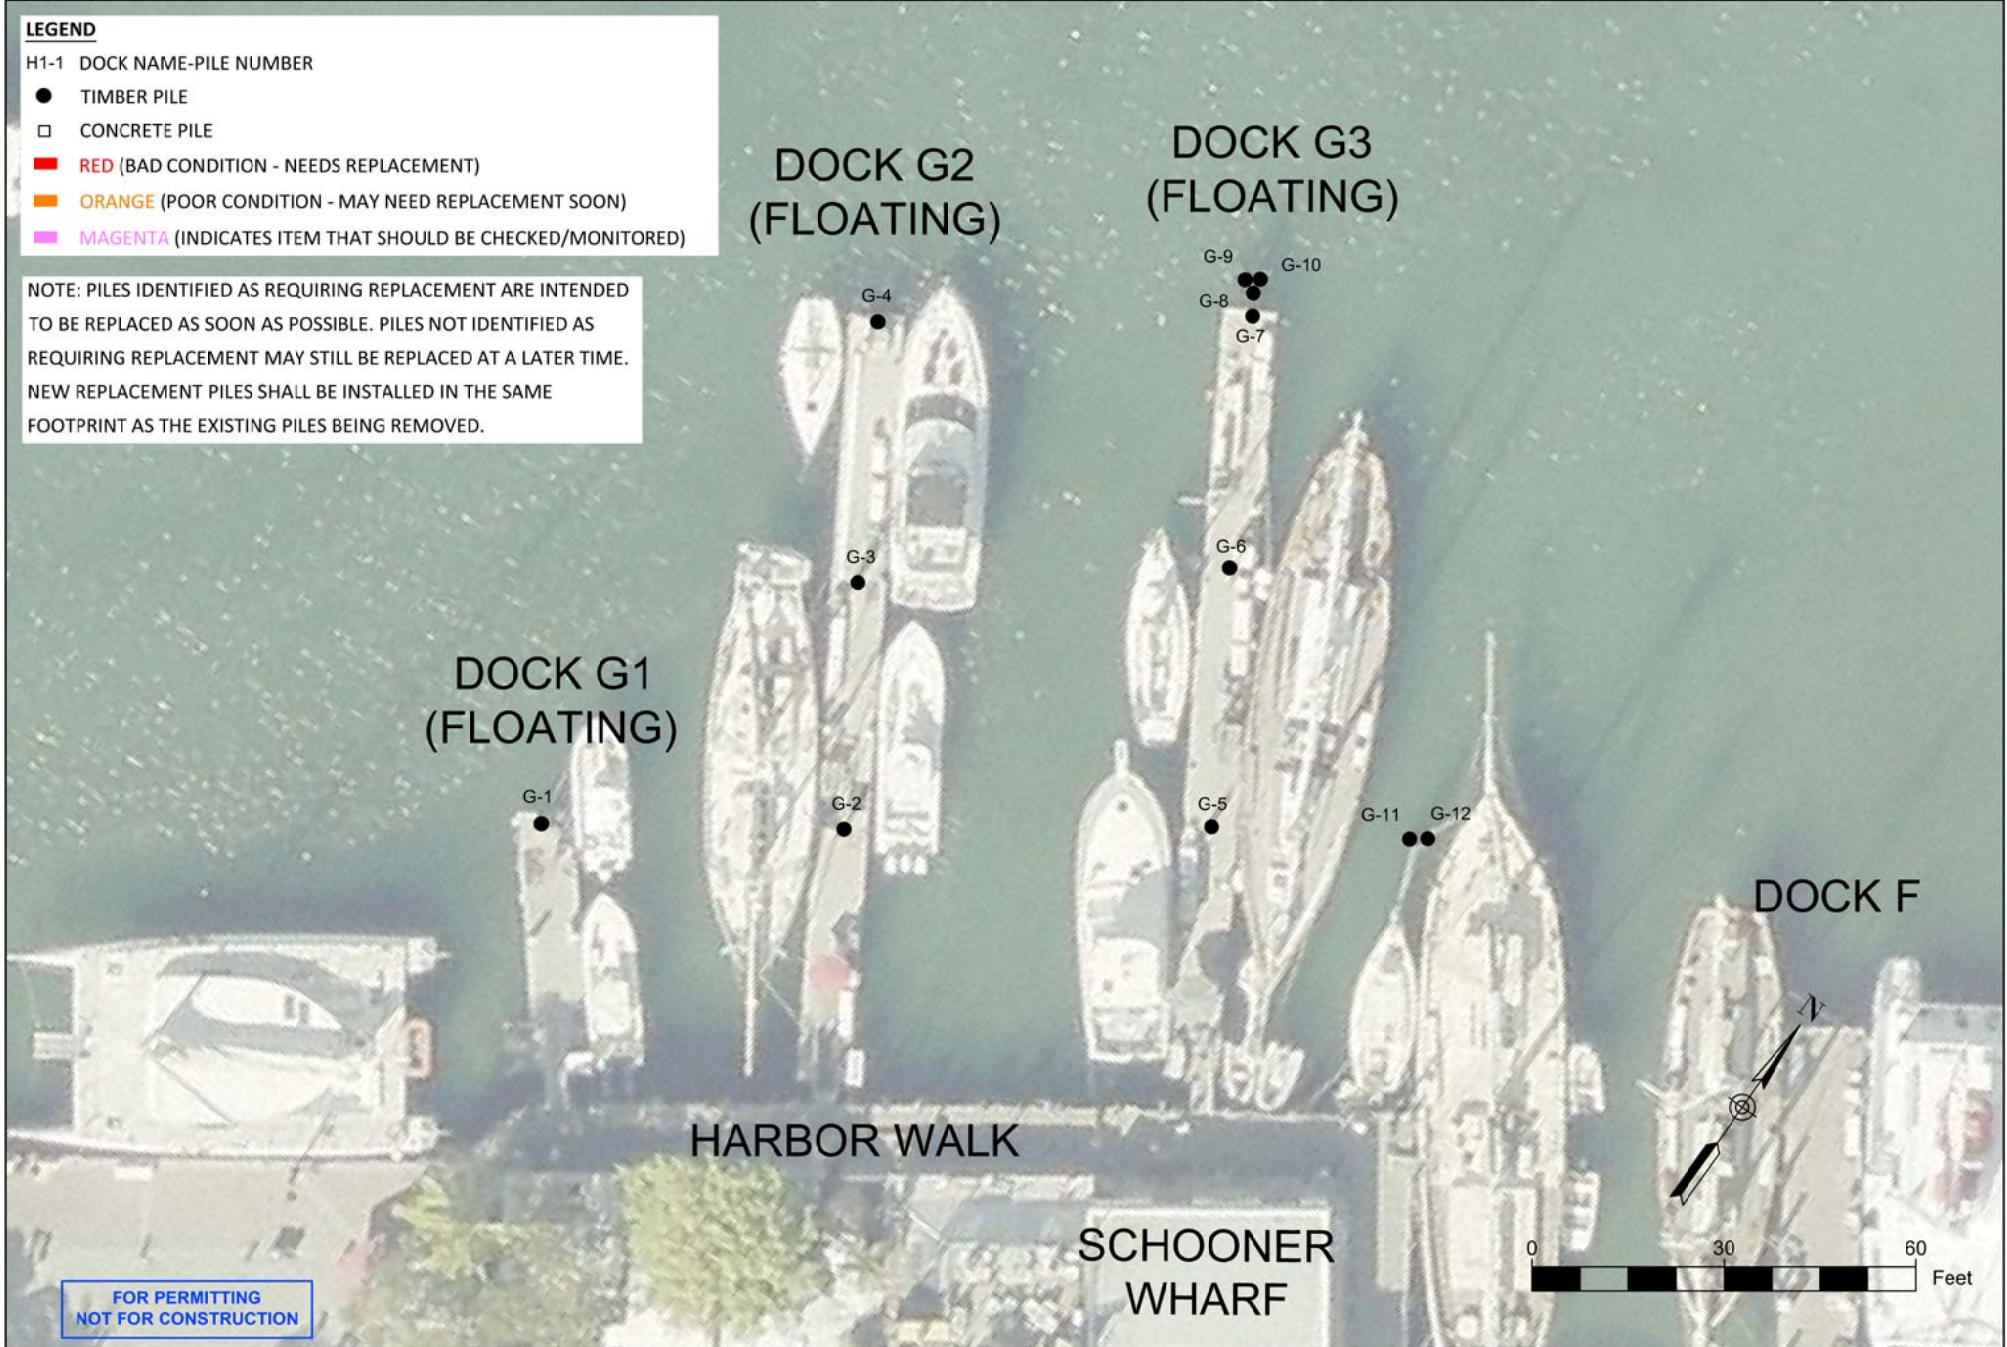

FOR PERMITTING
NOT FOR CONSTRUCTION



CITY OF KEY WEST
 KEY WEST BIGHT MARINA MAINTENANCE
 (PILING REPLACEMENT DOCK REPAIR)
 DOCK G PLAN VIEW
 KEY WEST, MONROE COUNTY, FLORIDA

Tt TETRA TECH INC.
 759 SOUTH FEDERAL HWY
 SUITE 314
 STUART, FL 34994-2936
 TEL: (772) 781-3400
 FAX: (772) 781-3411
 CERTIFICATE OF AUTHORIZATION
 NO. 1239

USACE SAJ-2017-01874-(NW-GGM)
 Page 13 of 20. July 10th, 2018.

Designed by:
 Drawn By:
 F. MARTINEZ
 Checked By:
 S. MCGAHEE
 Date:
 10/20/17
 Design file no:
 HWB_PILE_PERMIT_SITE_V1.DWG
 Scale:
 AS SHOWN


Sheet Reference:
C-109
 Sheet 13 of 20

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.


LEGEND

- H1-1 DOCK NAME-PILE NUMBER
- TIMBER PILE
- CONCRETE PILE
- RED (BAD CONDITION - NEEDS REPLACEMENT)
- ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
- MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)


CONCH REPUBLIC RESTAURANT

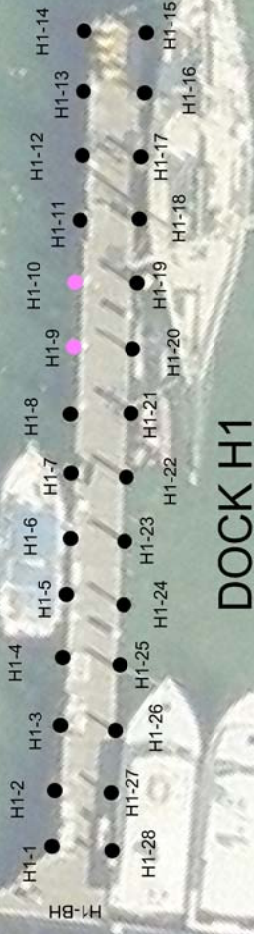

DOCK H1




DOCK H2



DOCK H3



FOR PERMITTING
NOT FOR CONSTRUCTION



CITY OF KEY WEST
**KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)**
DOCK H PLAN VIEW
KEY WEST, MONROE COUNTY, FLORIDA



TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 200
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411
CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:
Drawn By: F. MARTINEZ
Checked By: S. MCGAHEE
Date: 10/20/17
Design file no: NW_PILE_PERM_SHE_V1.DWG
Scale: AS SHOWN



Sheet Reference:
C-110
Sheet 14 of 20

P:\CITY OF KEY WEST\TASK 11 - KEY WEST BIGHT PILING ASSESSMENT\PERMITTING\DOCK H\DOCK H_PILE_PERM_SHE_V1.DWG

**DOCK G1
(FLOATING)**

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

DOCK F

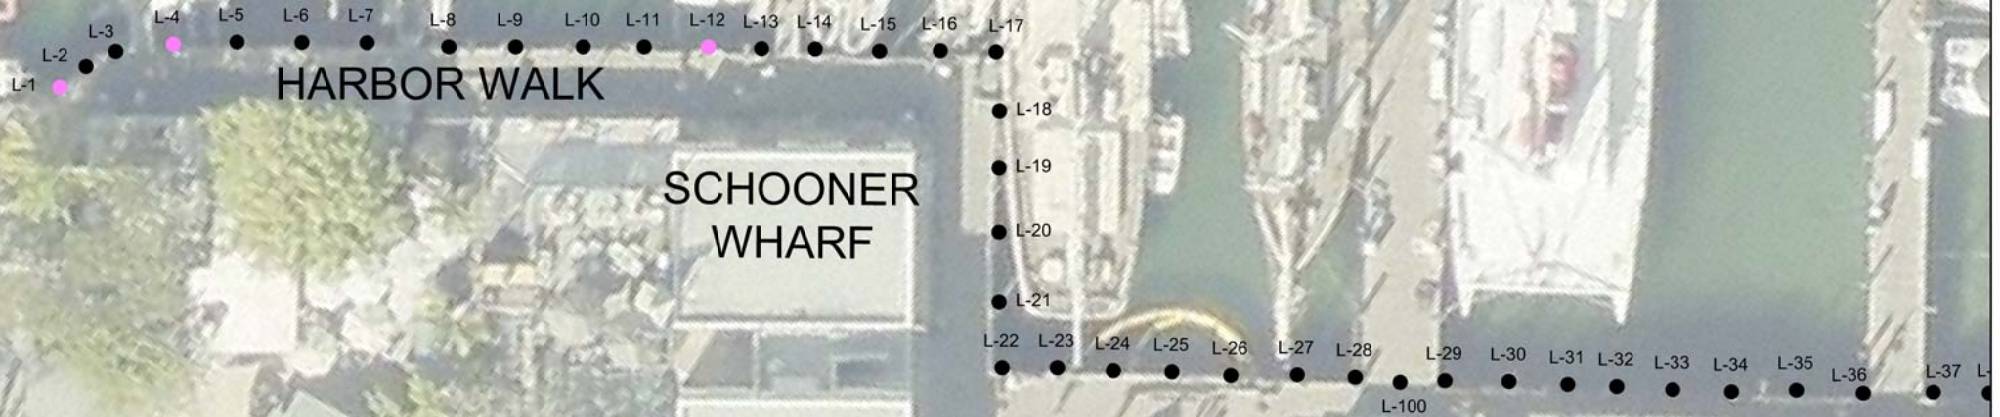

LEGEND

- H1-1 DOCK NAME-PILE NUMBER
- TIMBER PILE
- CONCRETE PILE
- RED (BAD CONDITION - NEEDS REPLACEMENT)
- ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
- MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

**FOR PERMITTING
NOT FOR CONSTRUCTION**



CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)
 HARBOR WALK PLAN VIEW
 KEY WEST, MONROE COUNTY, FLORIDA




TETRA TECH INC.
 759 SOUTH FEDERAL HWY
 SUITE 314
 STUART, FL 34994-2936
 TEL: (772) 781-3400
 FAX: (772) 781-3411
 CERTIFICATE OF AUTHORIZATION
 NO. 1229

USACE SAJ-2017-01874-(NW-GGM)
Page 15 of 20. July 10th, 2018.

Designed by:
Drawn By: F. MARTINEZ
Checked By: S. MCGAHEE
Date: 10/20/17
Design file no: HWB_PILE_PERMIT_SITE_V1.DWG
Scale: AS SHOWN

Sheet Reference:
C-111
 Sheet 15 of 20

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.

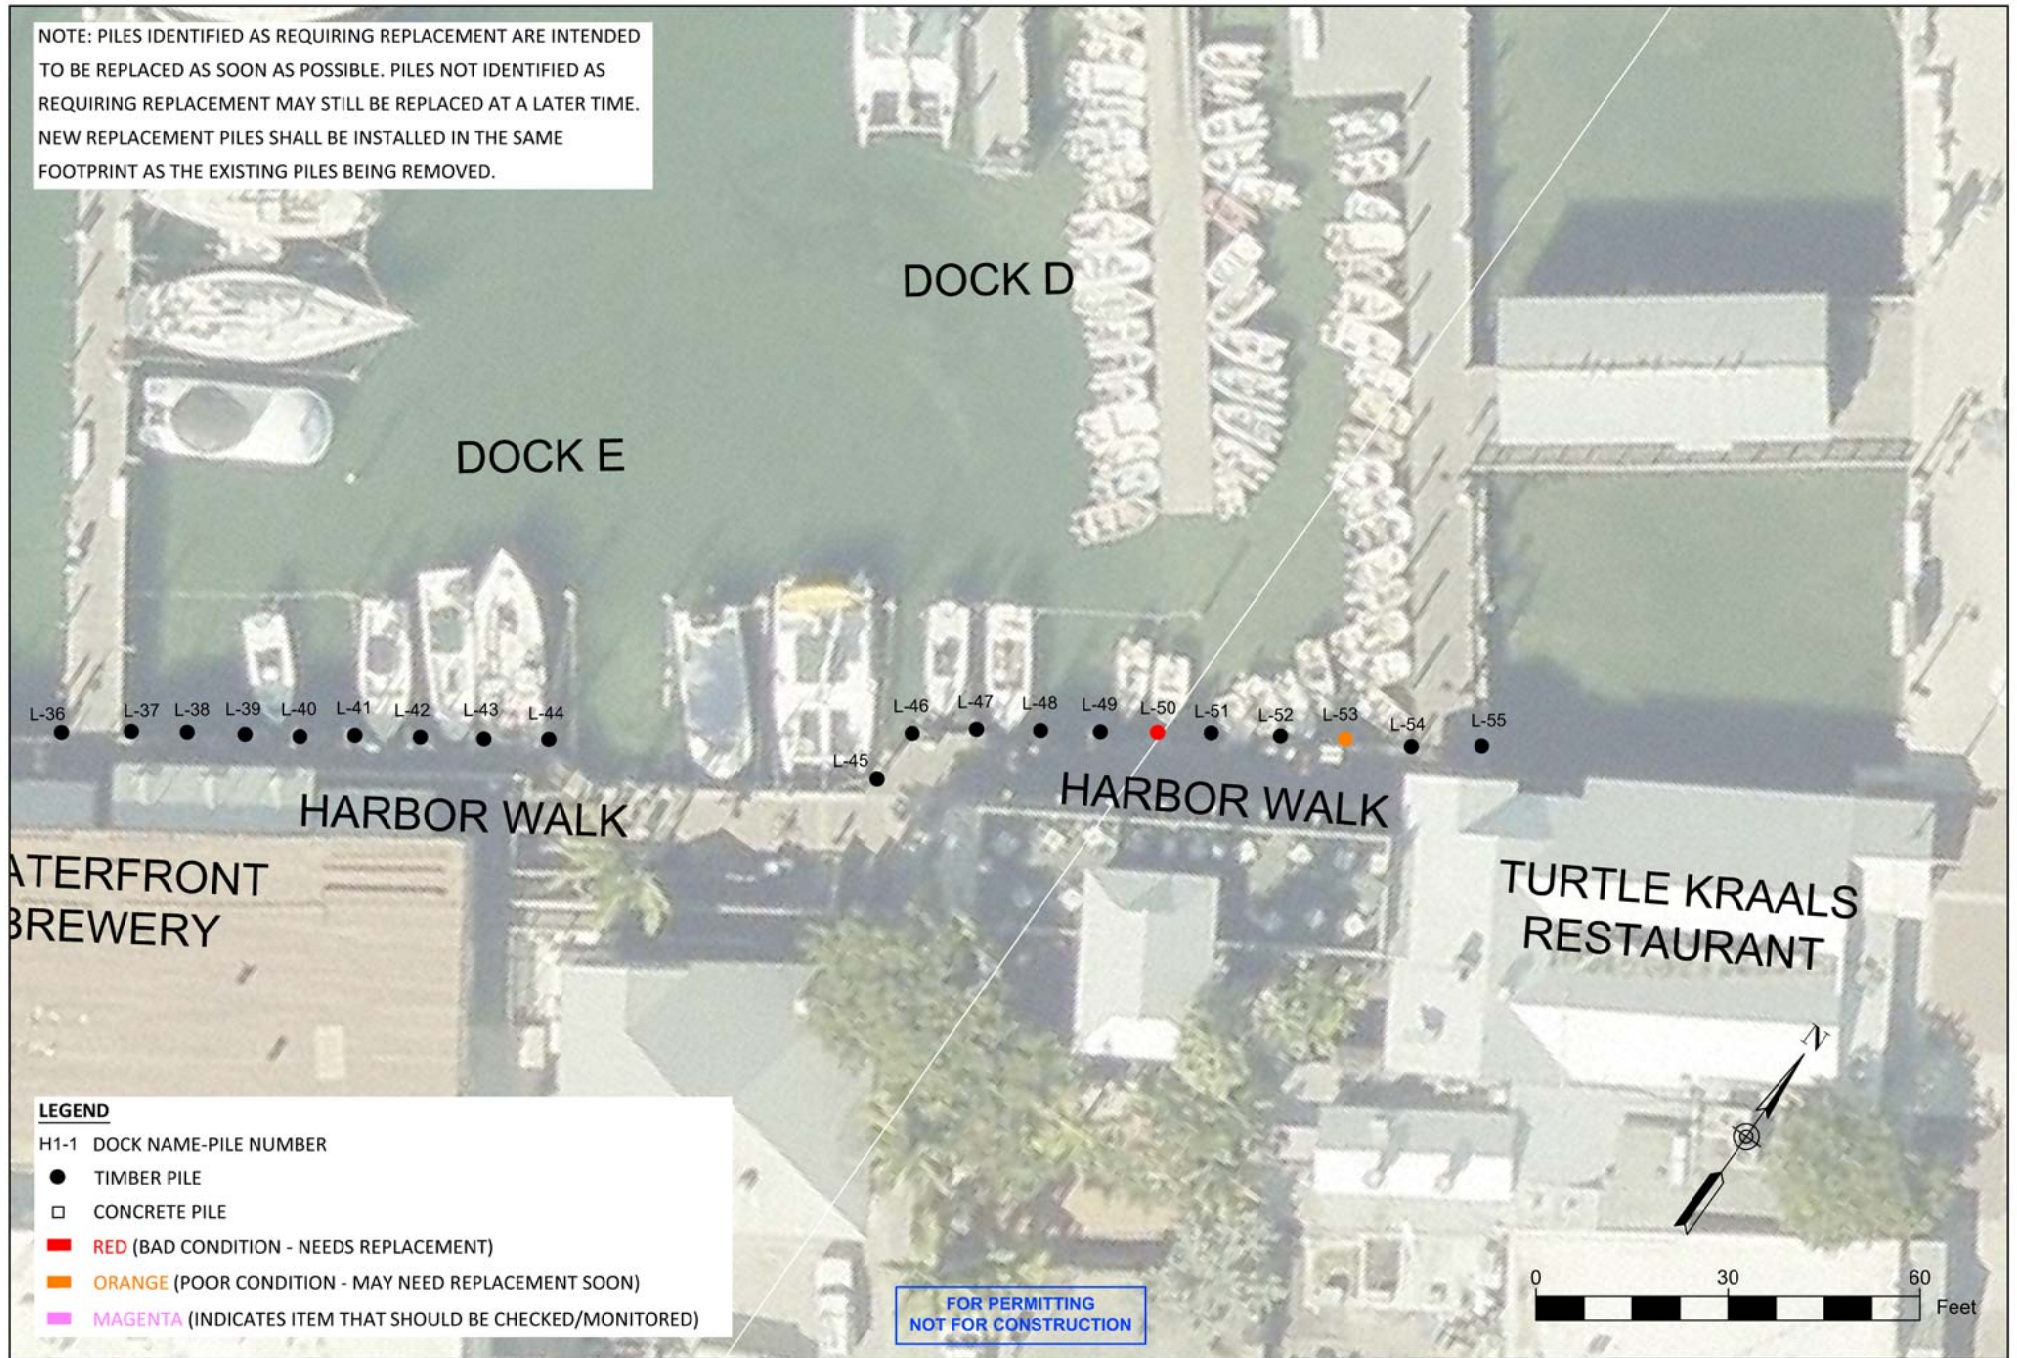

LEGEND

H1-1 DOCK NAME-PILE NUMBER

- TIMBER PILE
- CONCRETE PILE
- RED (BAD CONDITION - NEEDS REPLACEMENT)
- ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)
- MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

FOR PERMITTING
NOT FOR CONSTRUCTION



CITY OF KEY WEST
**KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)**
 HARBOR WALK PLAN VIEW
 KEY WEST, MONROE COUNTY, FLORIDA



TETRA TECH INC.
 759 SOUTH FEDERAL HWY
 SUITE 314
 STUART, FL 34994-2936
 TEL: (772) 781-3400
 FAX: (772) 781-3411

CERTIFICATE OF AUTHORIZATION
 No. 18-000029

**USACE SAJ-2017-01874-(NW-GGM)
 Page 16 of 20. July 10th, 2018.**

Designed by:
Drawn By: F. MARTINEZ
Checked By: S. MCGAHEE
Date: 10/20/17
Design file no: HWB_FILE_PERMIT_SITE_V1.DWG
Scale: AS SHOWN

Sheet Reference:
C-112
 Sheet 16 of 20

NOTE: PILES IDENTIFIED AS REQUIRING REPLACEMENT ARE INTENDED TO BE REPLACED AS SOON AS POSSIBLE. PILES NOT IDENTIFIED AS REQUIRING REPLACEMENT MAY STILL BE REPLACED AT A LATER TIME. NEW REPLACEMENT PILES SHALL BE INSTALLED IN THE SAME FOOTPRINT AS THE EXISTING PILES BEING REMOVED.



LEGEND

H1-1 DOCK NAME-PILE NUMBER

● TIMBER PILE

□ CONCRETE PILE

■ RED (BAD CONDITION - NEEDS REPLACEMENT)

■ ORANGE (POOR CONDITION - MAY NEED REPLACEMENT SOON)

■ MAGENTA (INDICATES ITEM THAT SHOULD BE CHECKED/MONITORED)

FOR PERMITTING
NOT FOR CONSTRUCTION



CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)
DOCK G PLAN VIEW
KEY WEST, MONROE COUNTY, FLORIDA




TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 314
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411
CERTIFICATE OF AUTHORIZATION
NO. 1229

USACE SAJ-2017-01874-(NW-GGM)
Page 17 of 20. July 10th, 2018.

Designed by:
Drawn By:
F. MARTINEZ
Checked By:
S. MCGAHEE
Date:
10/20/17
Design file no:
HWB_FILE_PERMIT_SITE_V1.DWG
Scale:
AS SHOWN

Sheet Reference:
C-113
Sheet 17 of 20

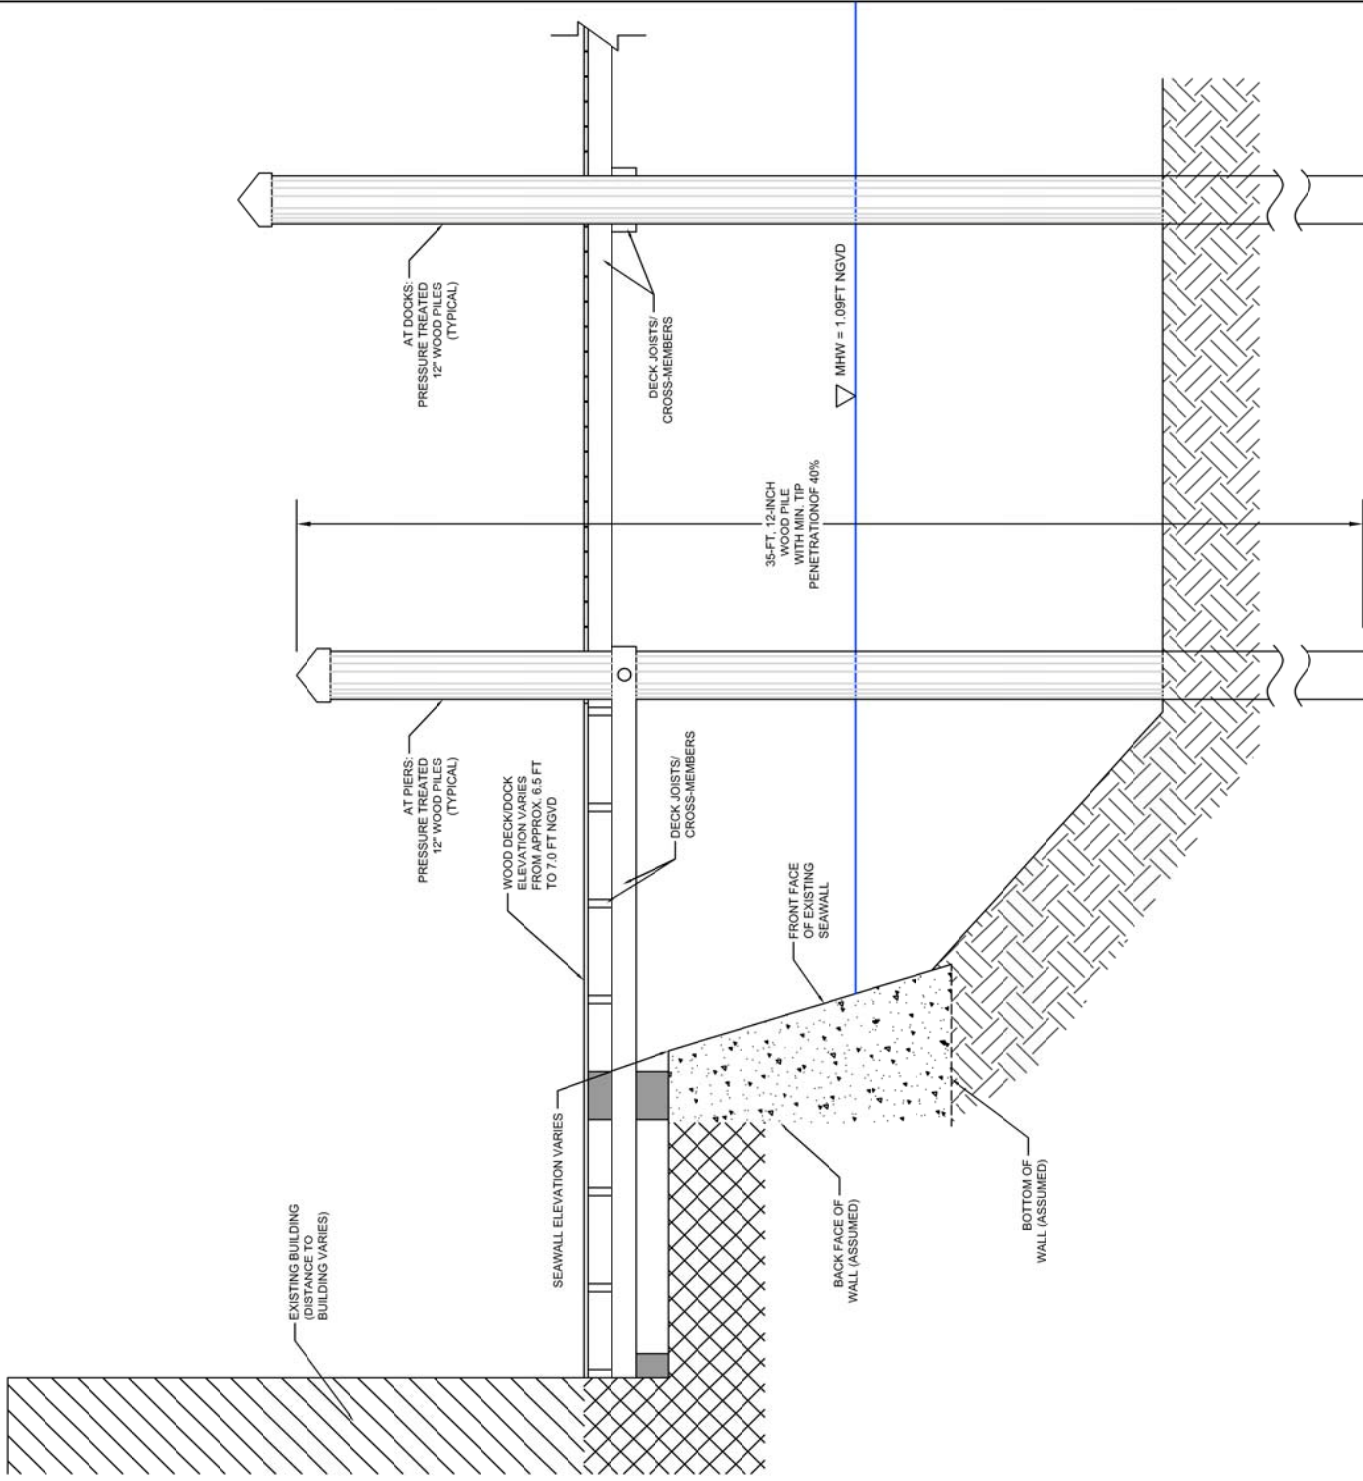


NOTES:

1. THIS CROSS-SECTION IS REPRESENTATIVE OF THE APPROXIMATE CONDITIONS/ELEVATIONS IN DOCK E, DOCK F, AND THE HARBOR WALK PIER IN FRONT OF THE WATERFRONT MARKET AND BREWERY.
2. WOOD PILES TO BE REPLACED INCLUDE STRUCTURAL AND FENDER PILES, 12" DIAMETER, APPROX. 35' MIN. LENGTH.
3. THE REPLACEMENT PILES ARE TO BE PLACED IN THE RESULTANT VOID CREATED BY REMOVAL OF THE EXISTING PILE.

**DOCK AND DECK CROSS-SECTION
(DOCK E, DOCK F, AND HARBOR WALK PIER)
[NOT TO SCALE]**

**FOR PERMITTING
NOT FOR CONSTRUCTION**



**CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)**

CROSS-SECTION DETAIL
KEY WEST, MONROE COUNTY, FLORIDA




TETRA TECH INC.
799 SOUTH FEDERAL HWY
SUITE 300
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411

CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:
Drawn By: F. MARTINEZ
Checked By: S. MCGAHEE
Date: 10/20/17
Design file no: NW_PILE_PERM_SHE_V1.DWG
Scale: AS SHOWN

Sheet Reference:
C-114
Sheet 18 of 20

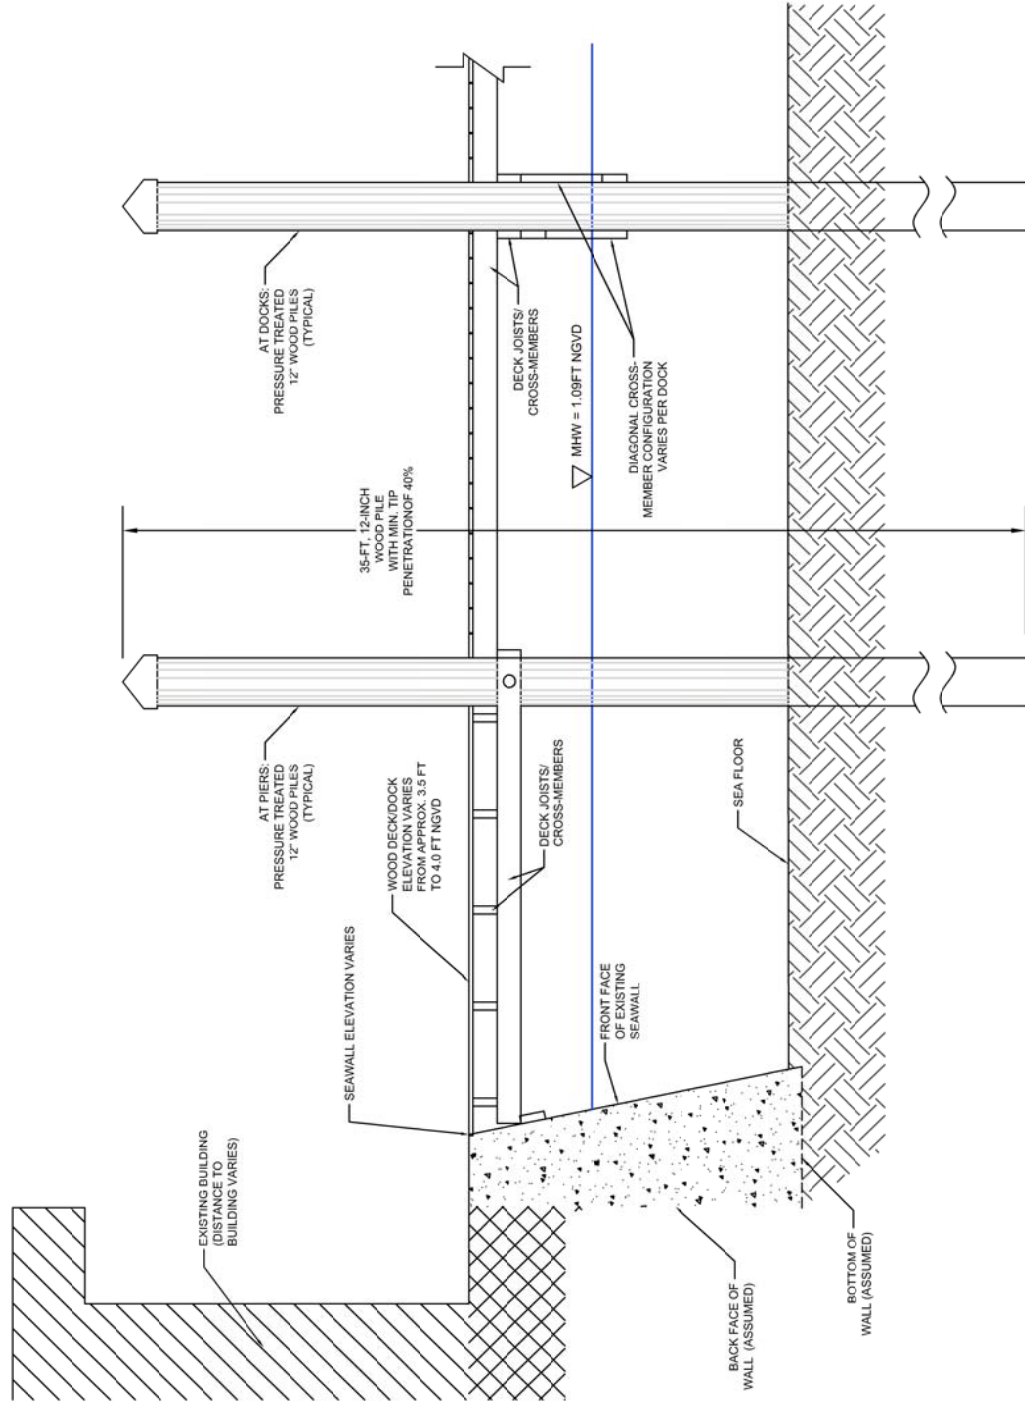


DOCK AND DECK CROSS-SECTION
(DOCK A, DOCK C, DOCK D, DOCK H, AND HARBOR WALK PIER)
[NOT TO SCALE]

NOTES:

1. THIS CROSS-SECTION IS REPRESENTATIVE OF THE APPROXIMATE CONDITIONS/ELEVATIONS OF DOCK A, DOCK C, DOCK D, DOCK H, AND THE HARBOR WALK PIER OUTSIDE OF THE AREA IN FRONT OF THE WATERFRONT MARKET AND BREWERY. DOCK H IS CONNECTED DIRECTLY TO THE SEAWALL, WITHOUT A WOOD PIER WALKWAY.
2. WOOD PILES TO BE REPLACED INCLUDE STRUCTURAL AND FENDER PILES, 12" DIAMETER, APPROX. 35' MIN. LENGTH.
3. THE REPLACEMENT PILES ARE TO BE PLACED IN THE RESULTANT VOID CREATED BY REMOVAL OF THE EXISTING PILE.

FOR PERMITTING
NOT FOR CONSTRUCTION



CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)

CROSS-SECTION DETAIL
KEY WEST, MONROE COUNTY, FLORIDA




TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 300
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411

CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:
Drawn By: F. MARTINEZ
Checked By: S. MCCAGHEE
Date: 10/20/17
Design file no: NW_PILE_REPLACE_SHE_V1.DWG
Scale: AS SHOWN

Sheet Reference:
C-115
Sheet 19 of 20

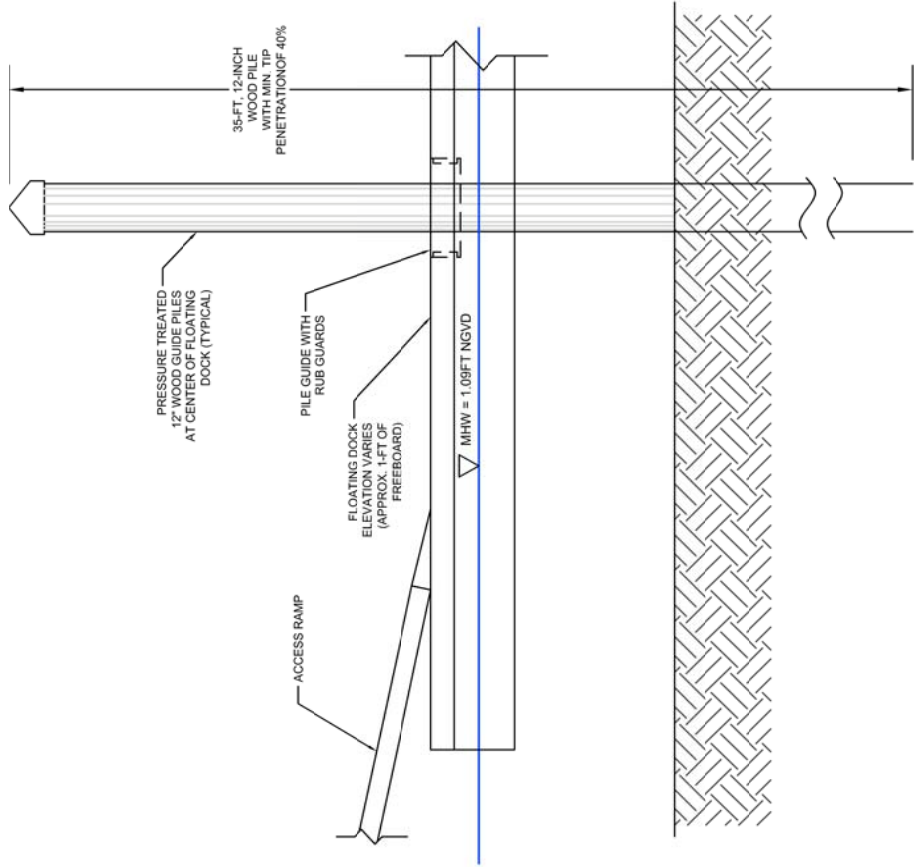


FLOATING DOCK CROSS-SECTION
(DOCK D AND DOCK G)
[NOT TO SCALE]

NOTES:

1. THIS CROSS-SECTION IS REPRESENTATIVE OF THE APPROXIMATE CONDITIONS/ELEVATIONS OF THE FLOATING DOCK SECTIONS OF DOCK D, AND DOCK G.
2. WOOD PILES TO BE REPLACED INCLUDE STRUCTURAL PILES, 12" DIAMETER, APPROX. 35' MIN. LENGTH.
3. THE REPLACEMENT PILES ARE TO BE PLACED IN THE RESULTANT VOID CREATED BY REMOVAL OF THE EXISTING PILE.

FOR PERMITTING
NOT FOR CONSTRUCTION



CITY OF KEY WEST
KEY WEST BIGHT MARINA MAINTENANCE
(PILING REPLACEMENT DOCK REPAIR)
CROSS-SECTION DETAIL
KEY WEST, MONROE COUNTY, FLORIDA



TETRA TECH INC.
759 SOUTH FEDERAL HWY
SUITE 300
STUART, FL 34994-2936
TEL: (772) 781-3400
FAX: (772) 781-3411
CERTIFICATE OF AUTHORIZATION
NO. 2429

Designed by:
Drawn By: F. MARTINEZ
Checked By: S. MCGAHEE
Date: 10/20/17
Design file no: NW_PILE_REPLACE_SHE_V1.DWG
Scale: AS SHOWN

Sheet Reference:
C-116
Sheet 20 of 20
